
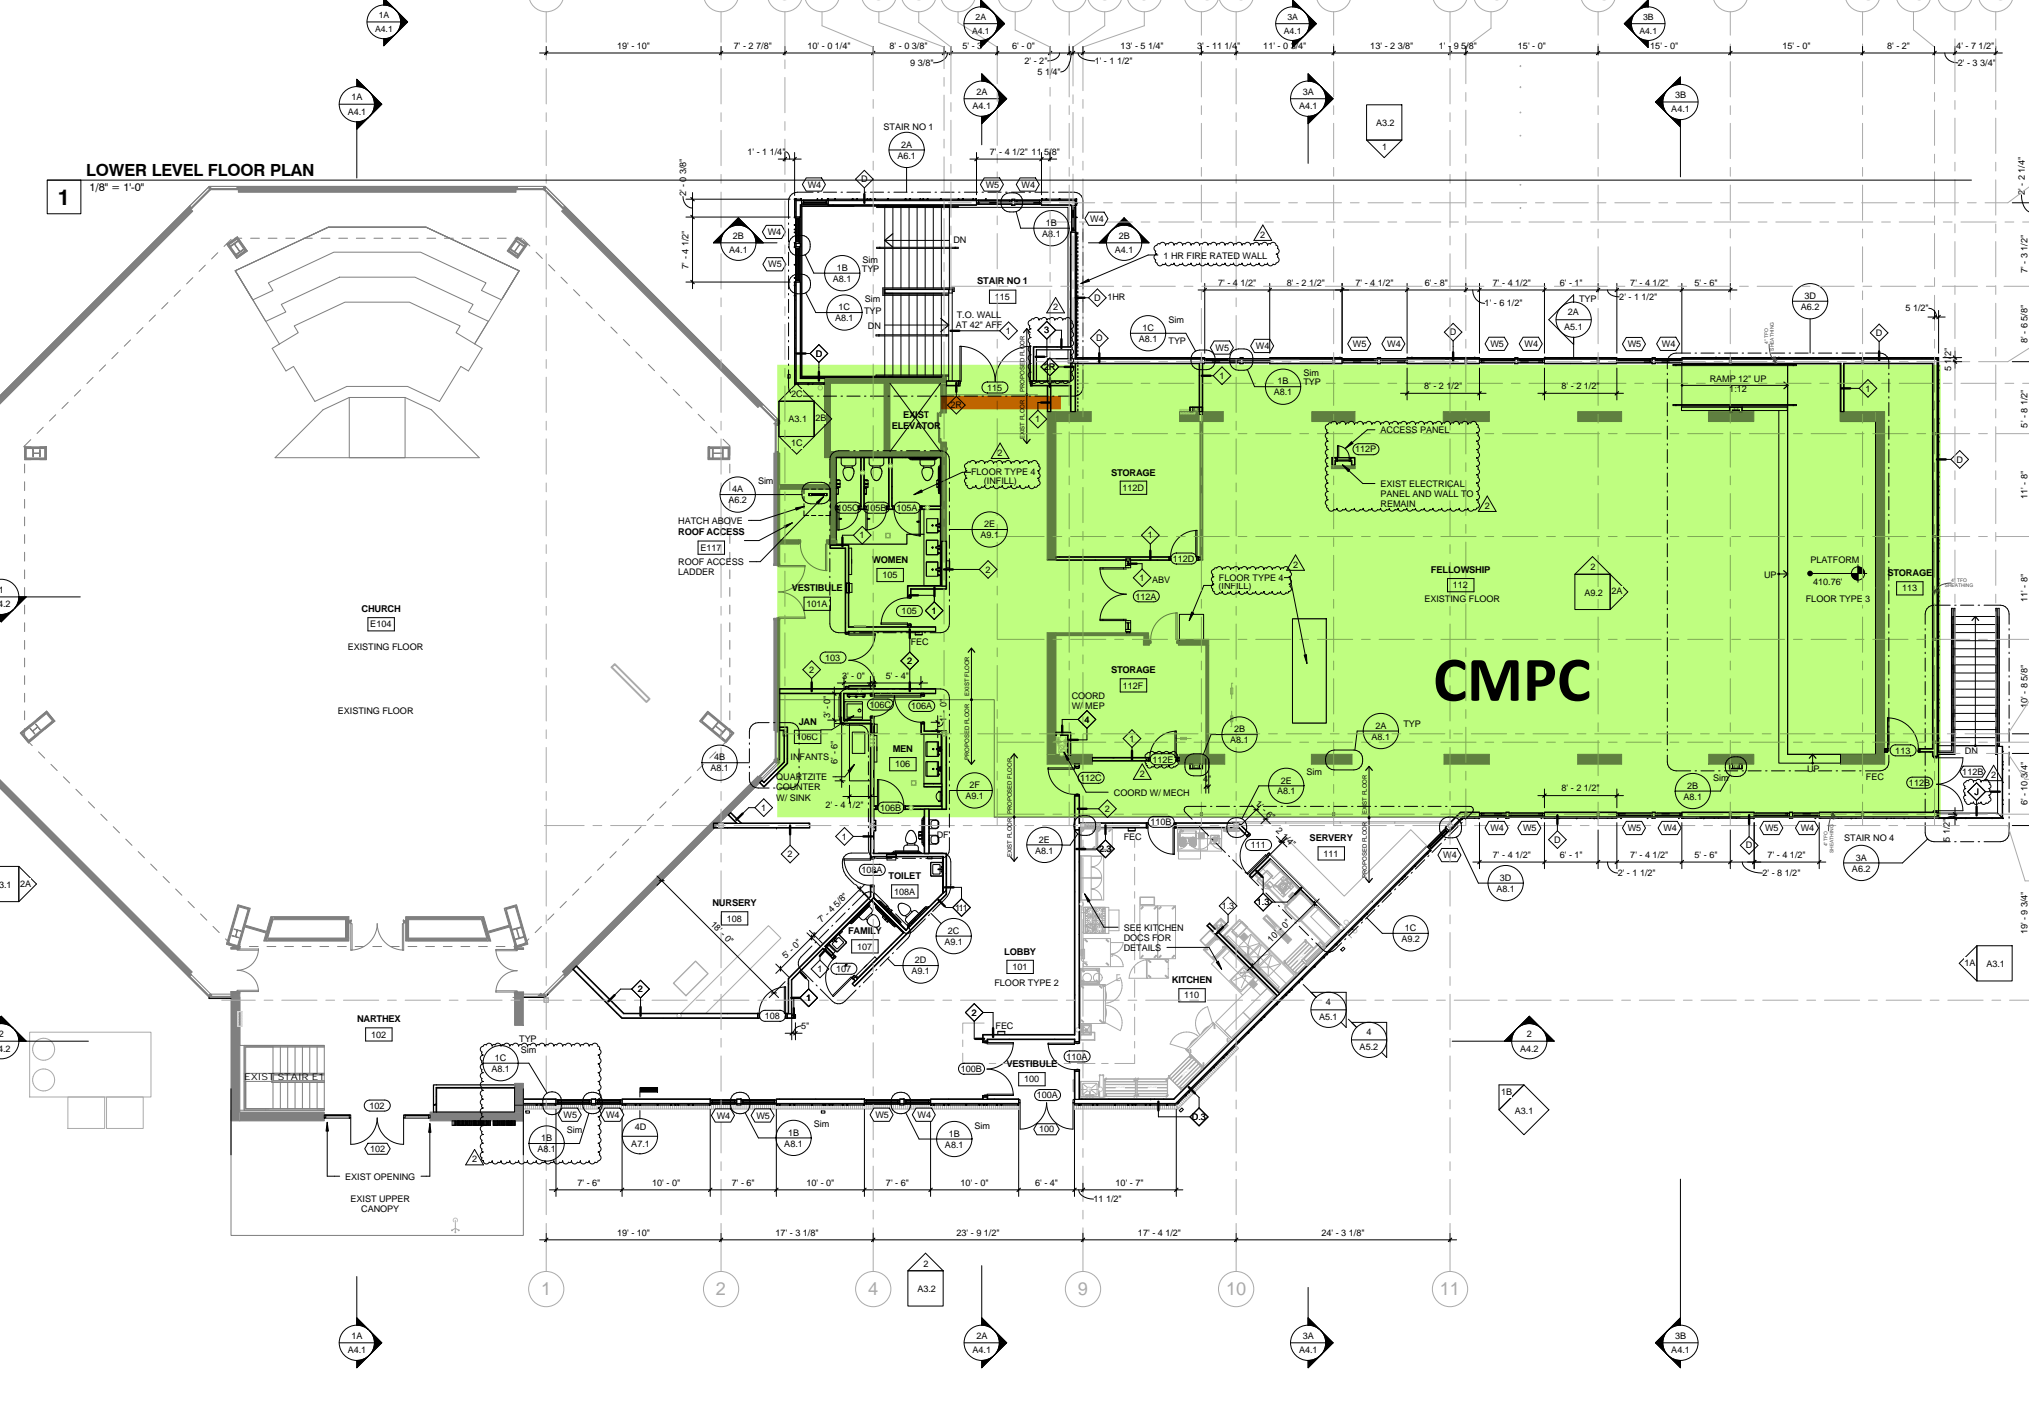


# Christ Memorial - Phasing Plan

## November 2018



- Preschool - ASI#06 Door 003E
- Lower Level Fellowship - Electrical Room Prep
- Sanctuary - No Work
- Upper Level Fellowship - No Work
- CMPC Occupied
- North Addition - Demolition, Prep Building Pad

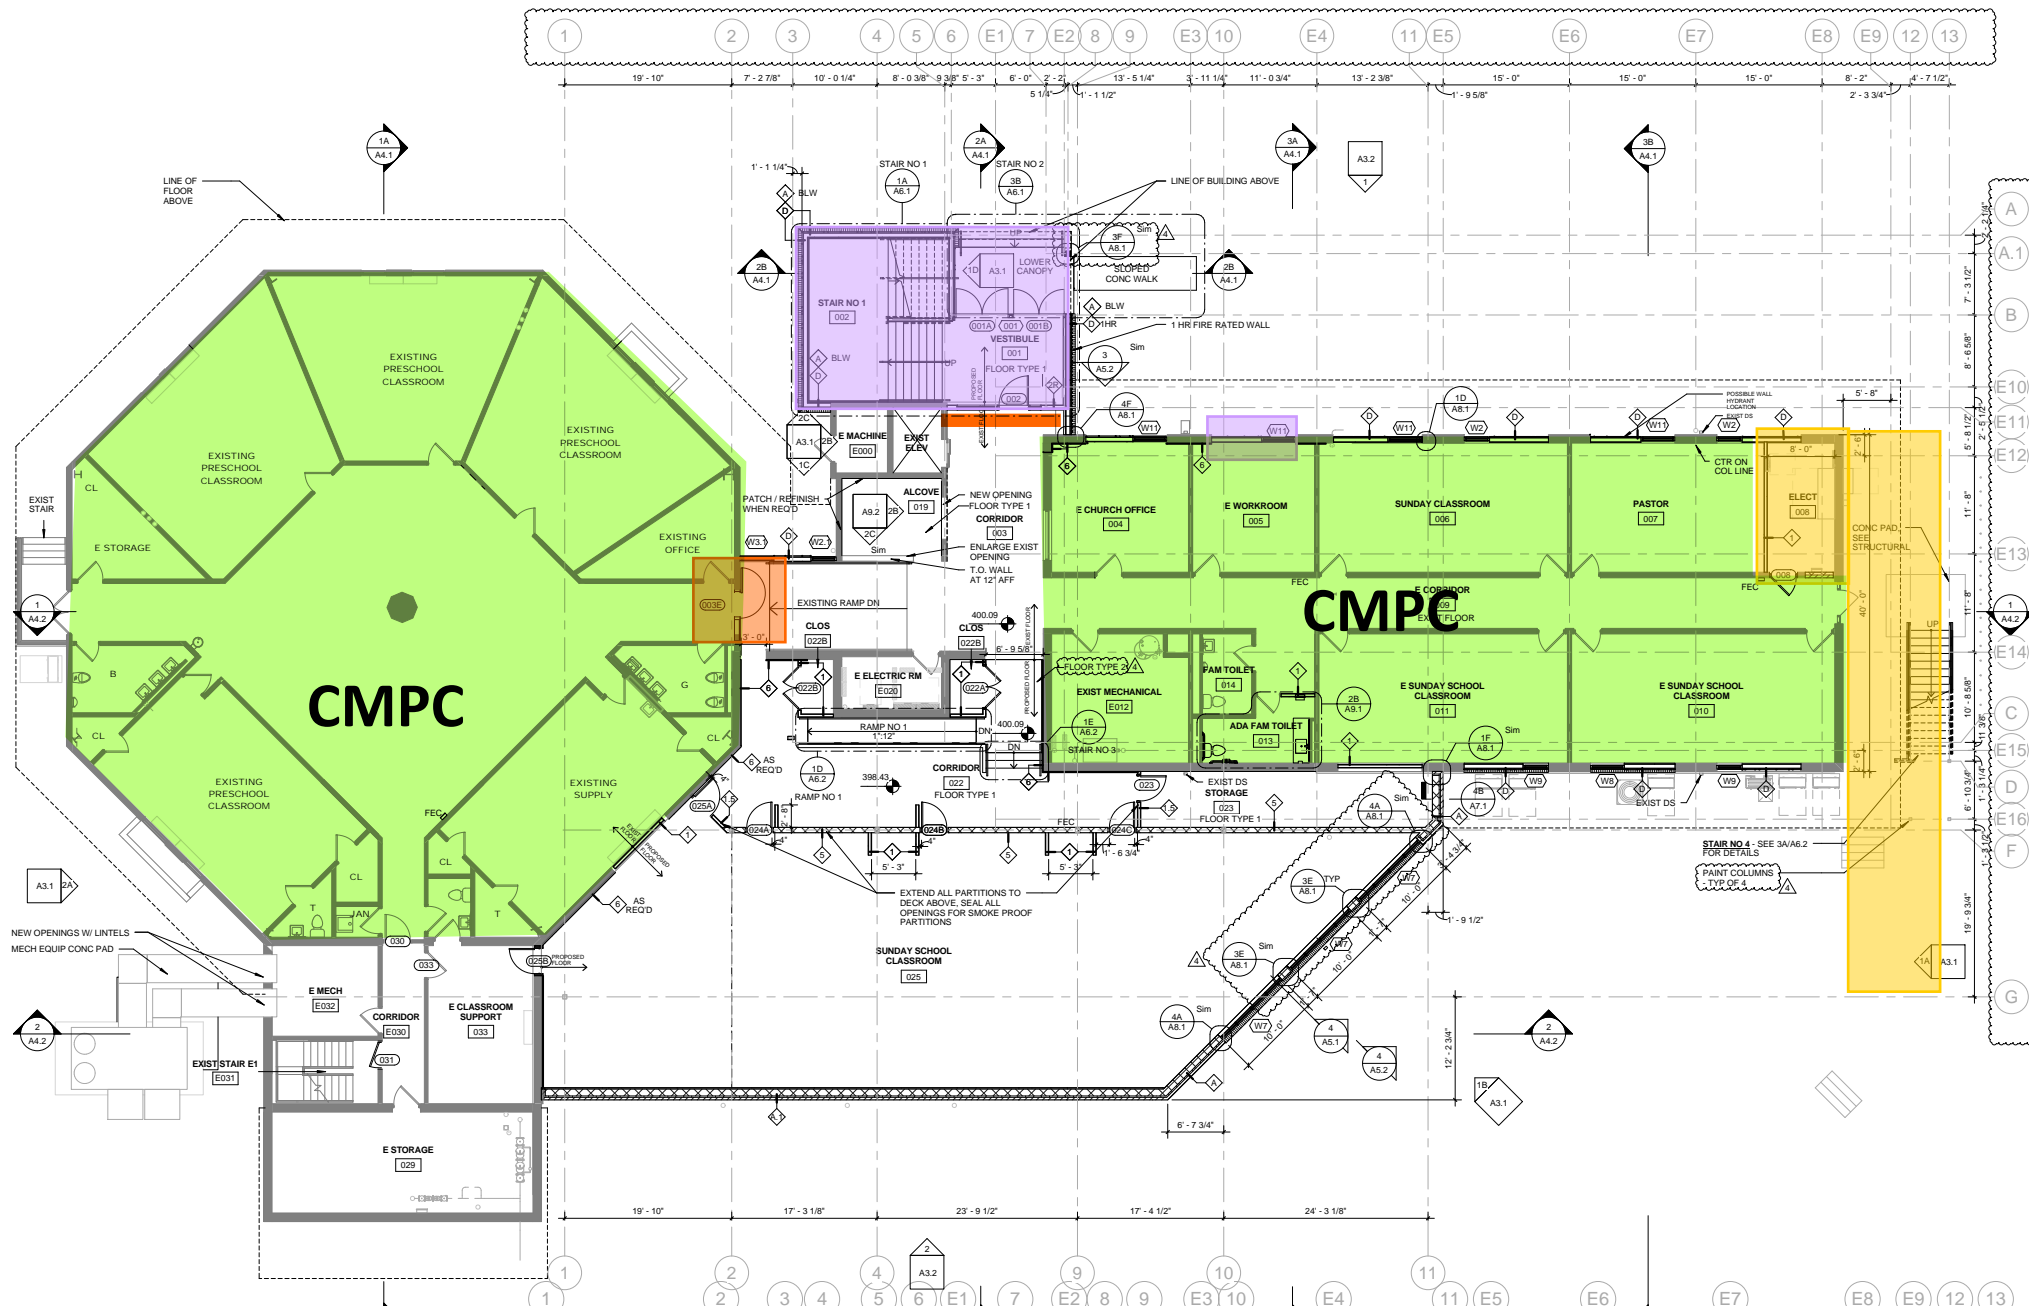

# Christ Memorial - Access Routes

## November 2018 - March 2019

- Preschool
- Lower Level Fellowship
- CMPC
- Sanctuary
- Upper Level Fellowship
- North Addition
- Access Routes
- CMPC Occupied

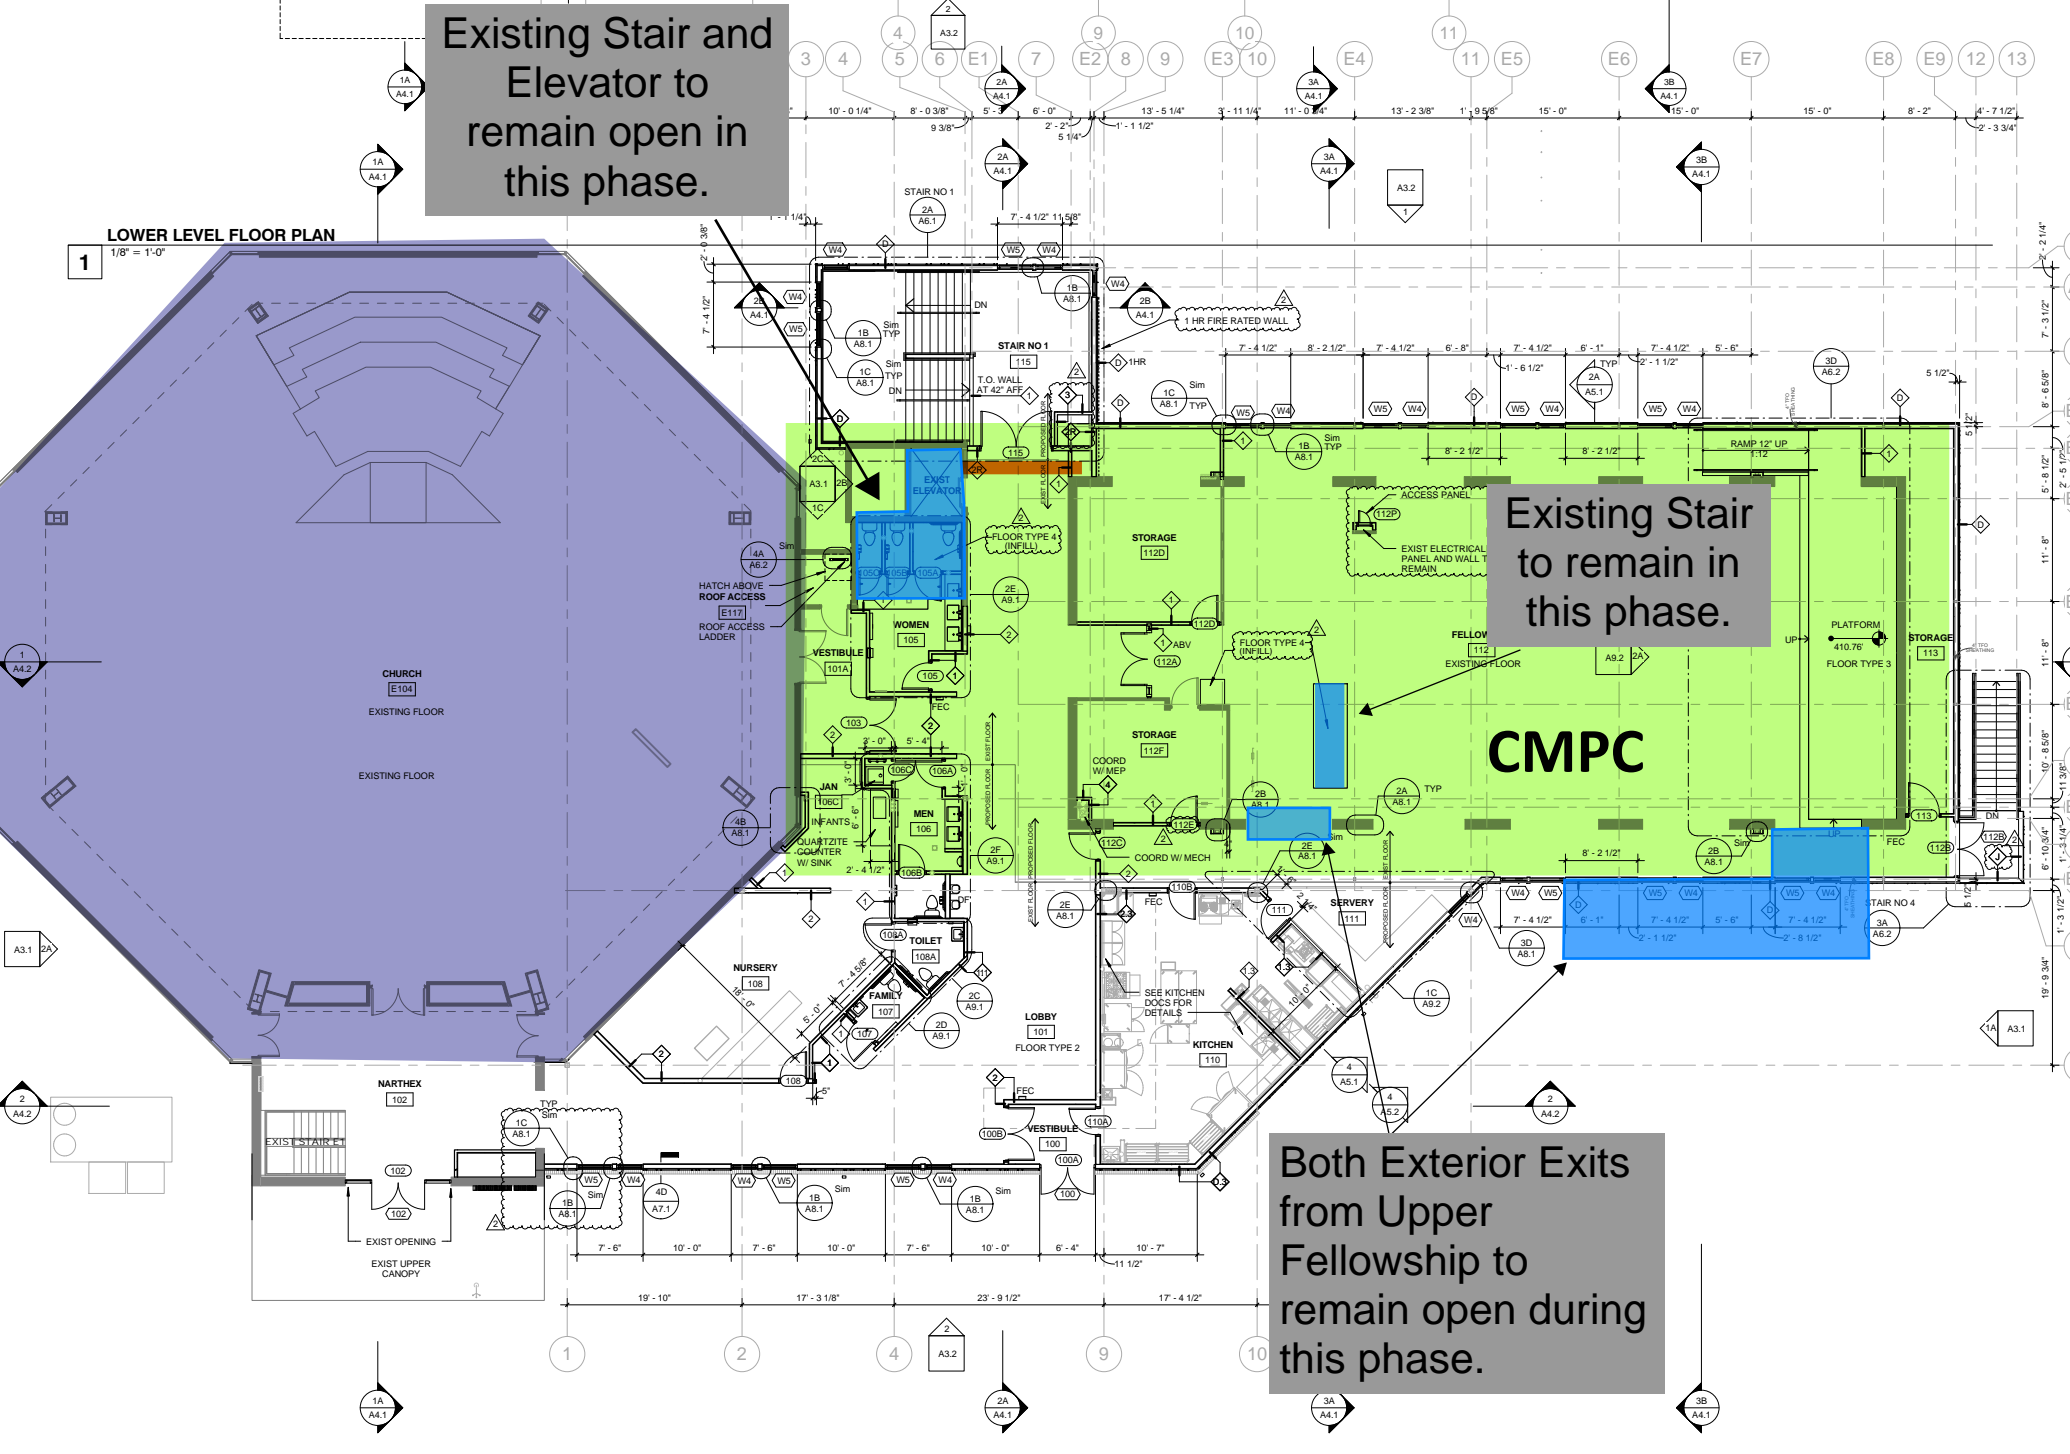
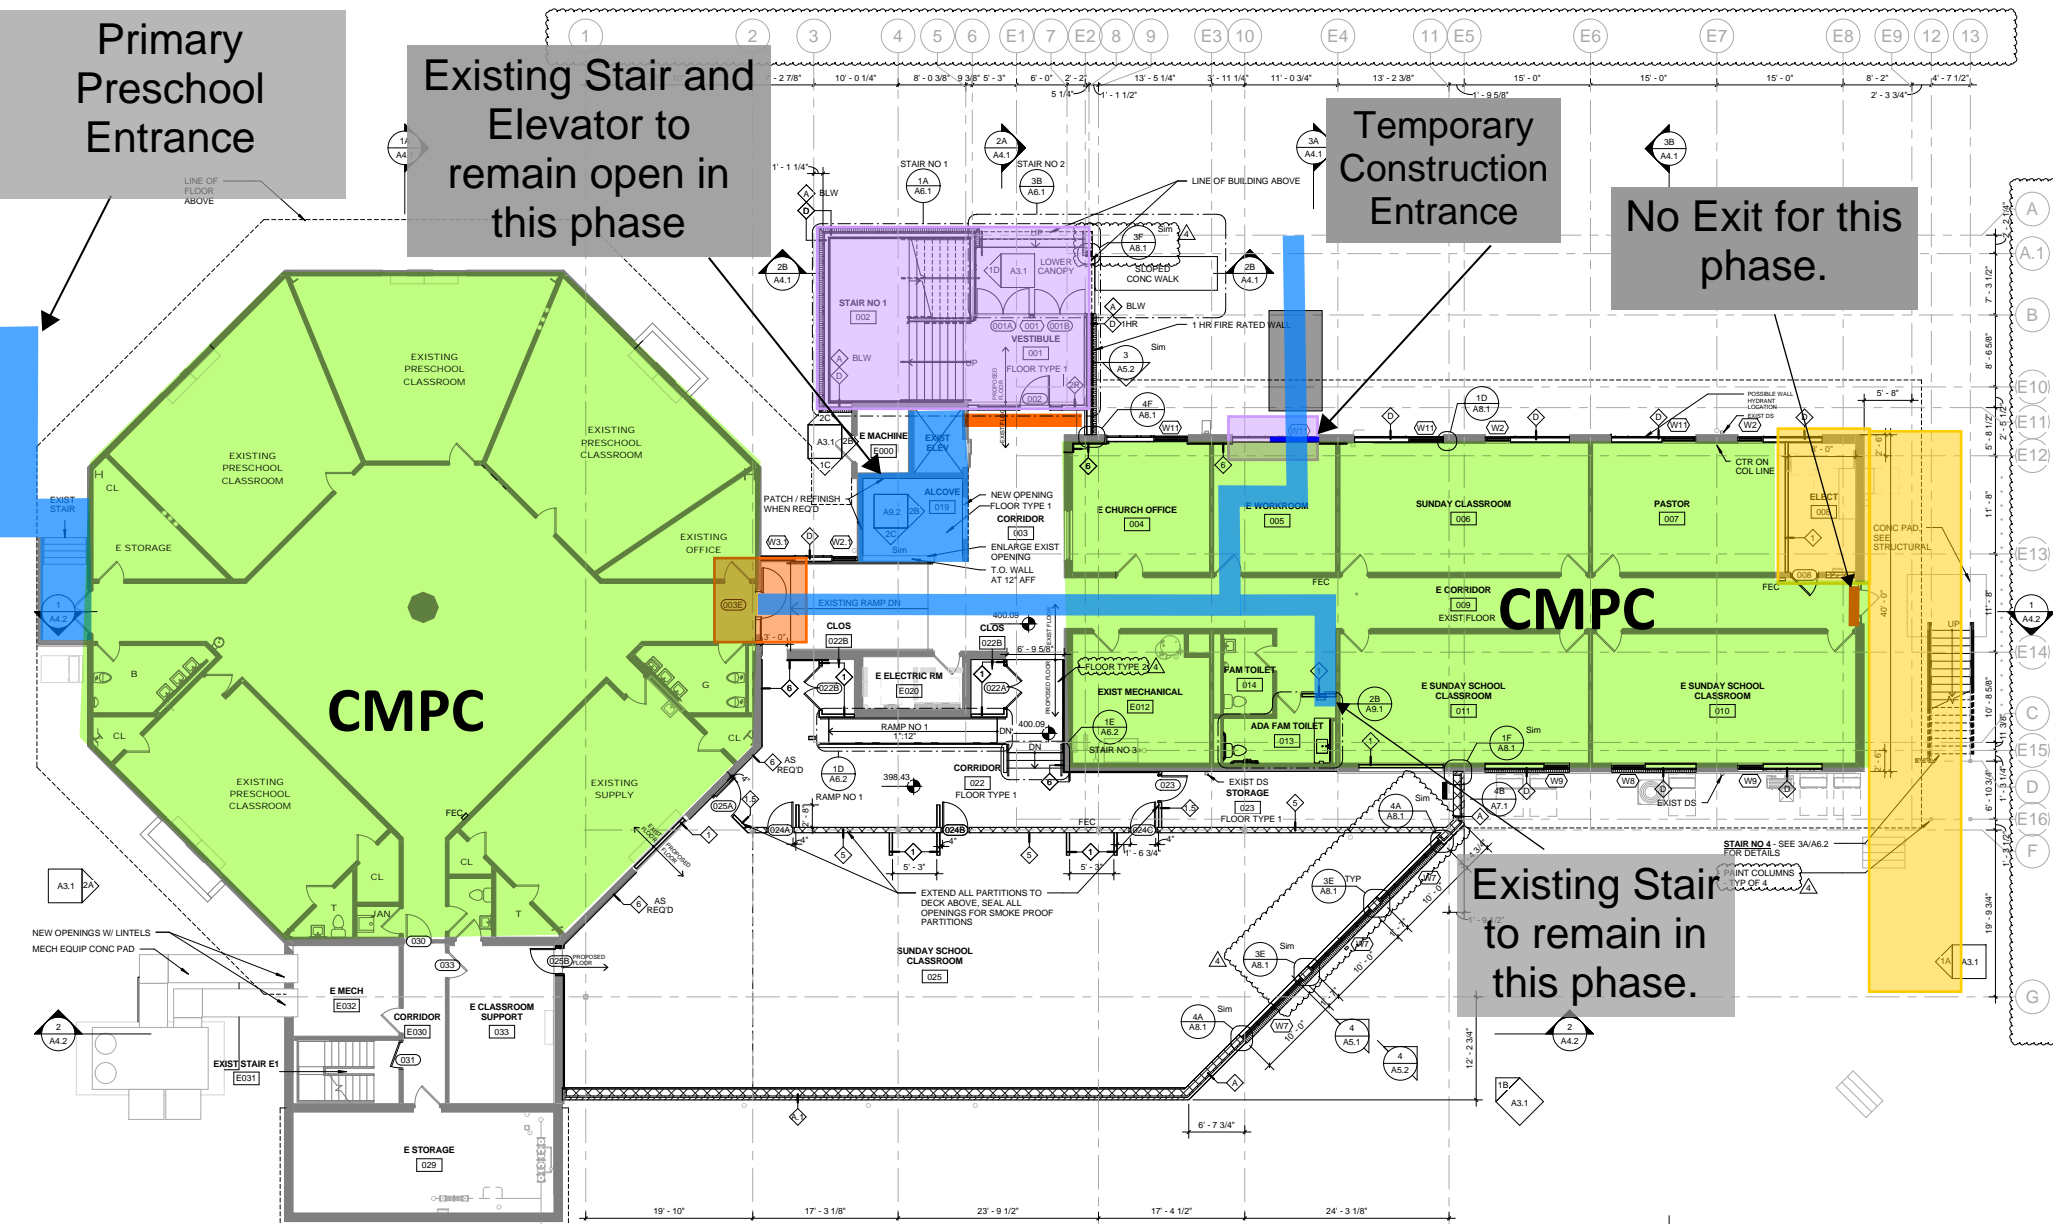




# Christ Memorial - Phasing Plan

## December 2018



- Preschool - No Work
- Lower Level Fellowship - BGE Power Reconfiguration
- Sanctuary - HVAC Upgrade
- Upper Level Fellowship - No Work
- CMPC Occupied
- North Addition - No Work

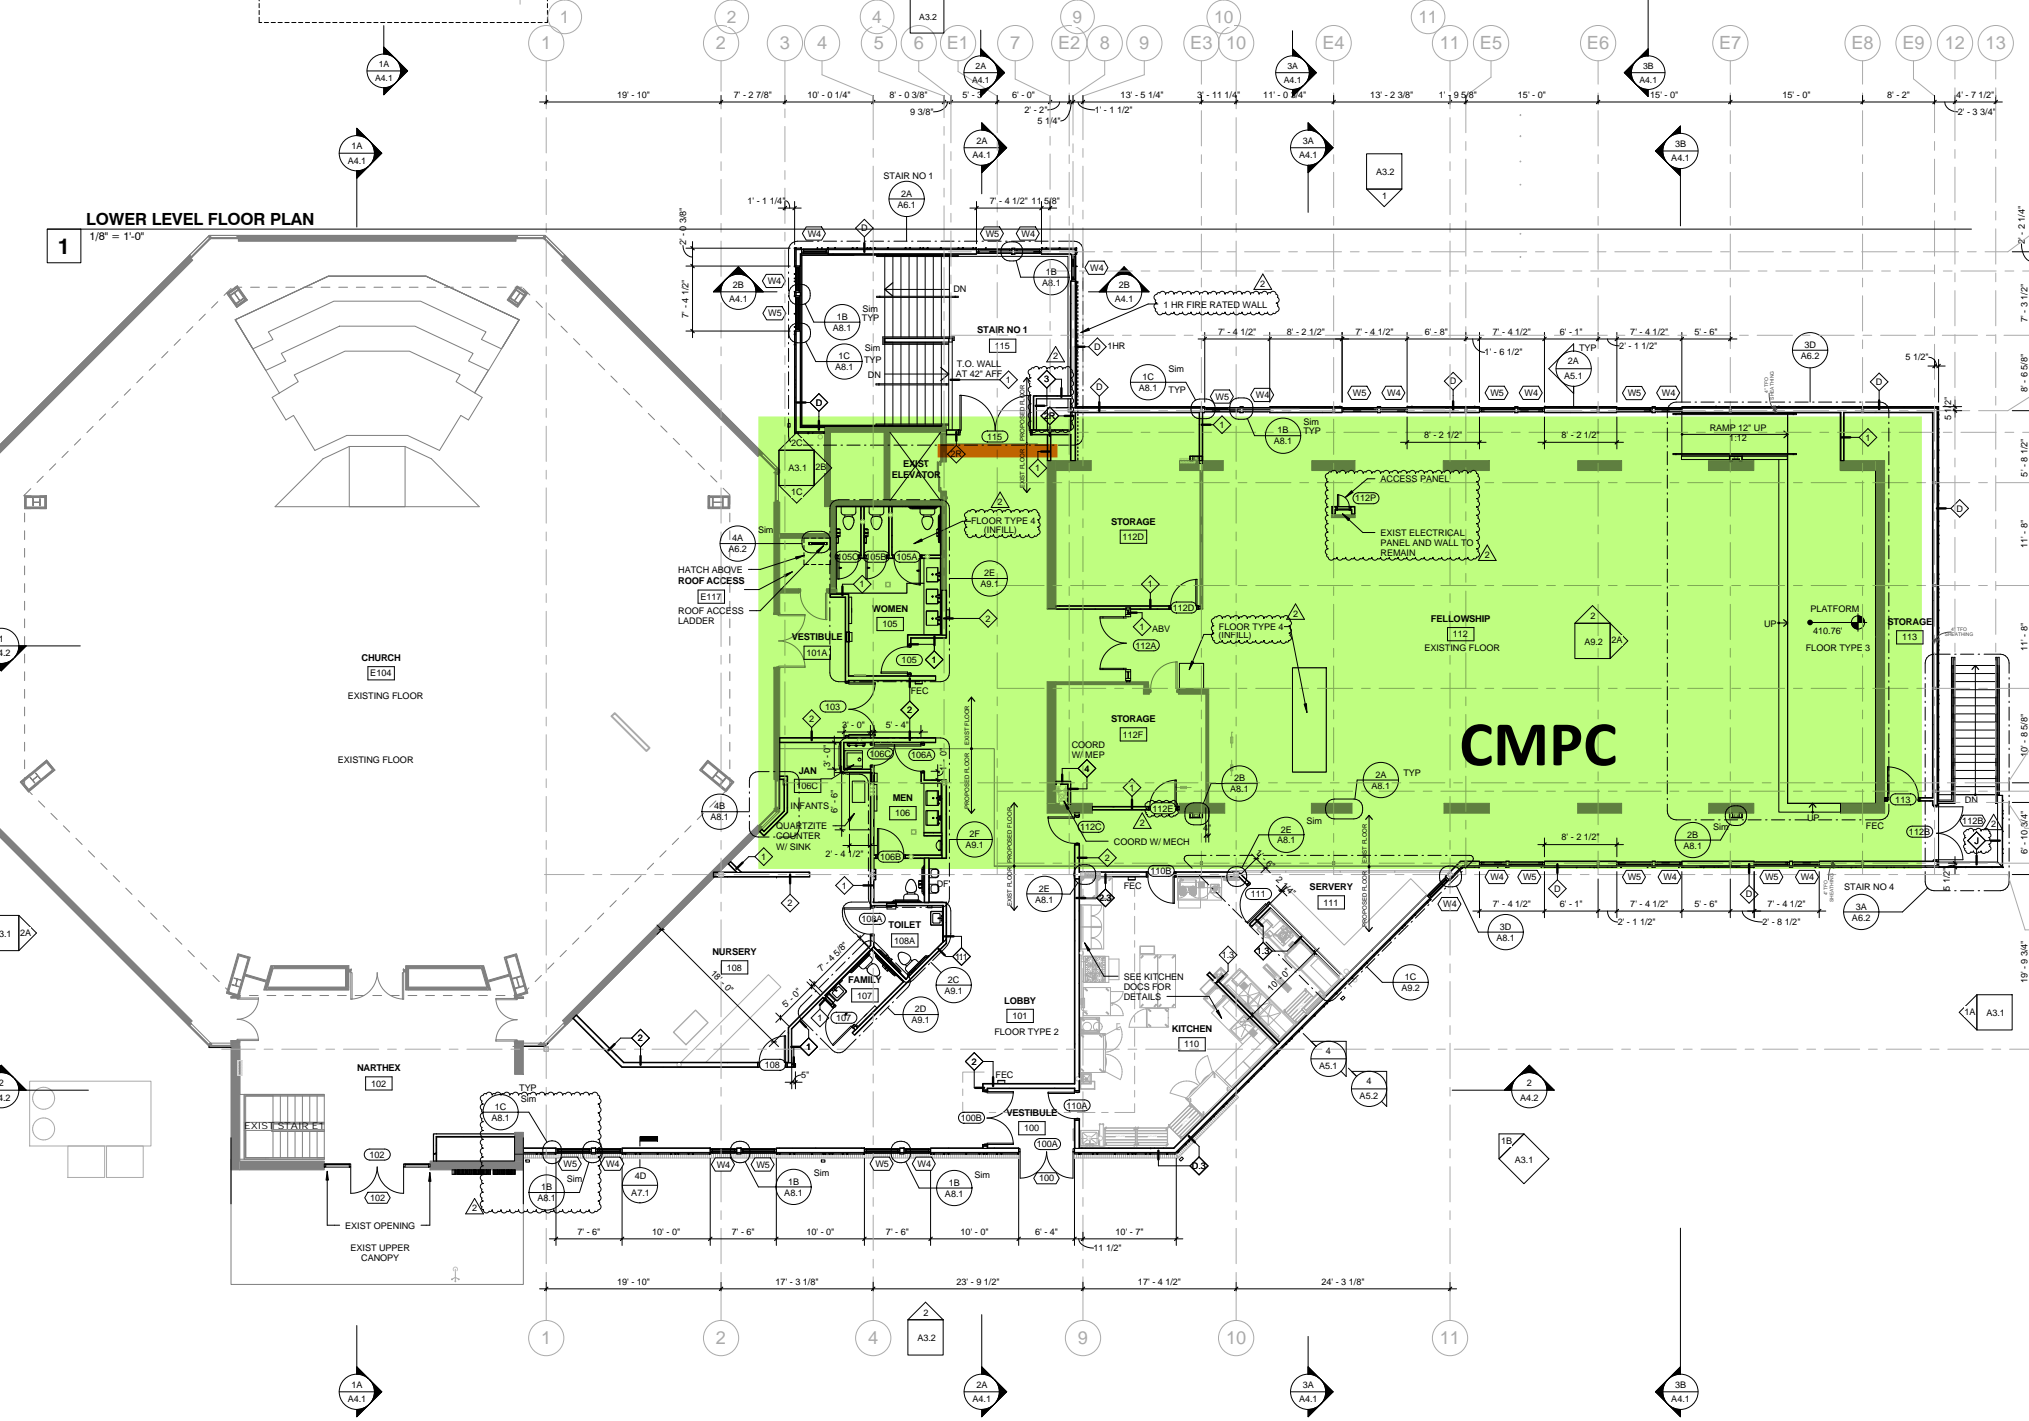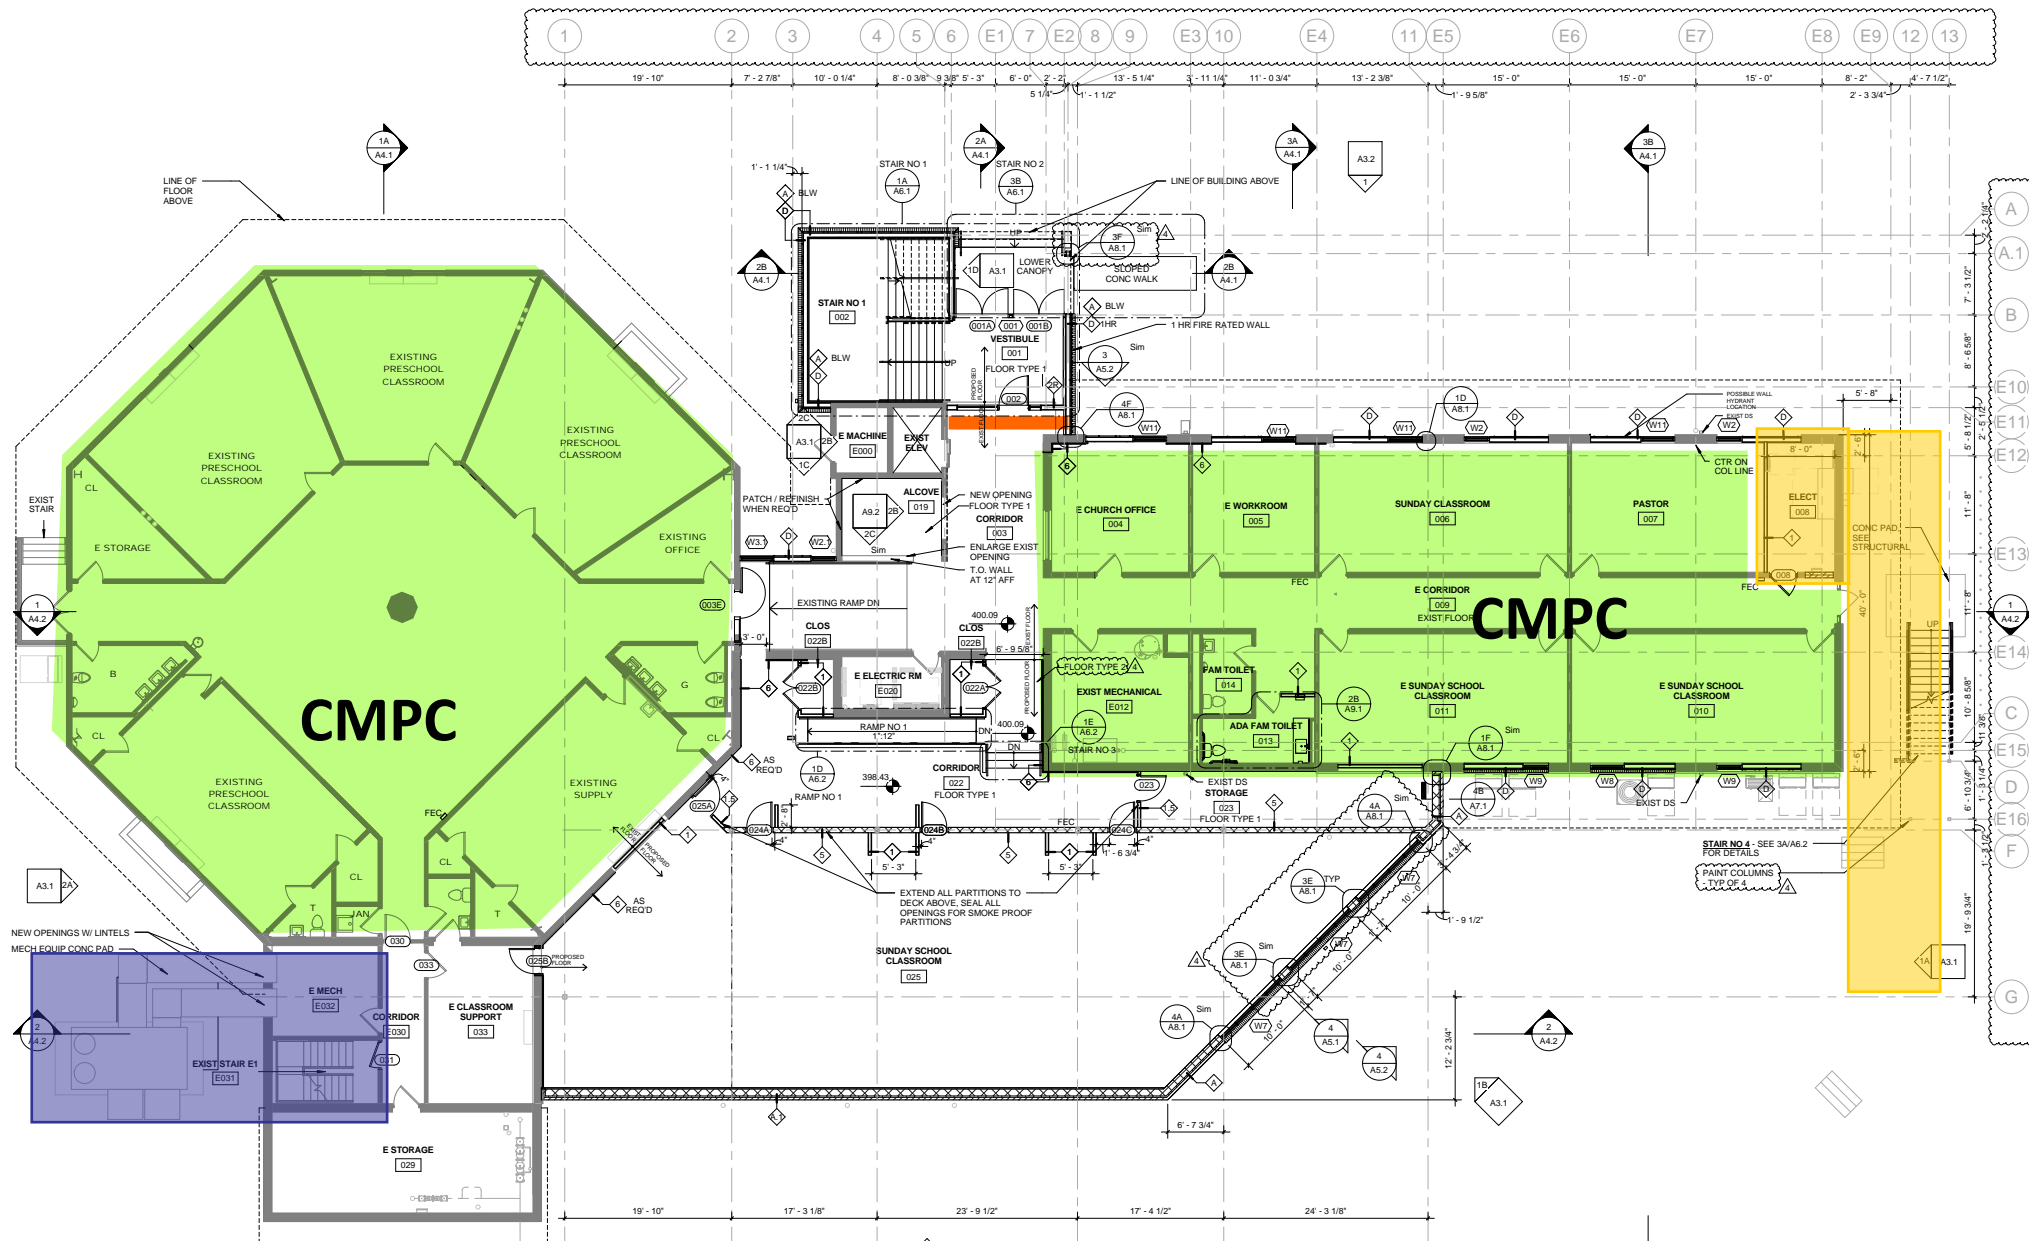

# Christ Memorial - Phasing Plan

## January 2019

- Preschool - No Work
- Lower Level Fellowship - BGE Power Reconfiguration
- Sanctuary - HVAC Upgrade, Fire Alarm Rough In, Framing, Fire Sprinklers, Light Fixture Rough In
- Upper Level Fellowship - No Work
- North Addition - Foundations
- CMPC Occupied

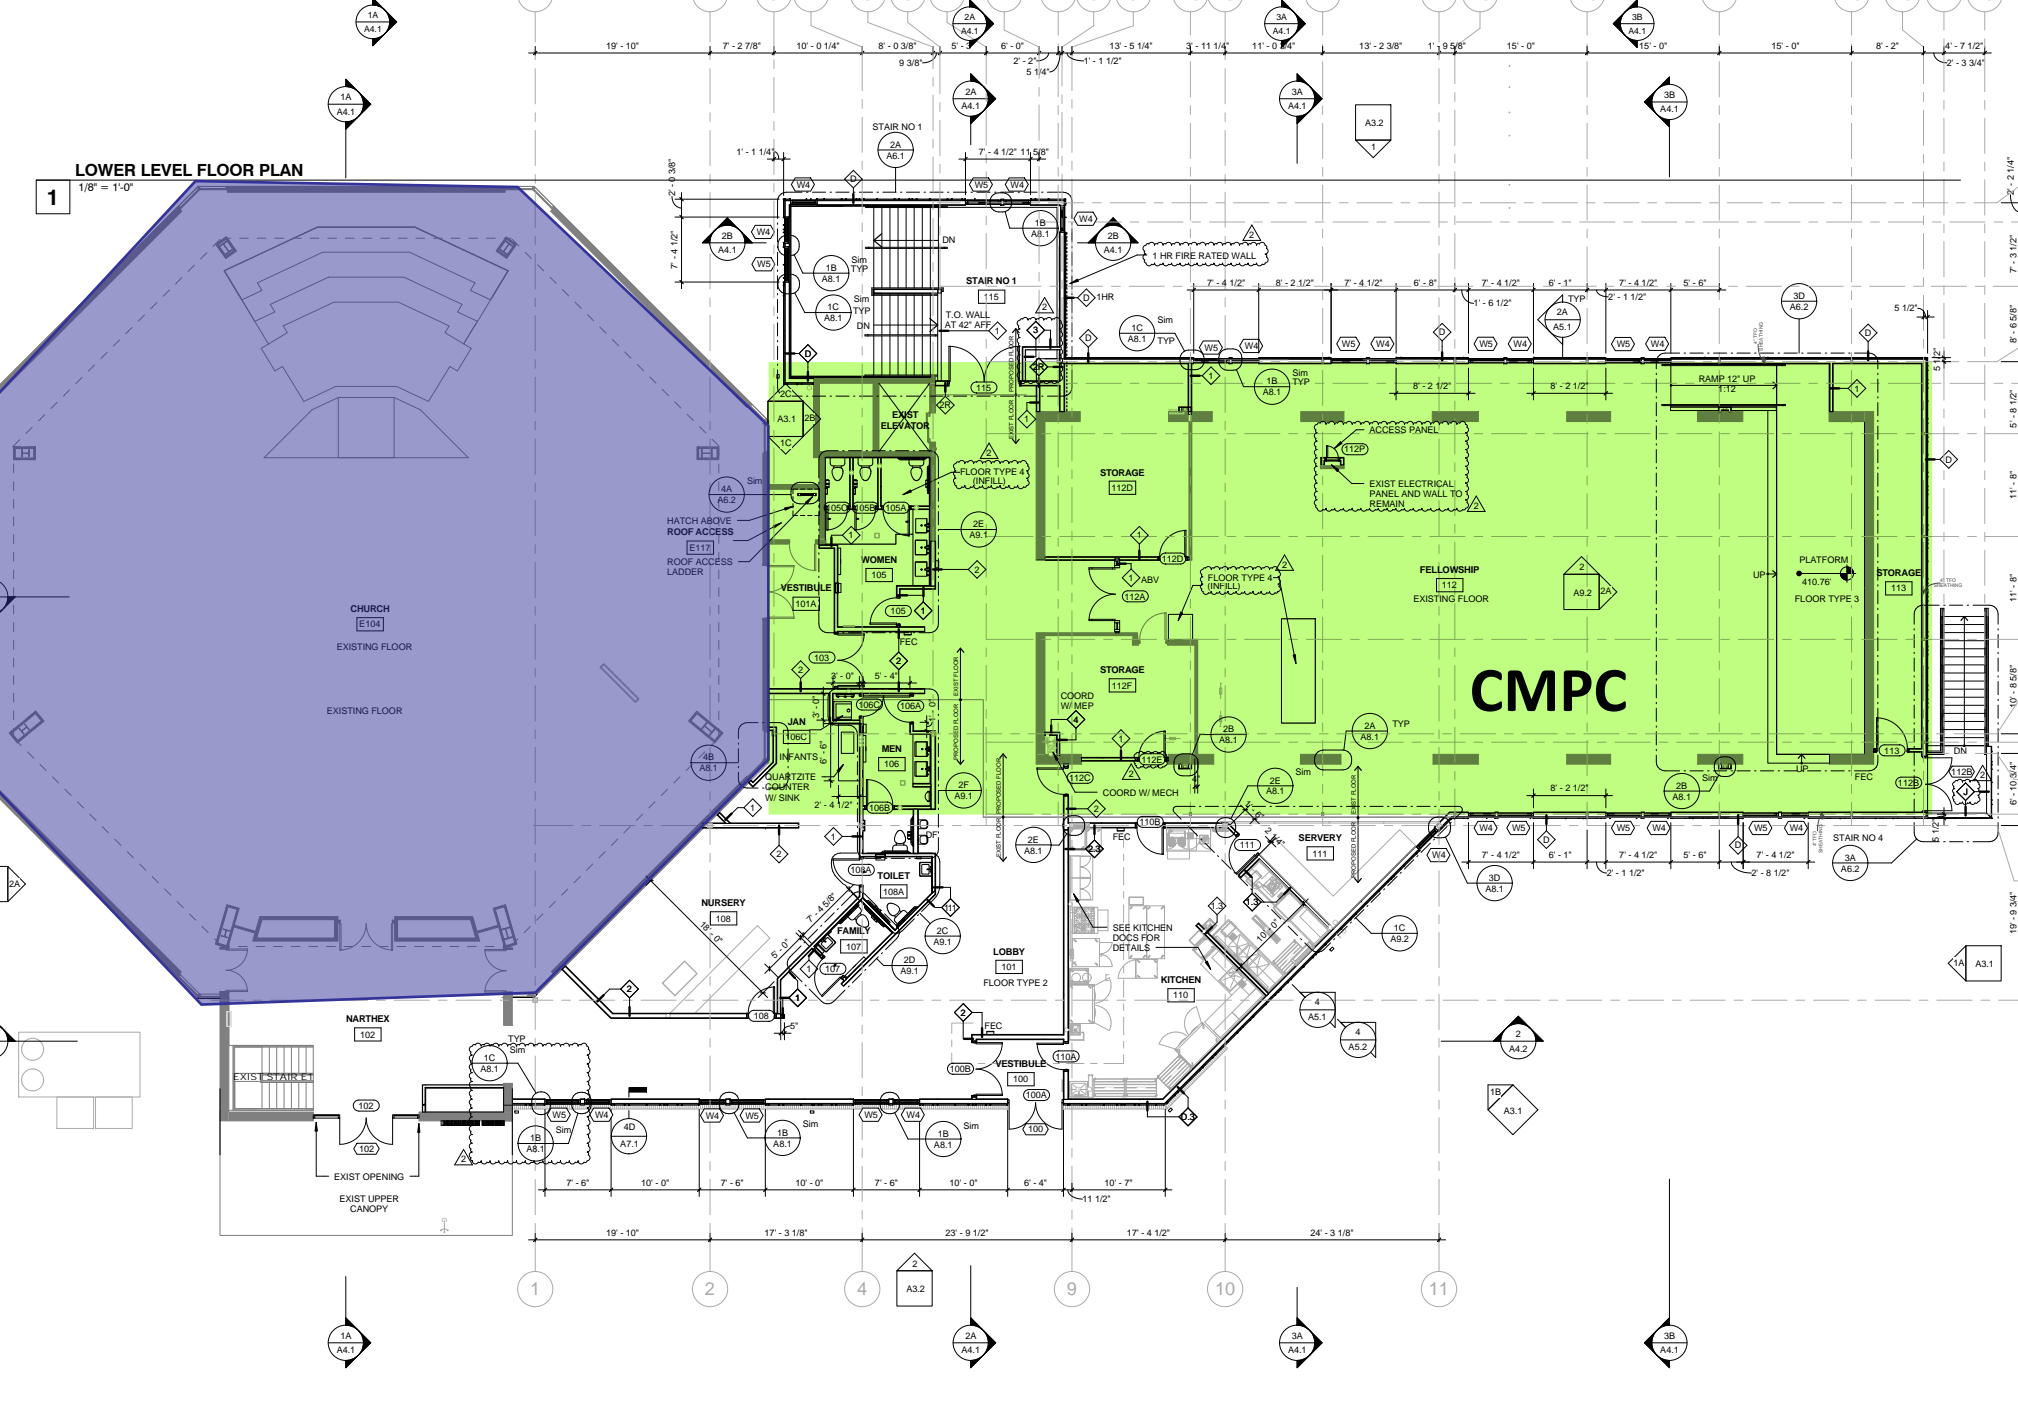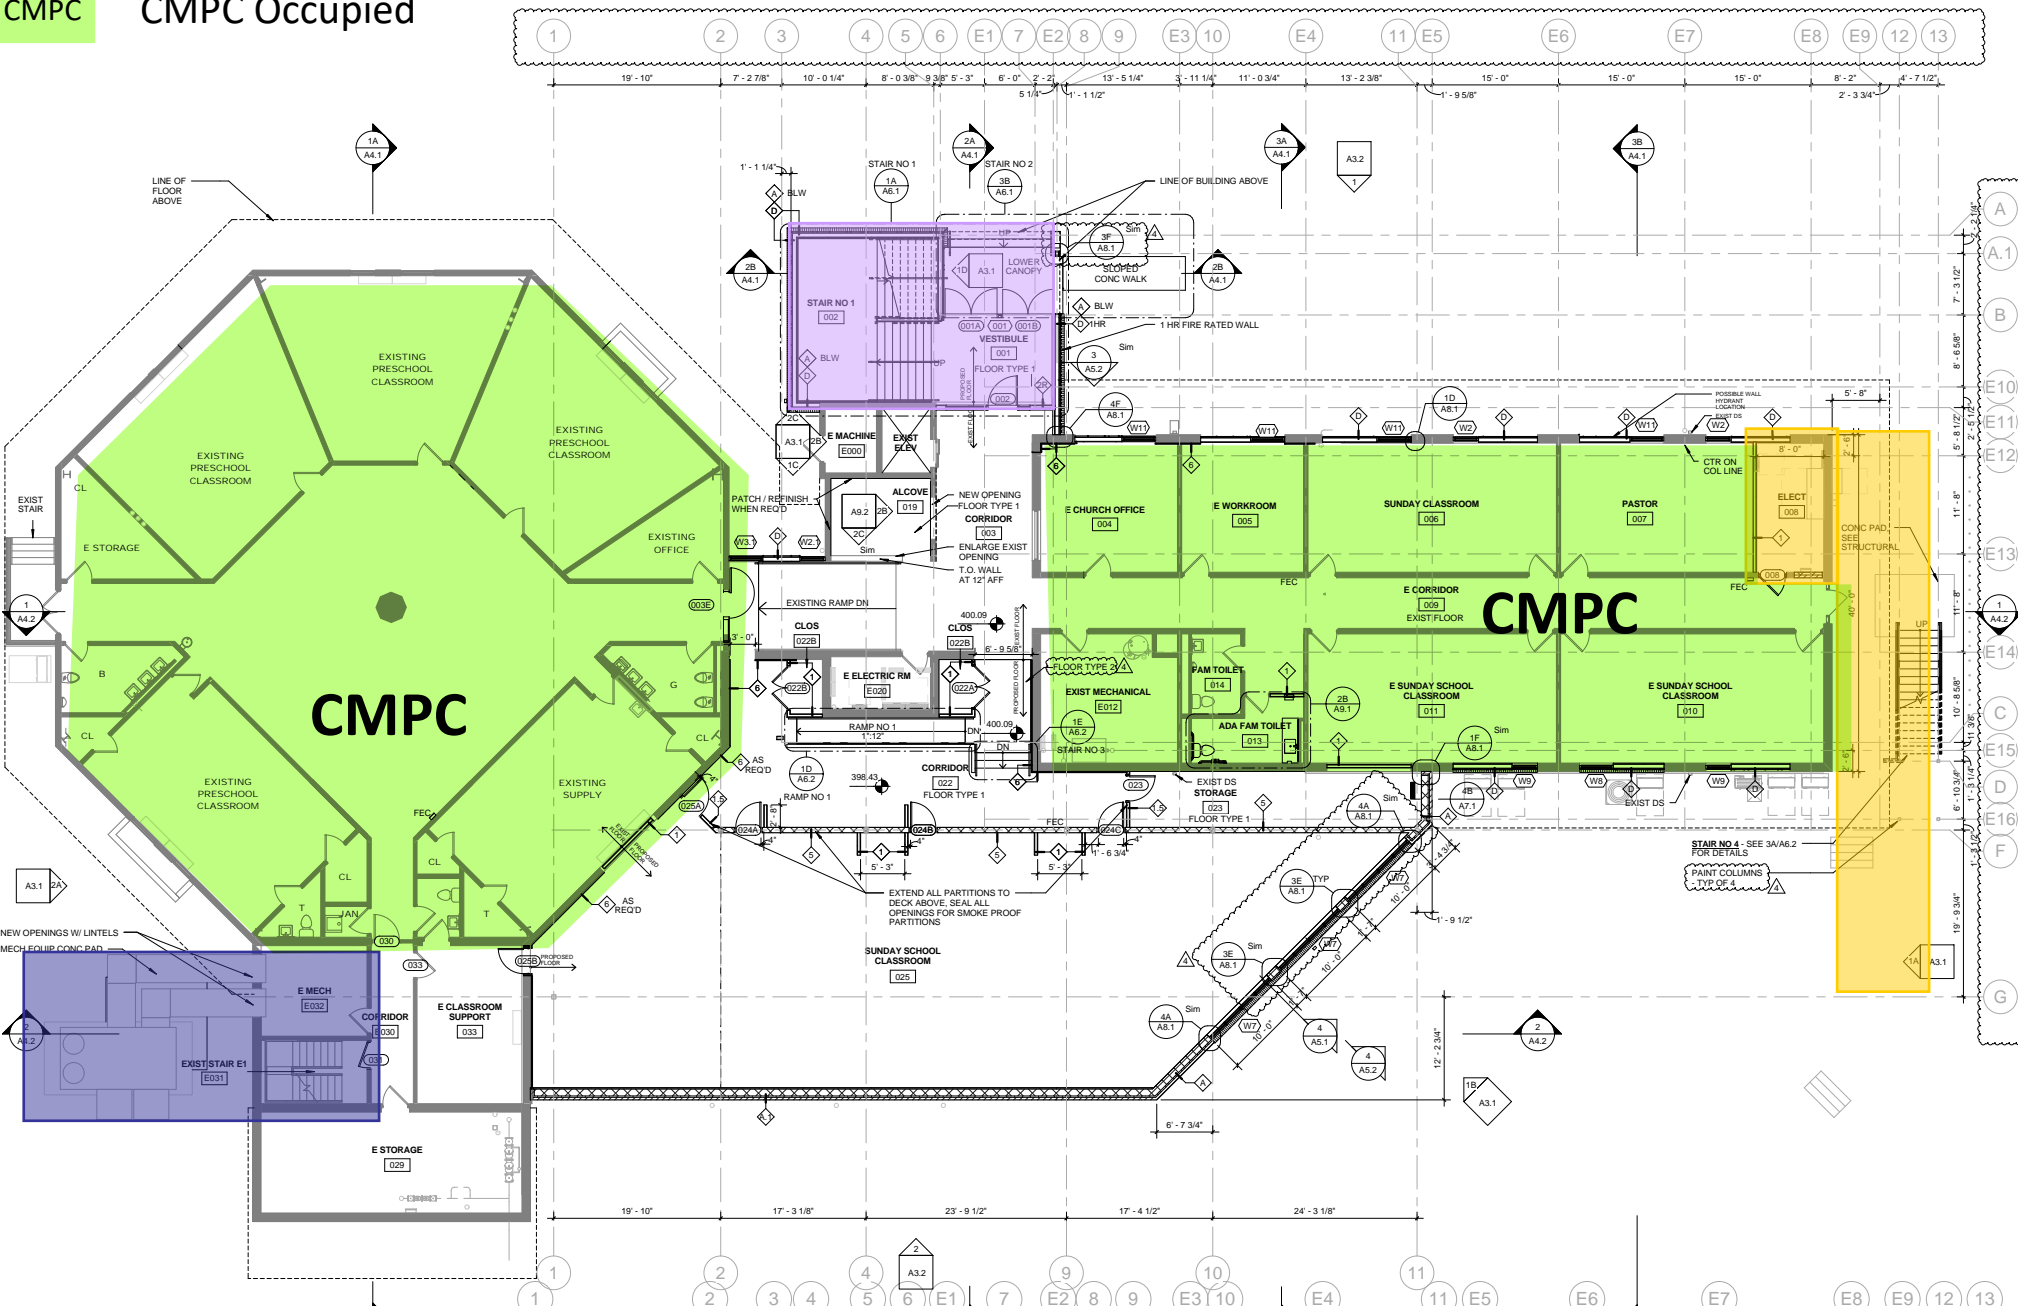



**LOWER LEVEL FLOOR PLAN**  
1/8" = 1'-0"



# Christ Memorial - Phasing Plan

## February 2019

- Preschool - No Work
- Lower Level Fellowship - BGE Power Reconfiguration
- Sanctuary - Fire Alarm Rough In, Framing, Fire Sprinklers, Light Fixture Rough In
- Upper Level Fellowship - No Work
- North Addition - Structure
- CMPC Occupied

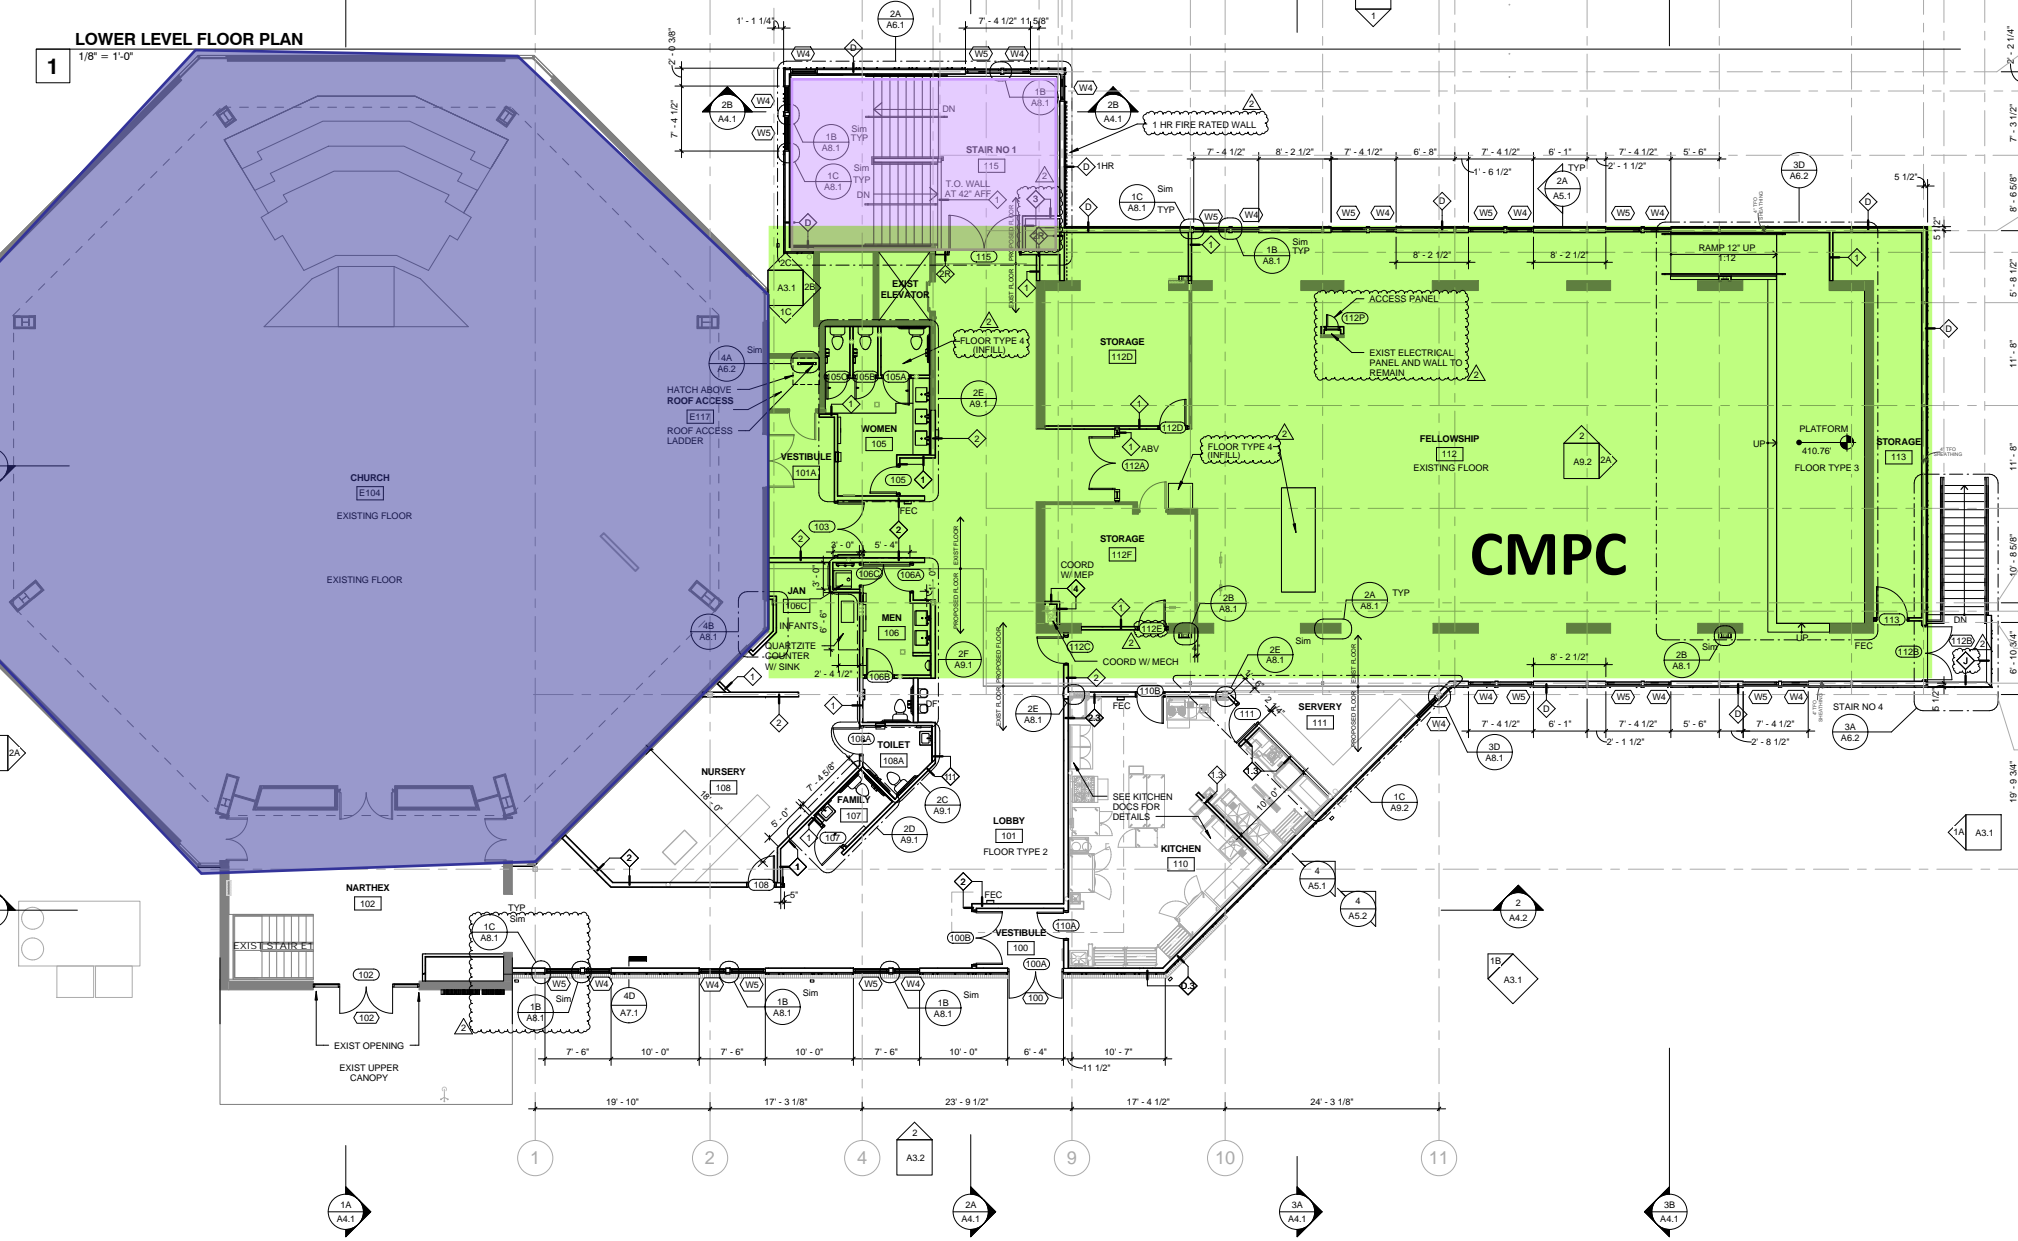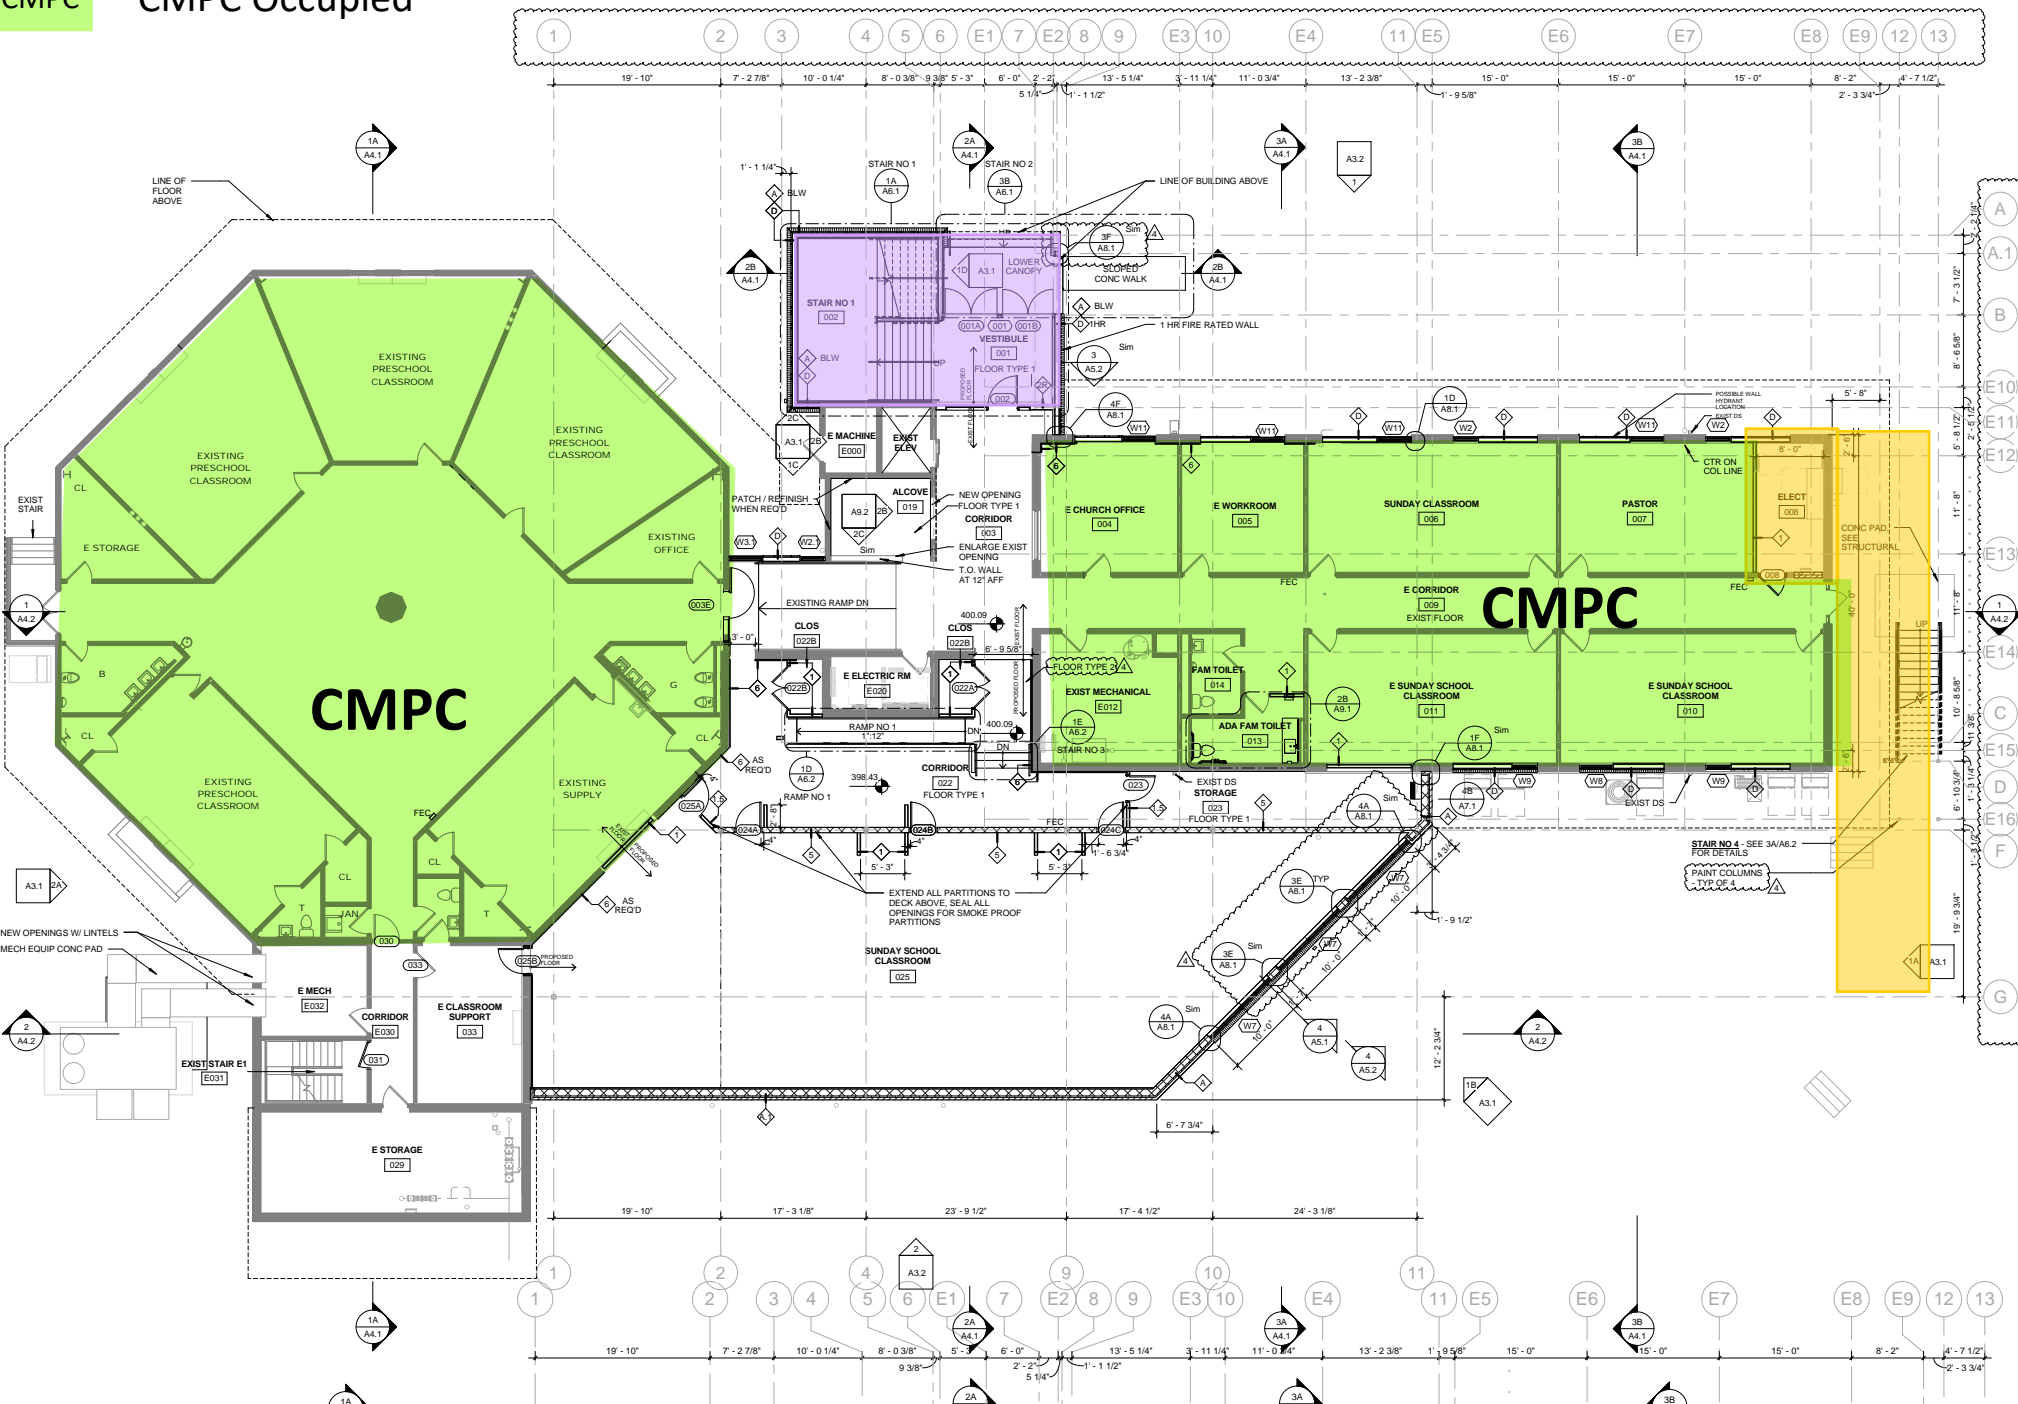


# Christ Memorial - Phasing Plan


## March 2019

- Preschool - No Work
- Lower Level Fellowship - No Work
- Sanctuary - Drywall, Finishes, Fire Alarm Trim Out, Light Fixture Installation
- Upper Level Fellowship - No Work
- South Addition - Prep Building Pad
- North Addition - Structure, Slabs, Roof

CMPC Occupied

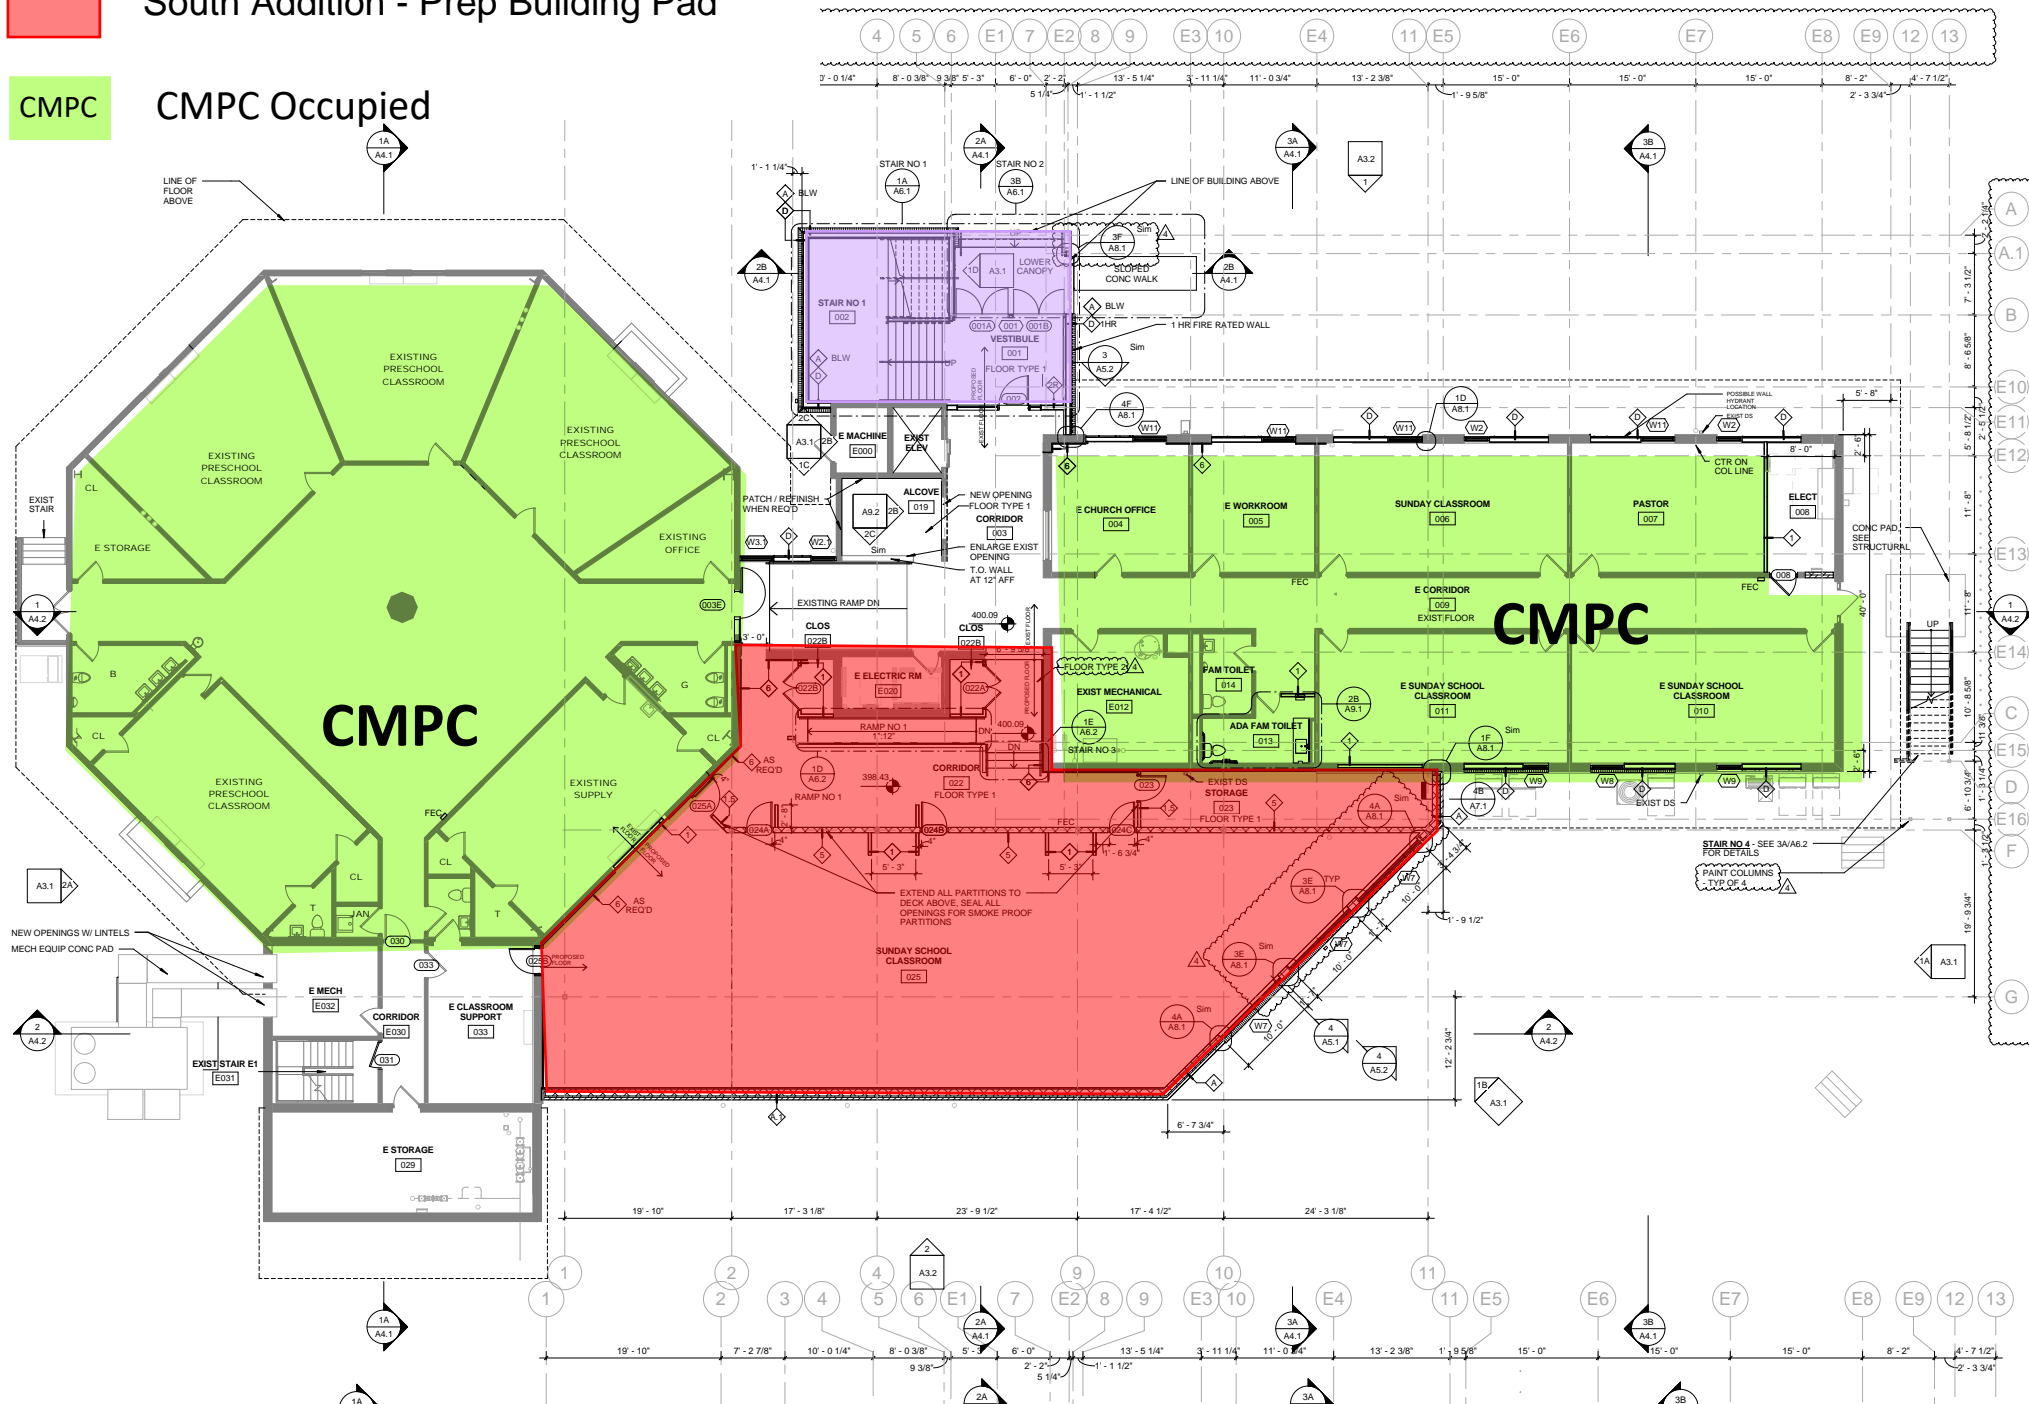

**LOWER LEVEL FLOOR PLAN**  
1/8" = 1'-0"

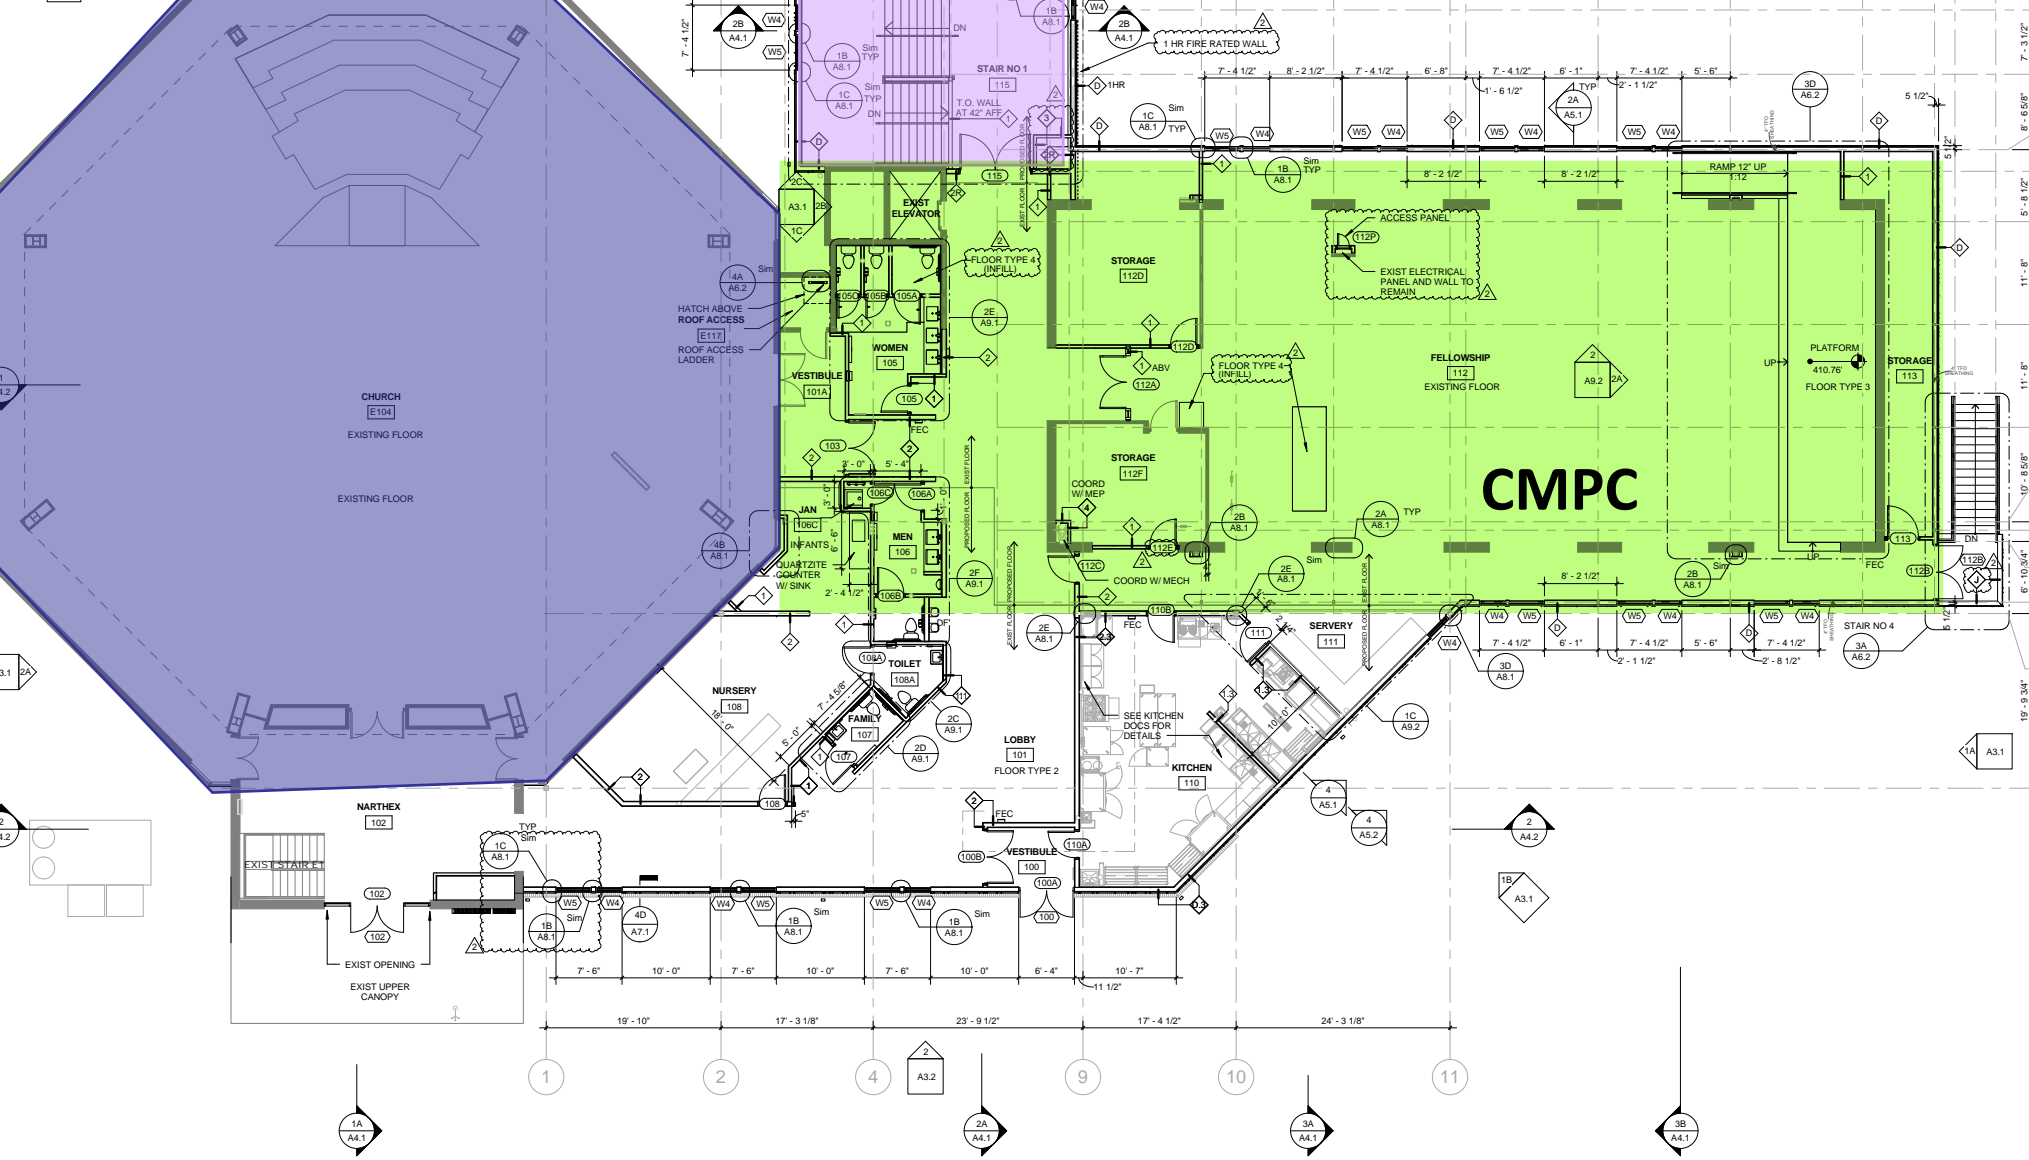




# Christ Memorial - Access Routes

## March 2019 - Mid April 2019

- Preschool
- Lower Level Fellowship
- CMPC
- Access Routes
- CMPC Occupied
- Sanctuary
- Upper Level Fellowship
- North Addition
- South Addition

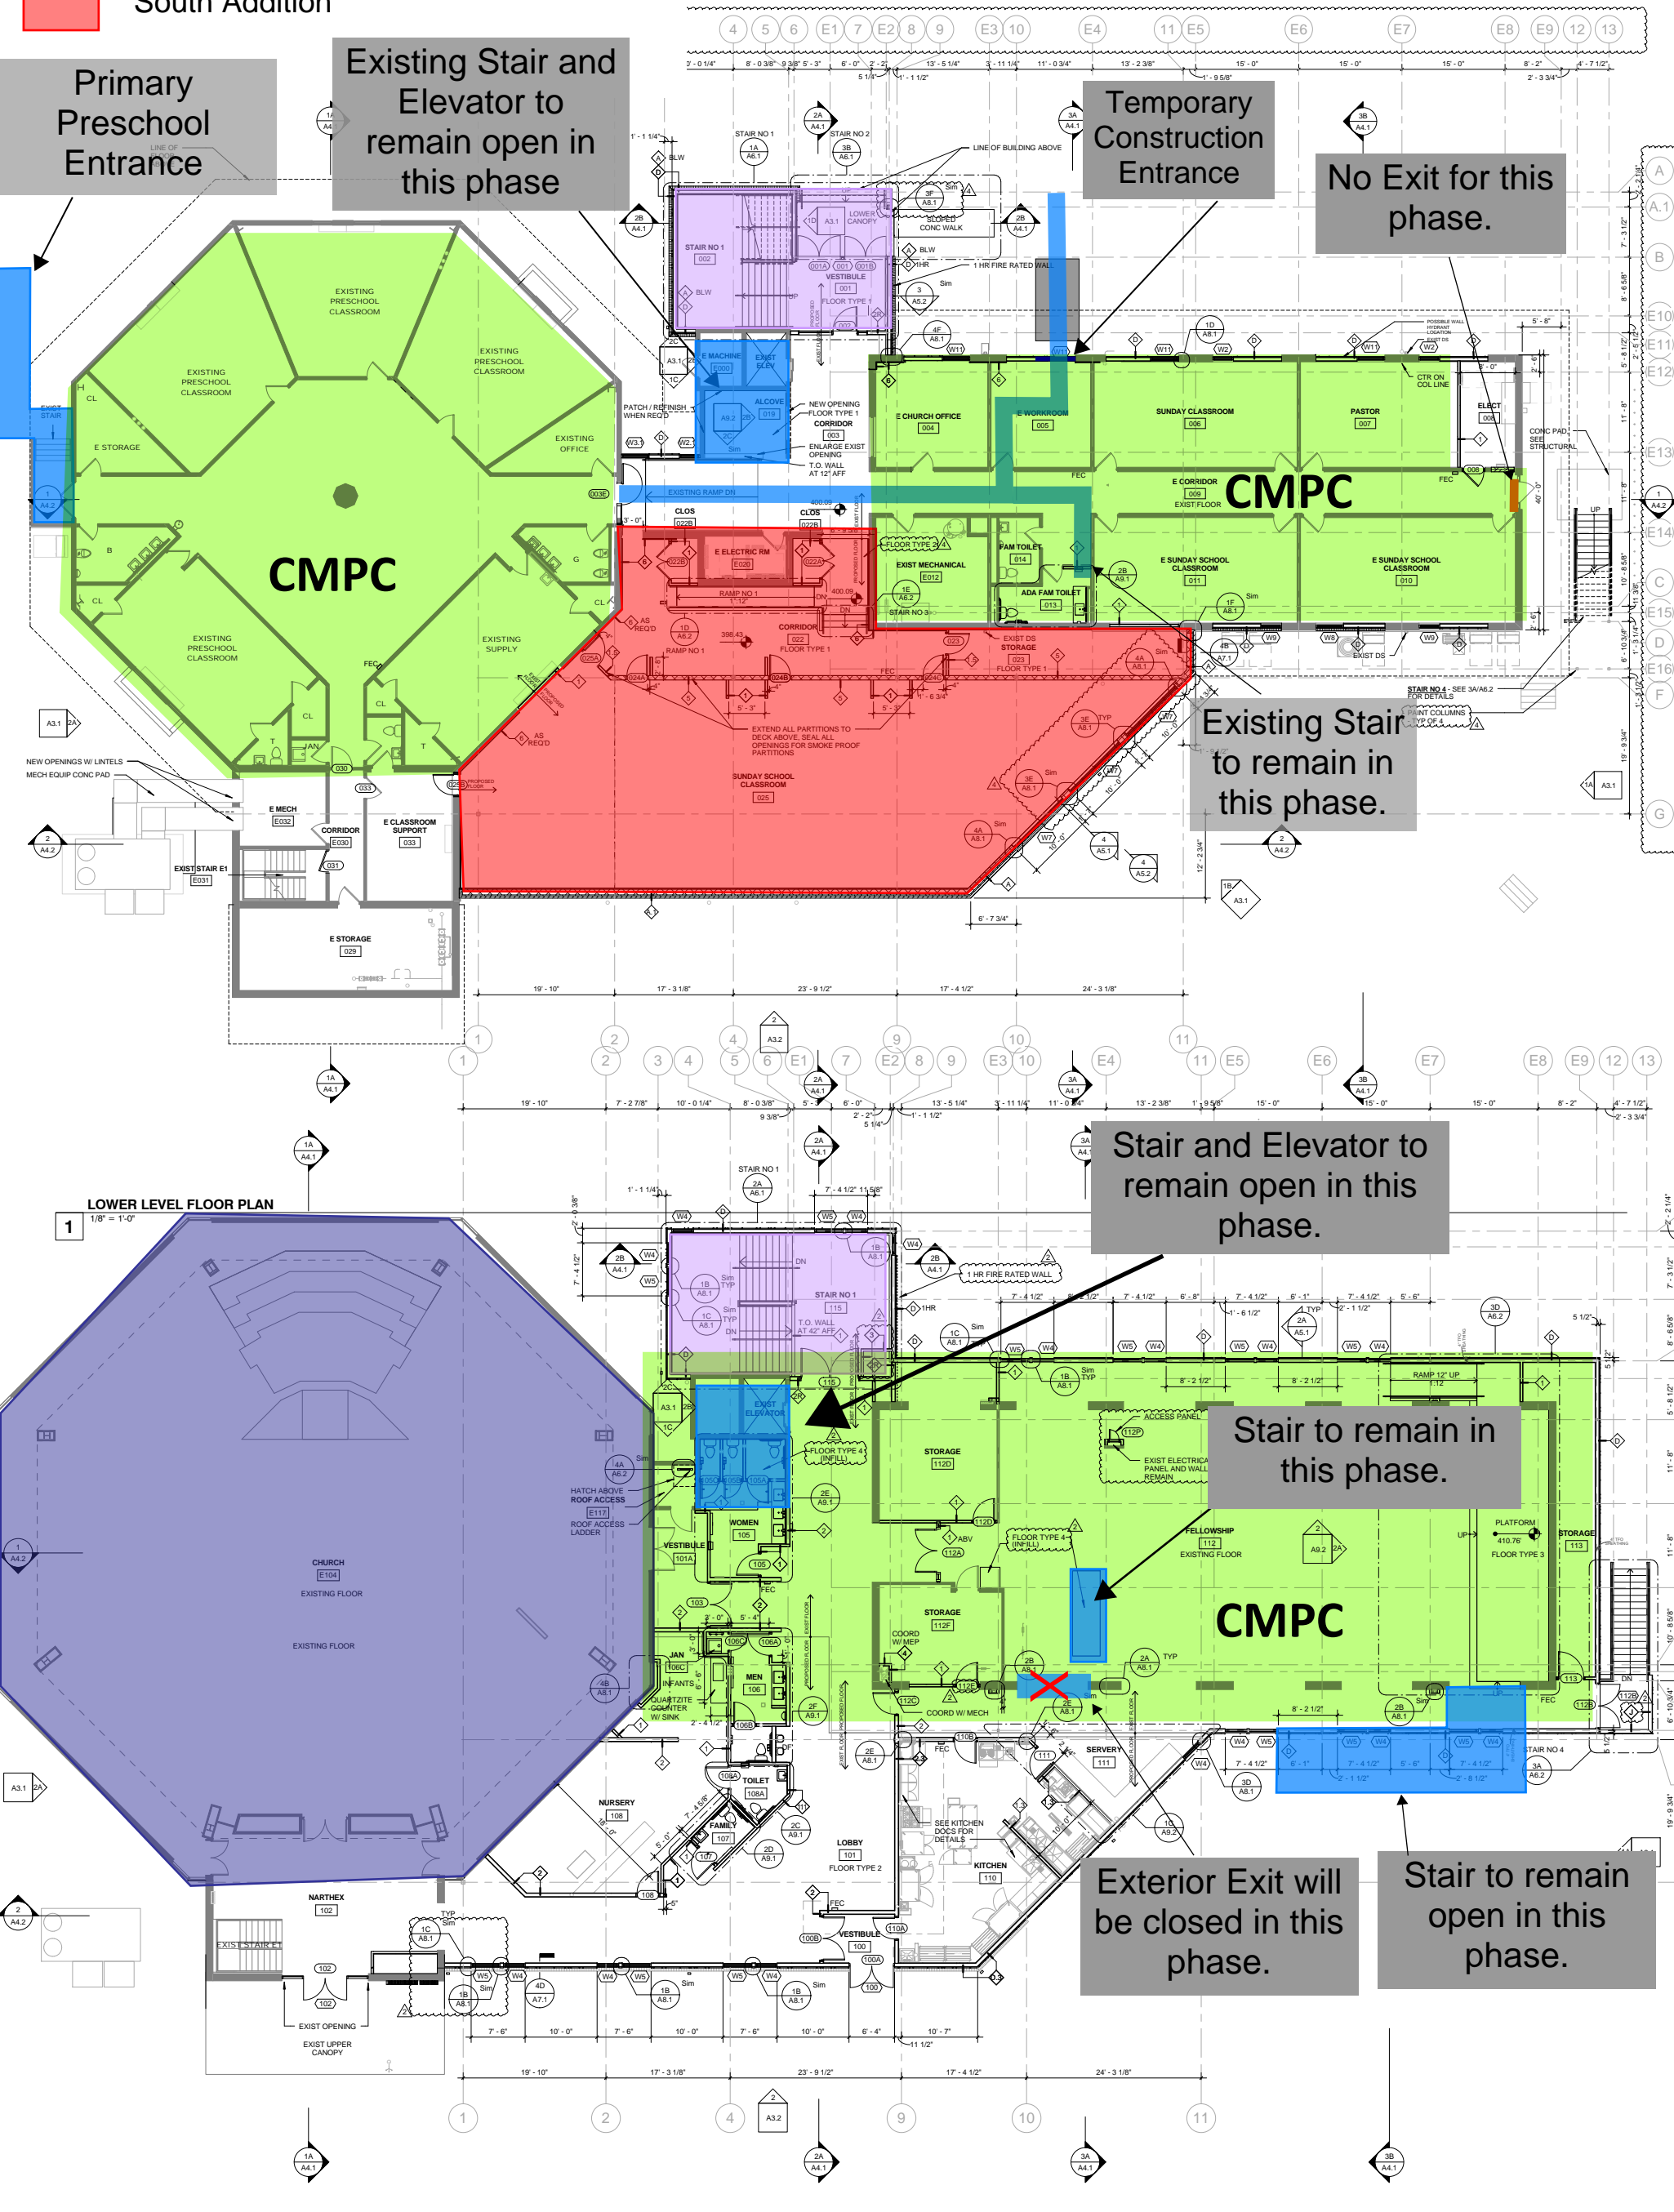


# Christ Memorial - Phasing Plan


## April 2019

- Preschool - No Work
- Lower Level Fellowship - Demolition, Framing
- Sanctuary - EIFS, Roofing
- Upper Level Fellowship - Demolition, Framing
- South Addition - Foundations, Structure
- North Addition - Roof, Framing, Facade, Doors, Windows, MEP Rough In

CMPC CMPC Occupied

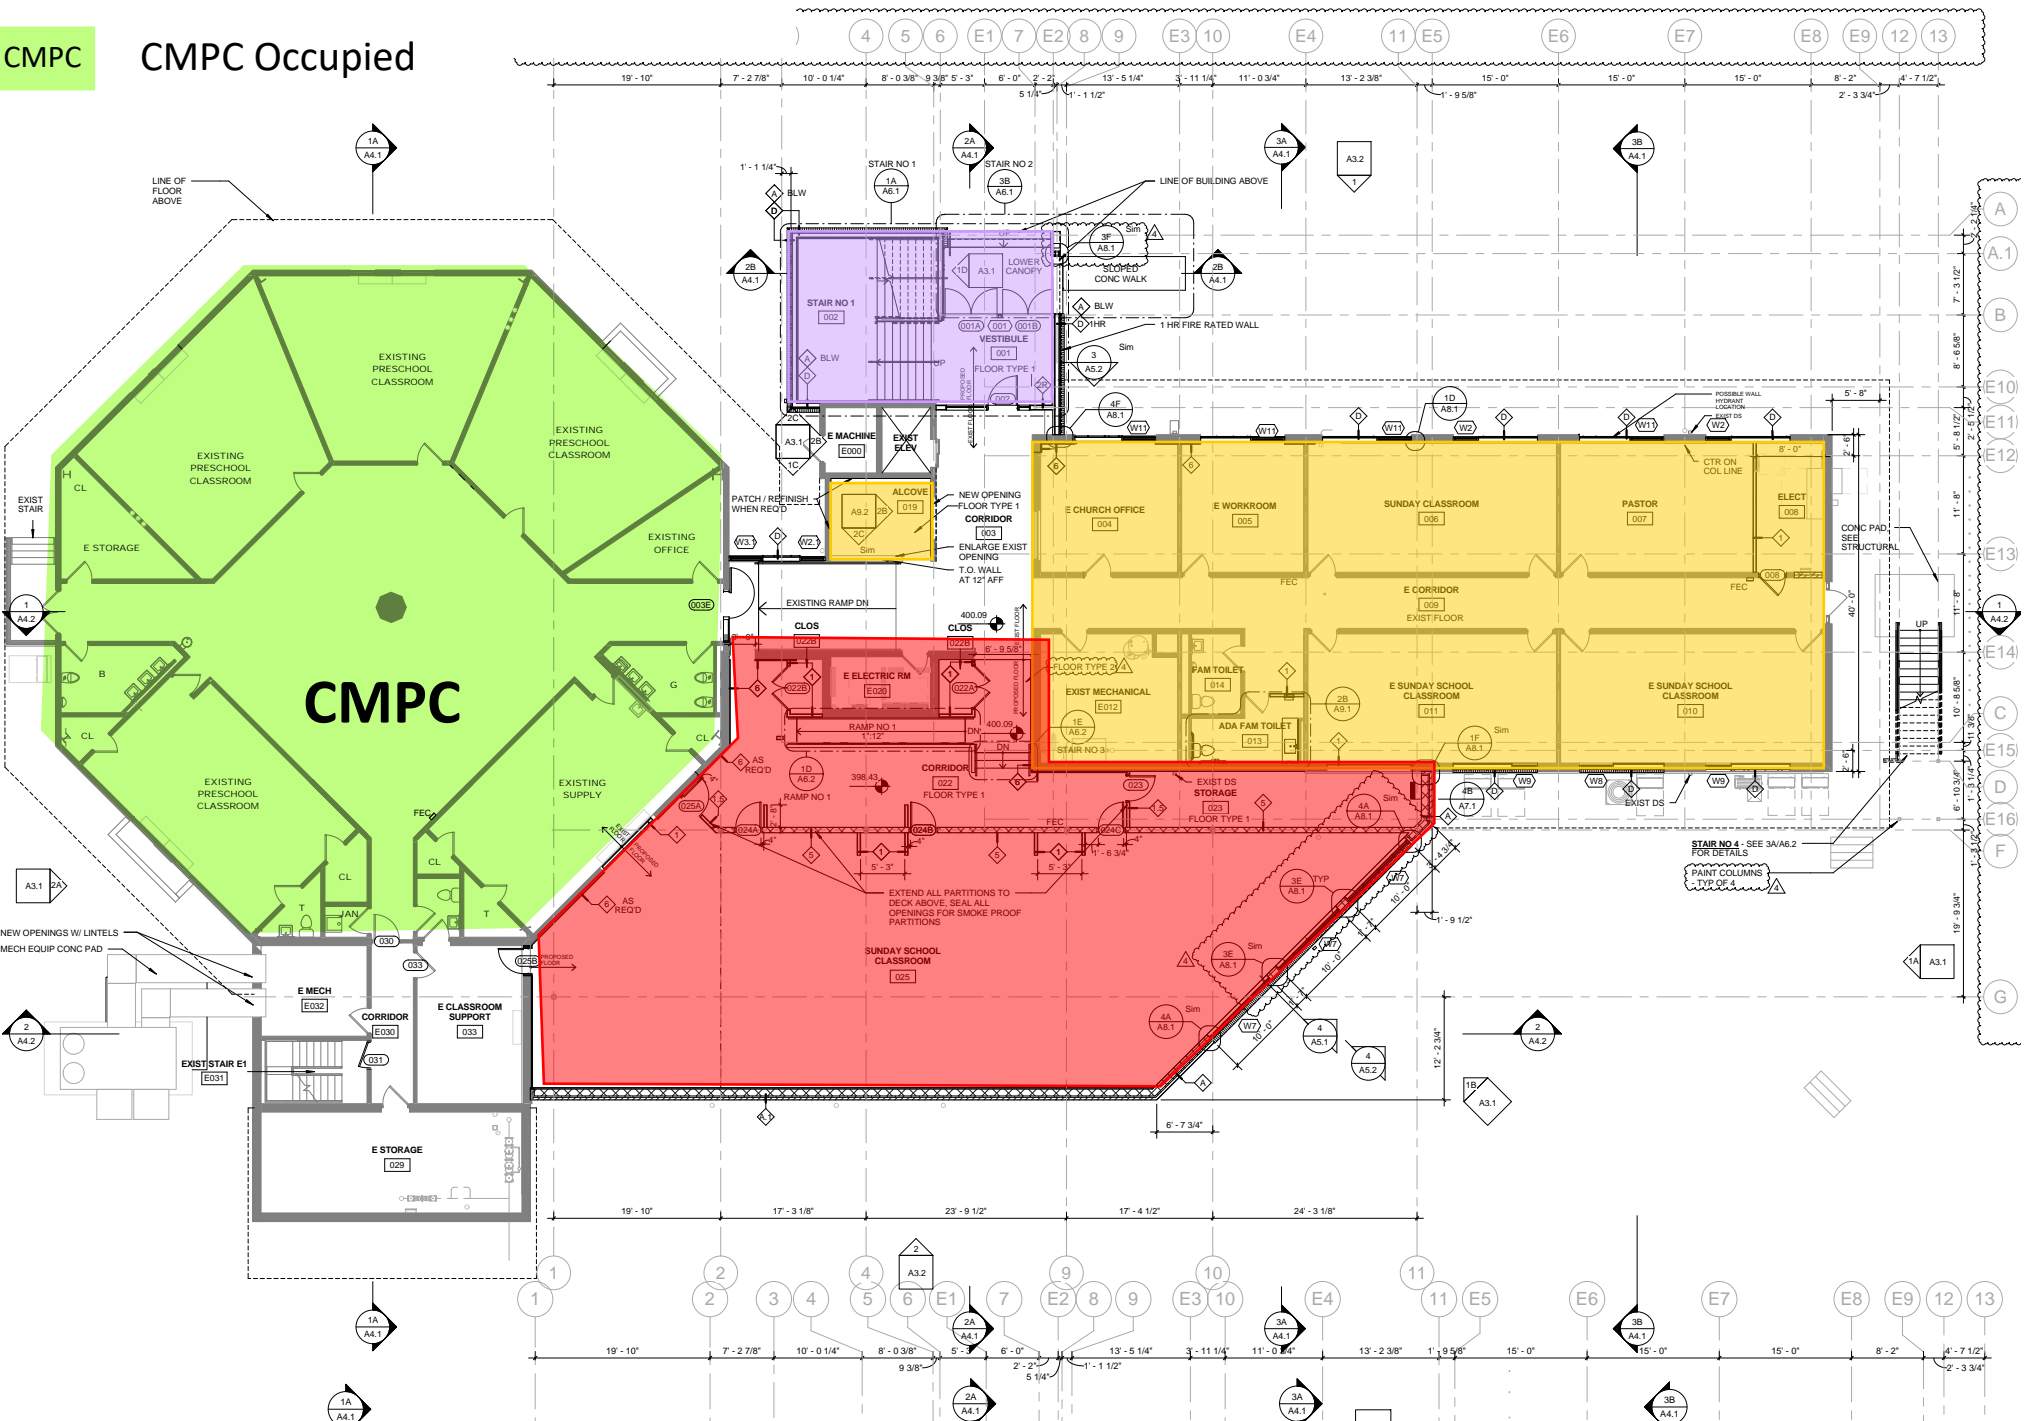

**LOWER LEVEL FLOOR PLAN**  
1/8" = 1'-0"

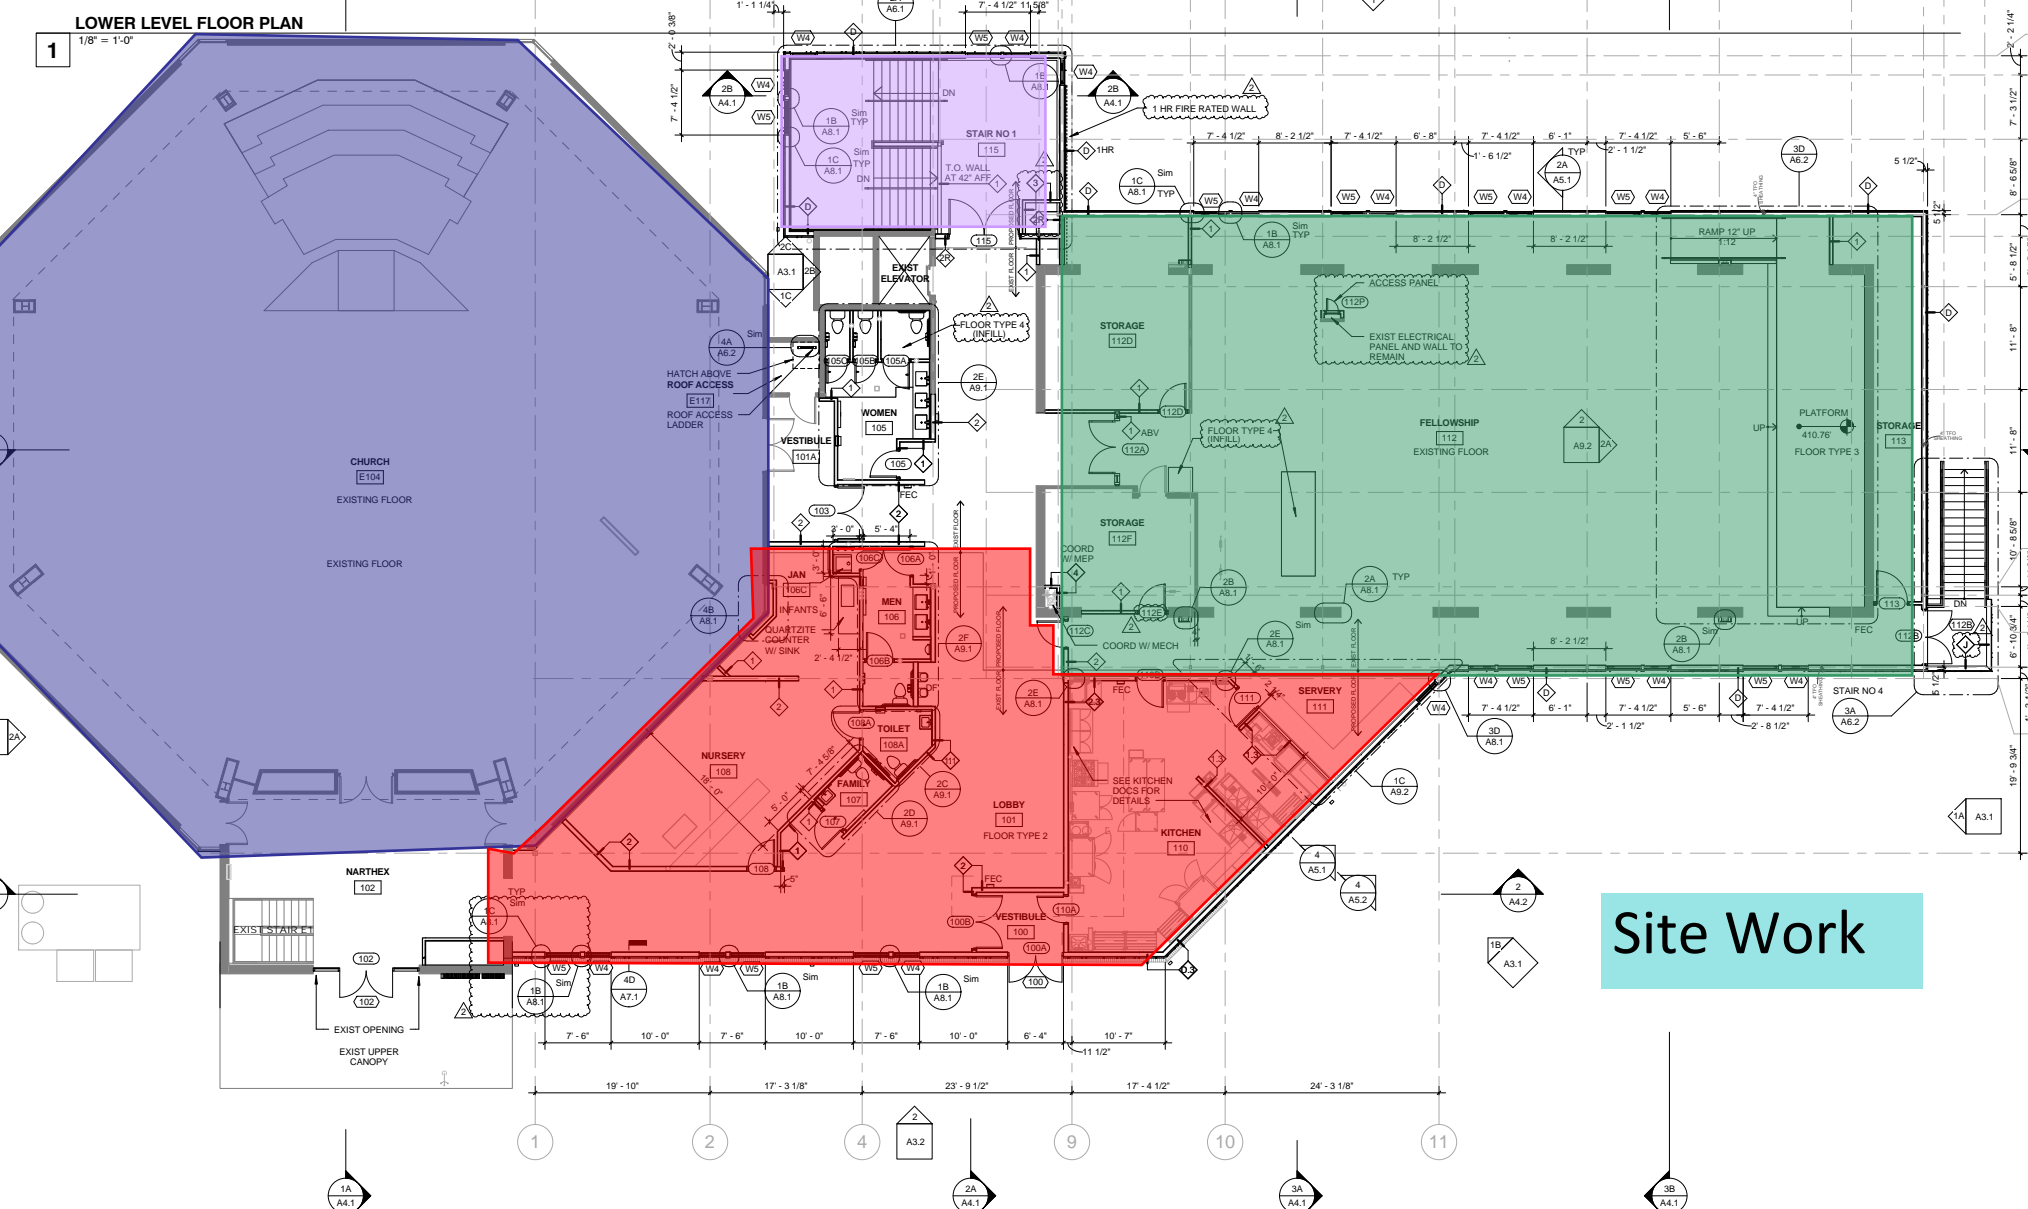

**Site Work**




# Christ Memorial - Access Routes

Mid April 2019 - June 2019

- Preschool
- Sanctuary
- South Addition

- Access Routes
- Lower Level Fellowship
- Upper Level Fellowship
- North Addition
- CMPC
- CMPC Occupied

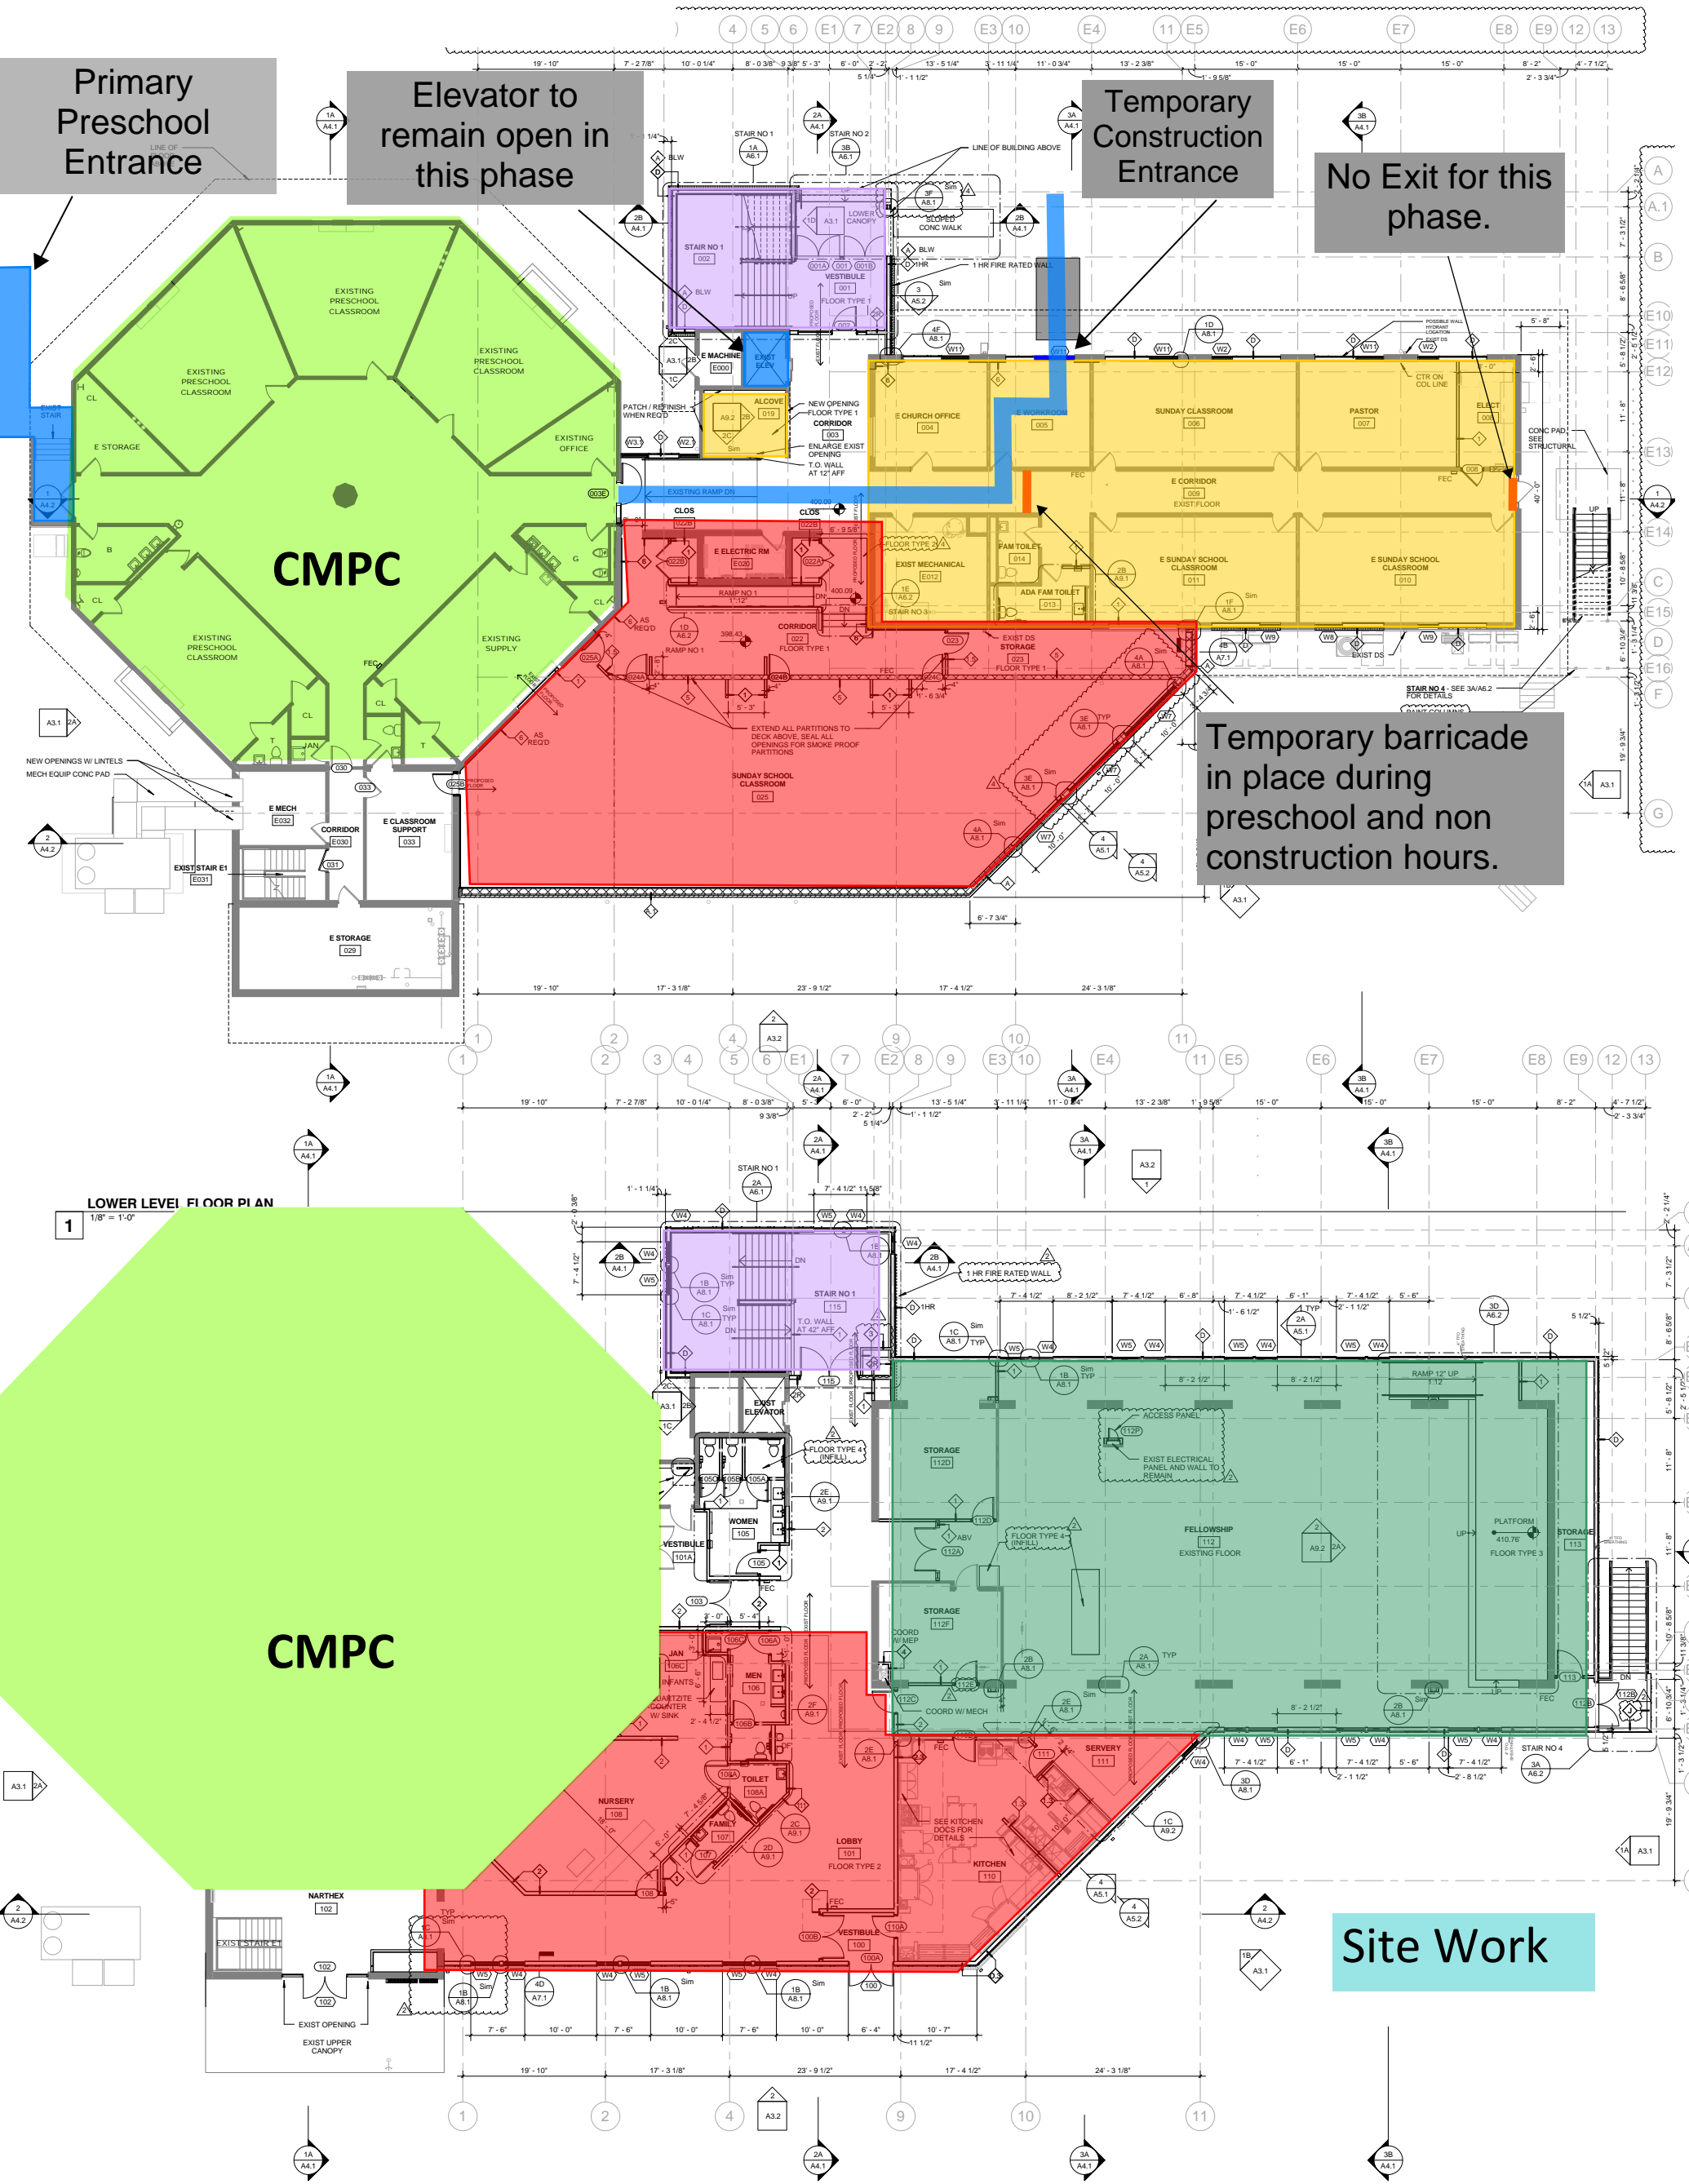

LOWER LEVEL FLOOR PLAN  
1/8" = 1'-0"

CMPC


Site Work



# Christ Memorial - Access Routes

Mid April 2019 - June 2019

## Sanctuary Access / Egress Path

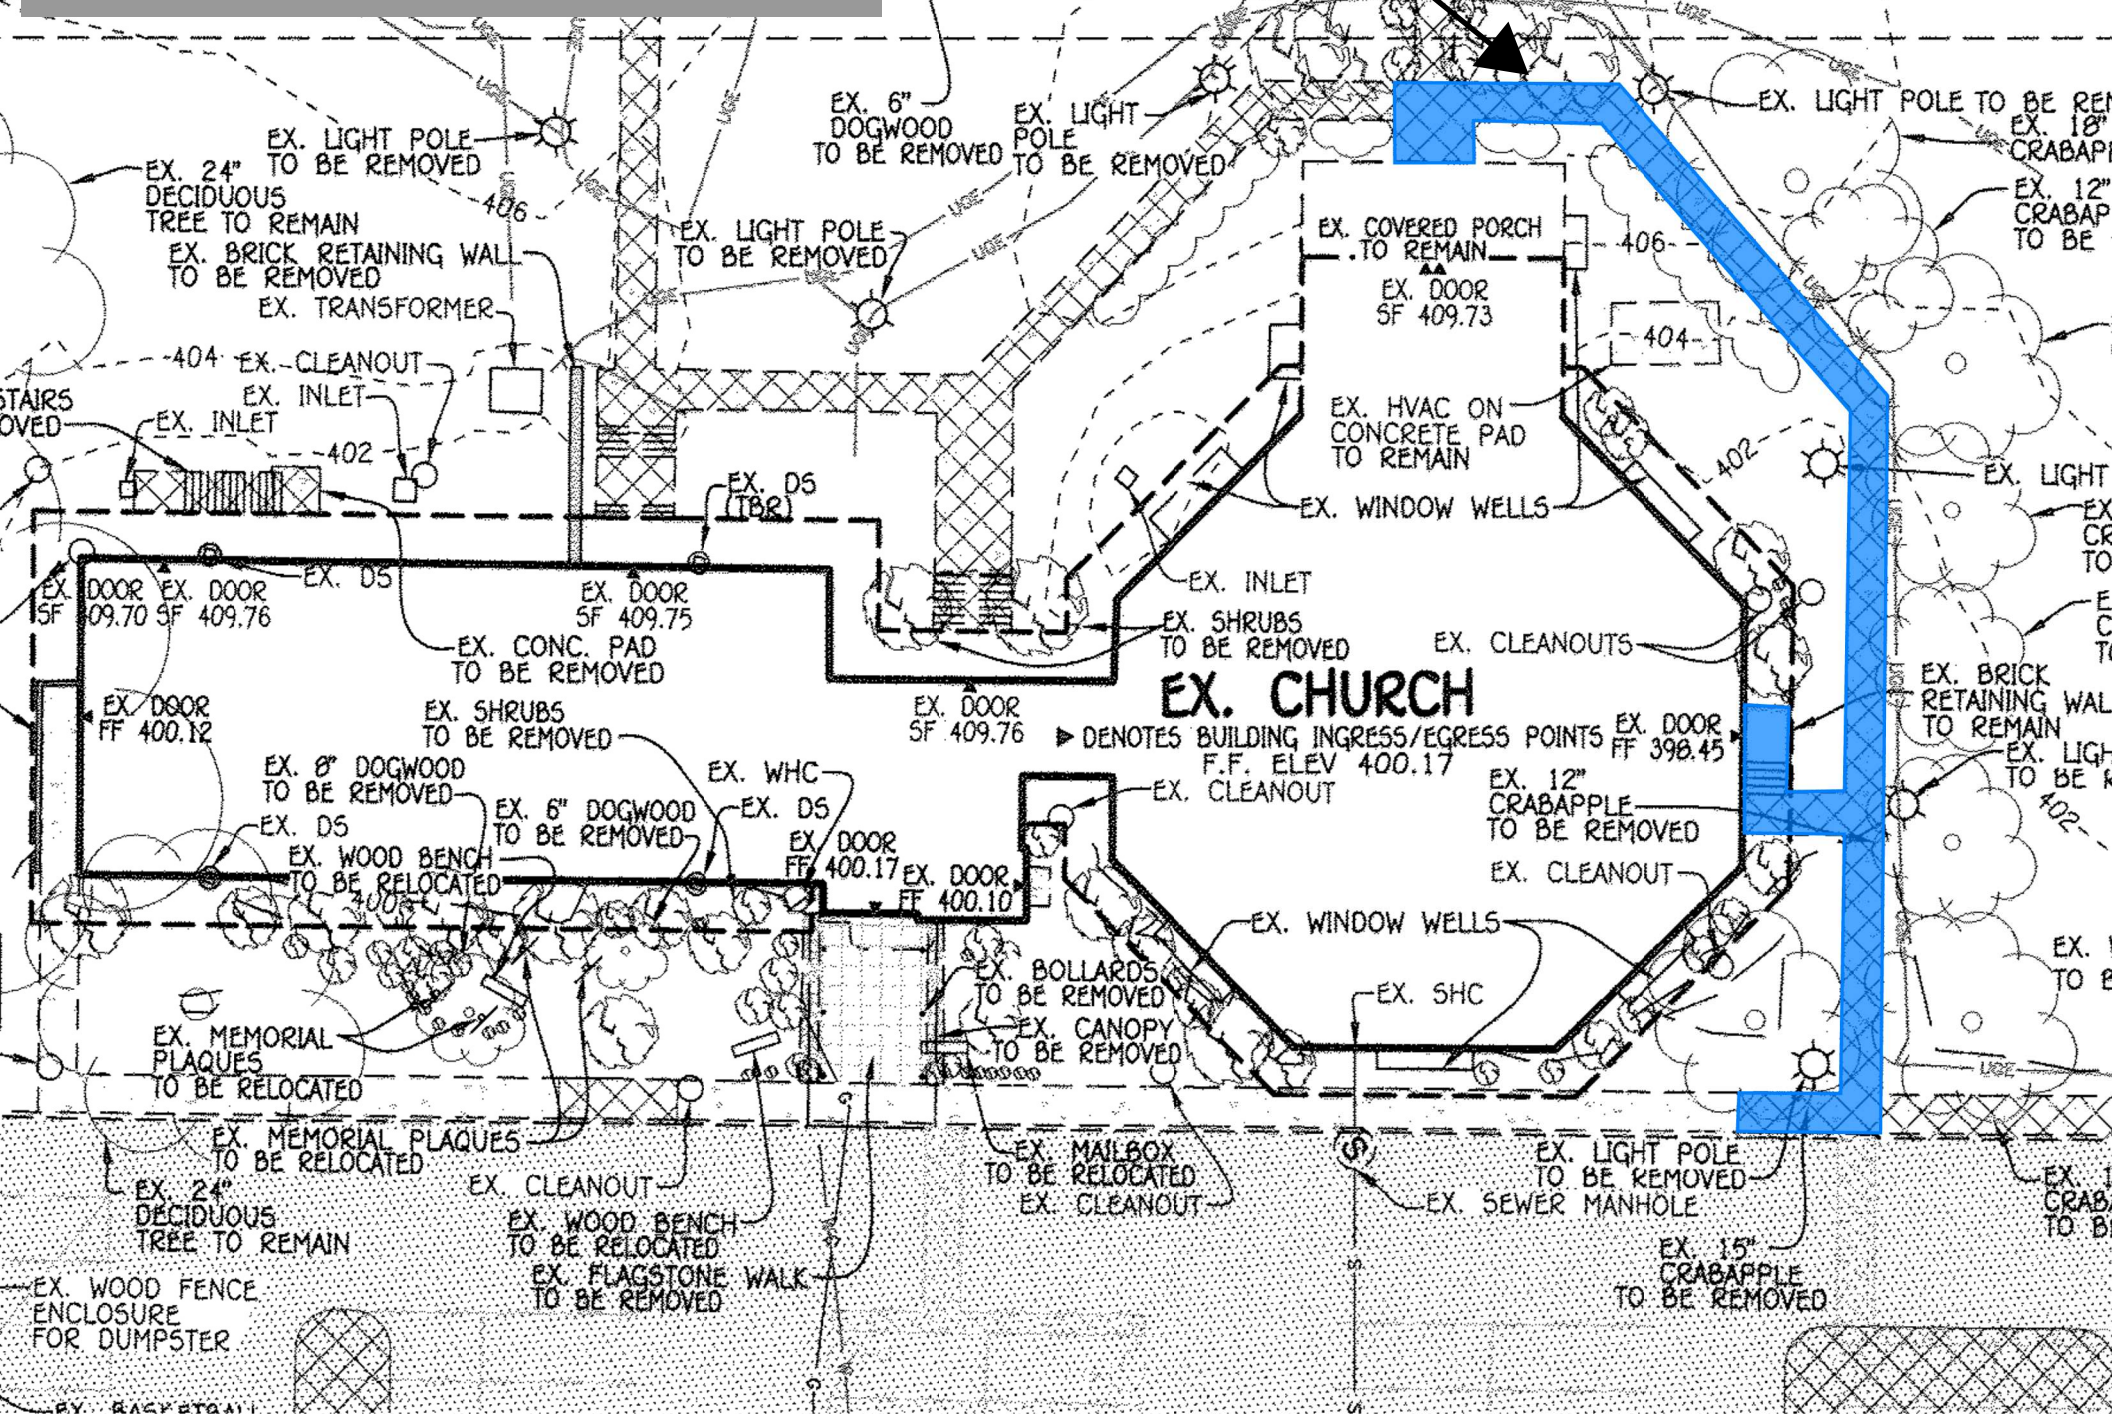




# Christ Memorial - Phasing Plan

## May 2019


- Preschool - No Work
- Sanctuary - Complete
- South Addition - Structure, Slabs, Stair Installation, Facade, Roof
- Lower Level Fellowship - Framing, Fire Sprinklers, Doors Installation, Window Installation, MEP Rough IN, Drywall, Finishes
- Upper Level Fellowship - Framing, Fire Sprinklers, Doors Installation, Window Installation, MEP Rough In, Drywall, Finishes
- North Addition - MEP Rough In, Building Tie In, Drywall, Stair Installation

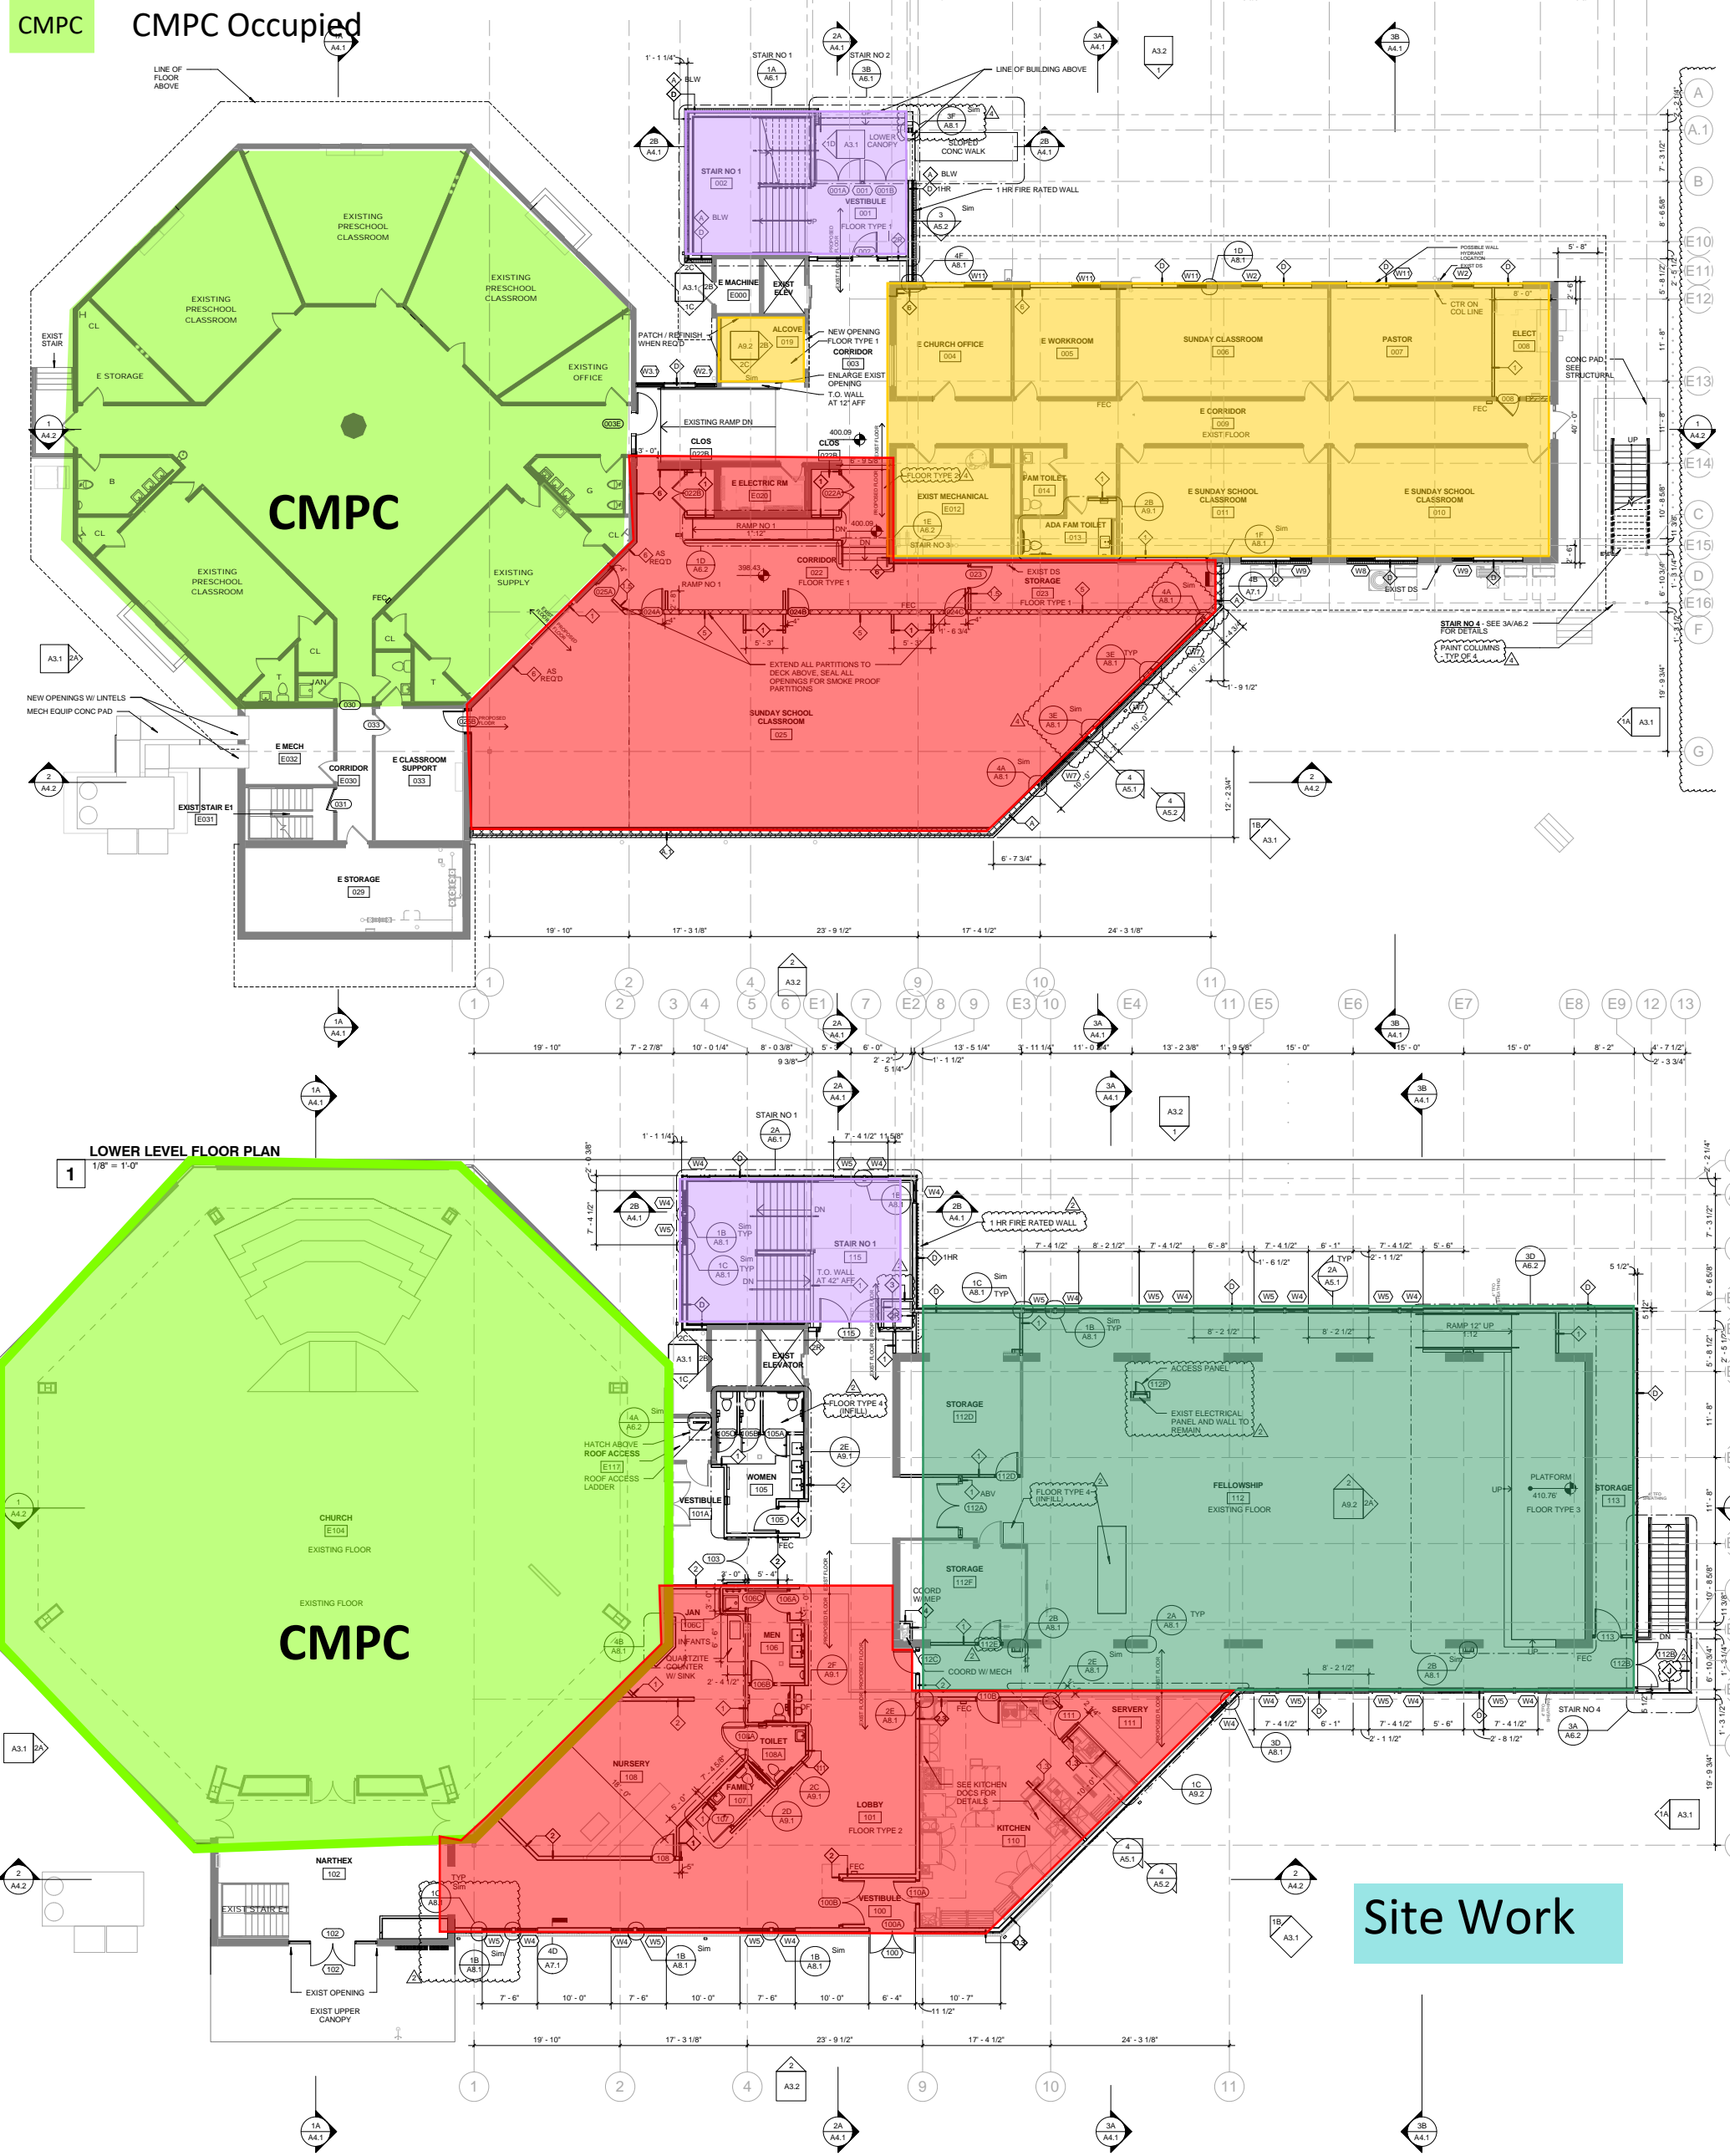

# Christ Memorial - Phasing Plan

## June 2019

- Preschool - Fire Sprinklers
- Lower Level Fellowship - Finishes, MEP Trimout
- Sanctuary - Complete
- Upper Level Fellowship - Finishes, MEP Trimout
- South Addition - Roofing, Framing, Doors, Windows, MEP Rough In
- North Addition - Finishes, MEP Trimout
- CMPC Occupied

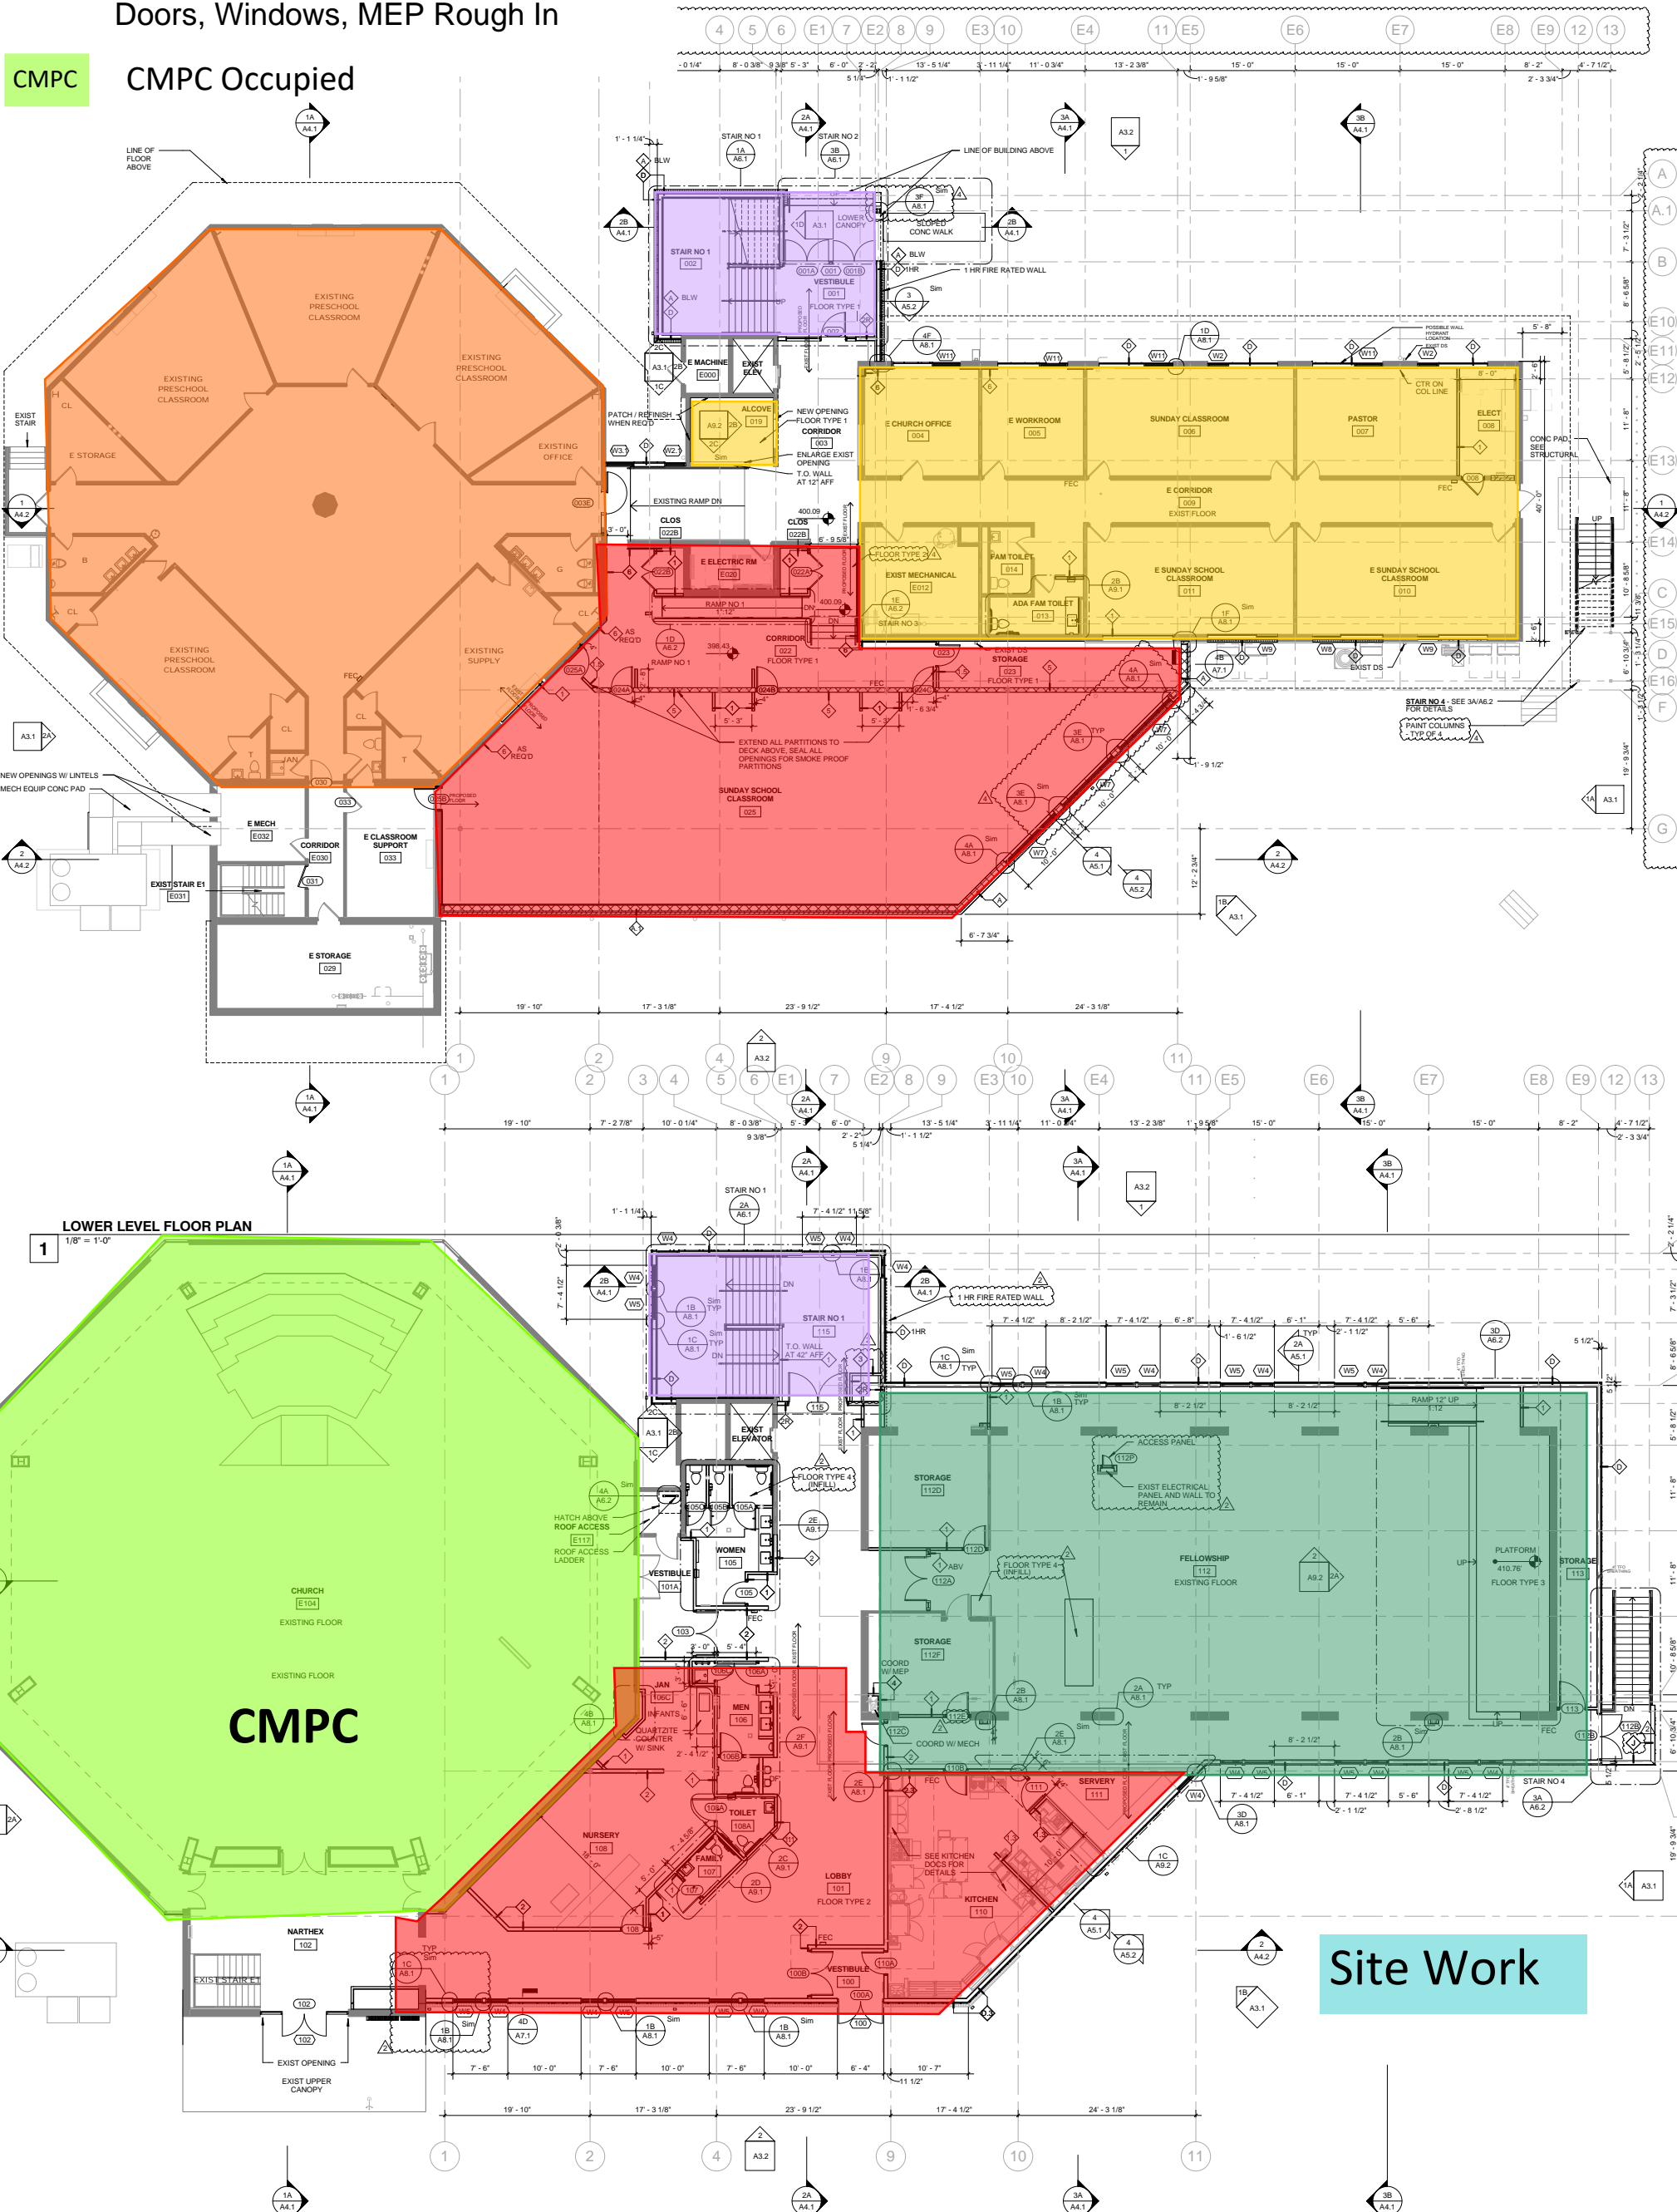

**LOWER LEVEL FLOOR PLAN**  
1/8" = 1'-0"



**Site Work**



# Christ Memorial - Phasing Plan

## July 2019



- Preschool - Complete
- Lower Level Fellowship - Complete
- Sanctuary - Complete
- Upper Level Fellowship - Complete
- South Addition - Building Tie, Drywall
- North Addition - Complete
- CMPC CMPC Occupied

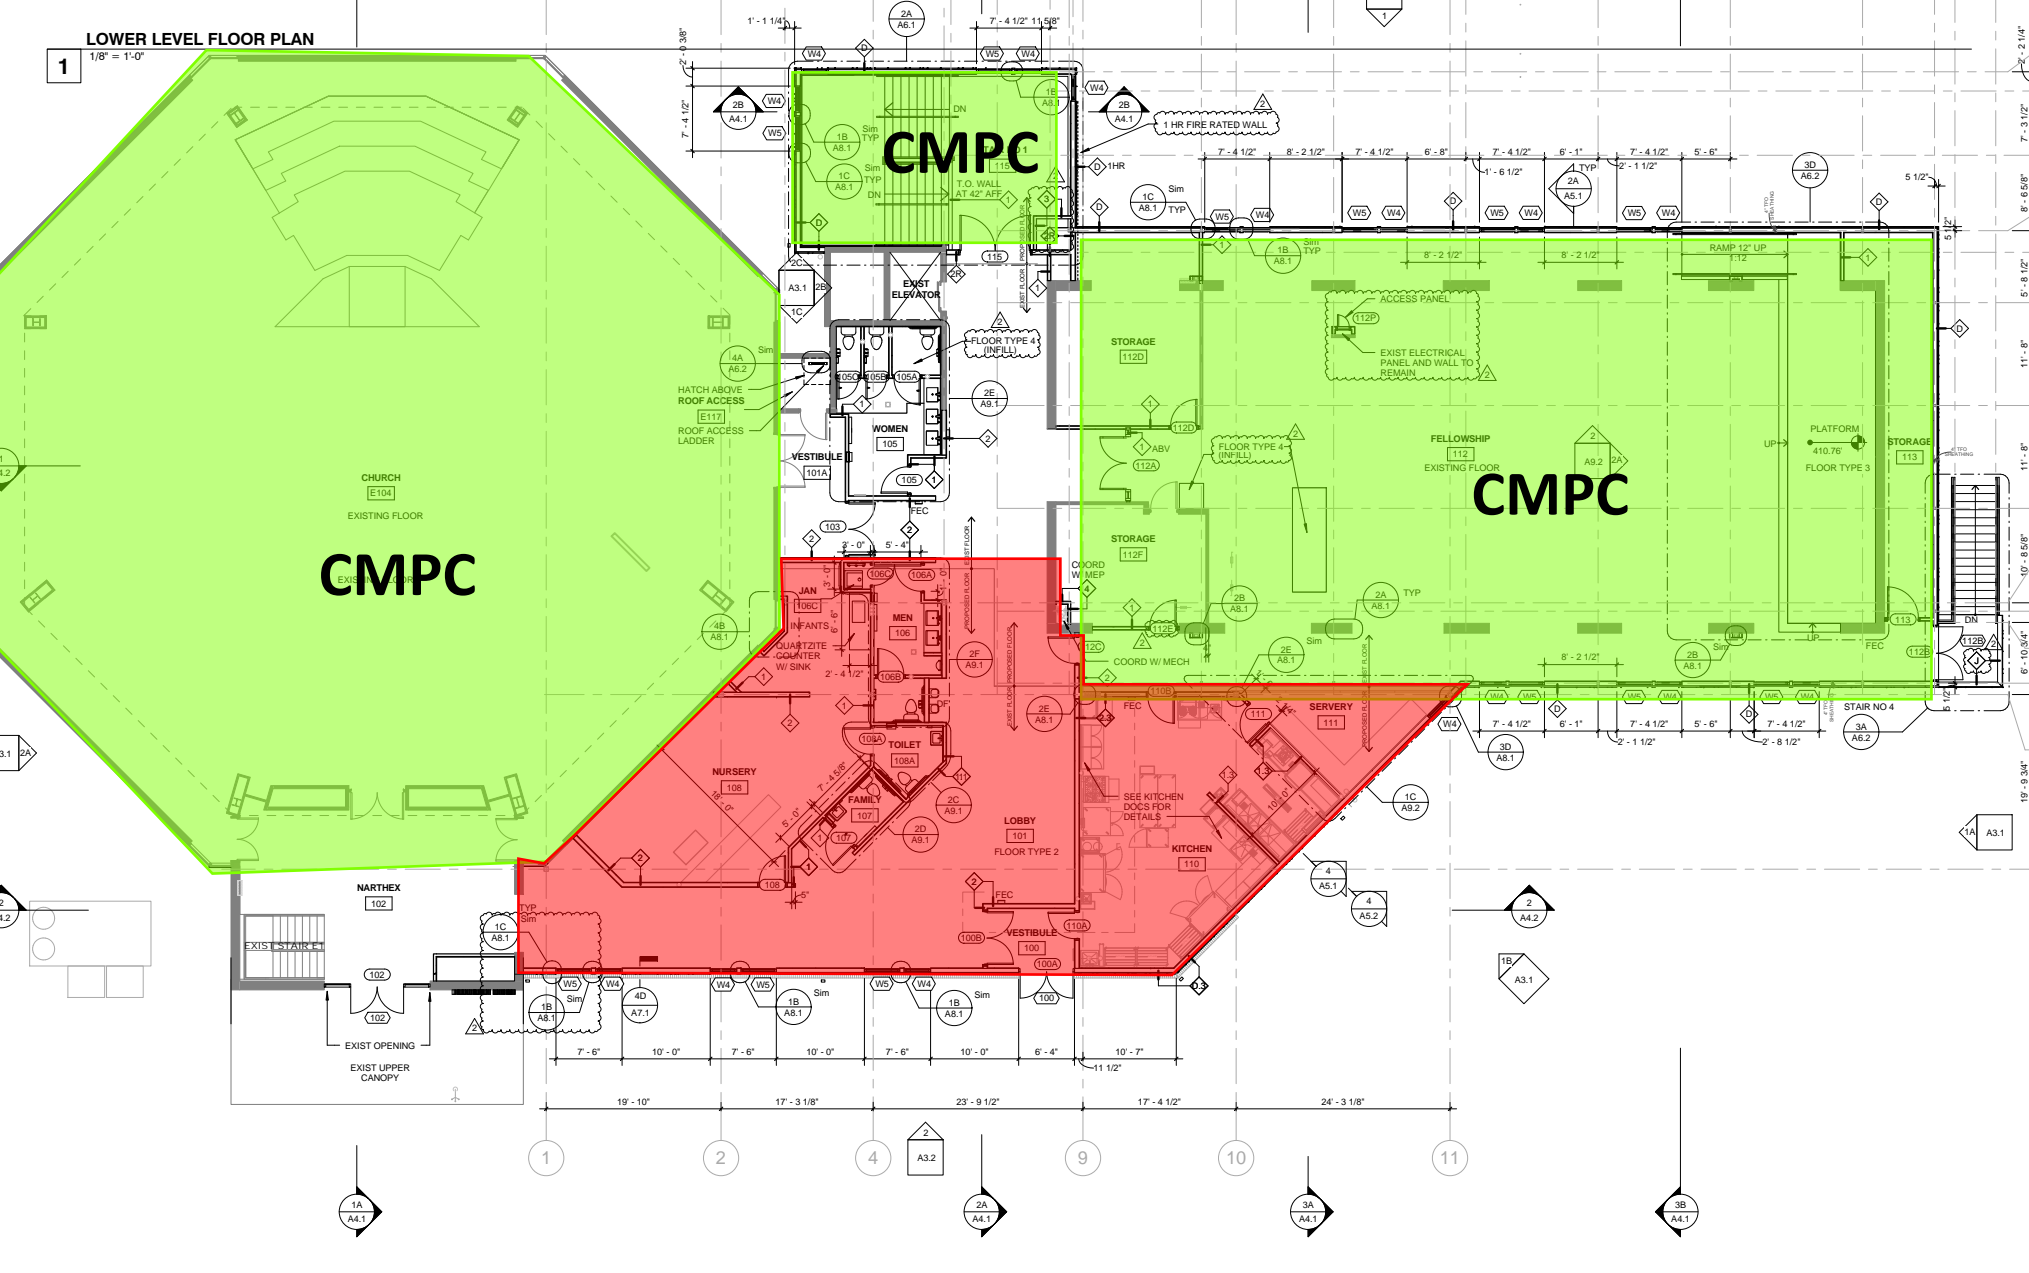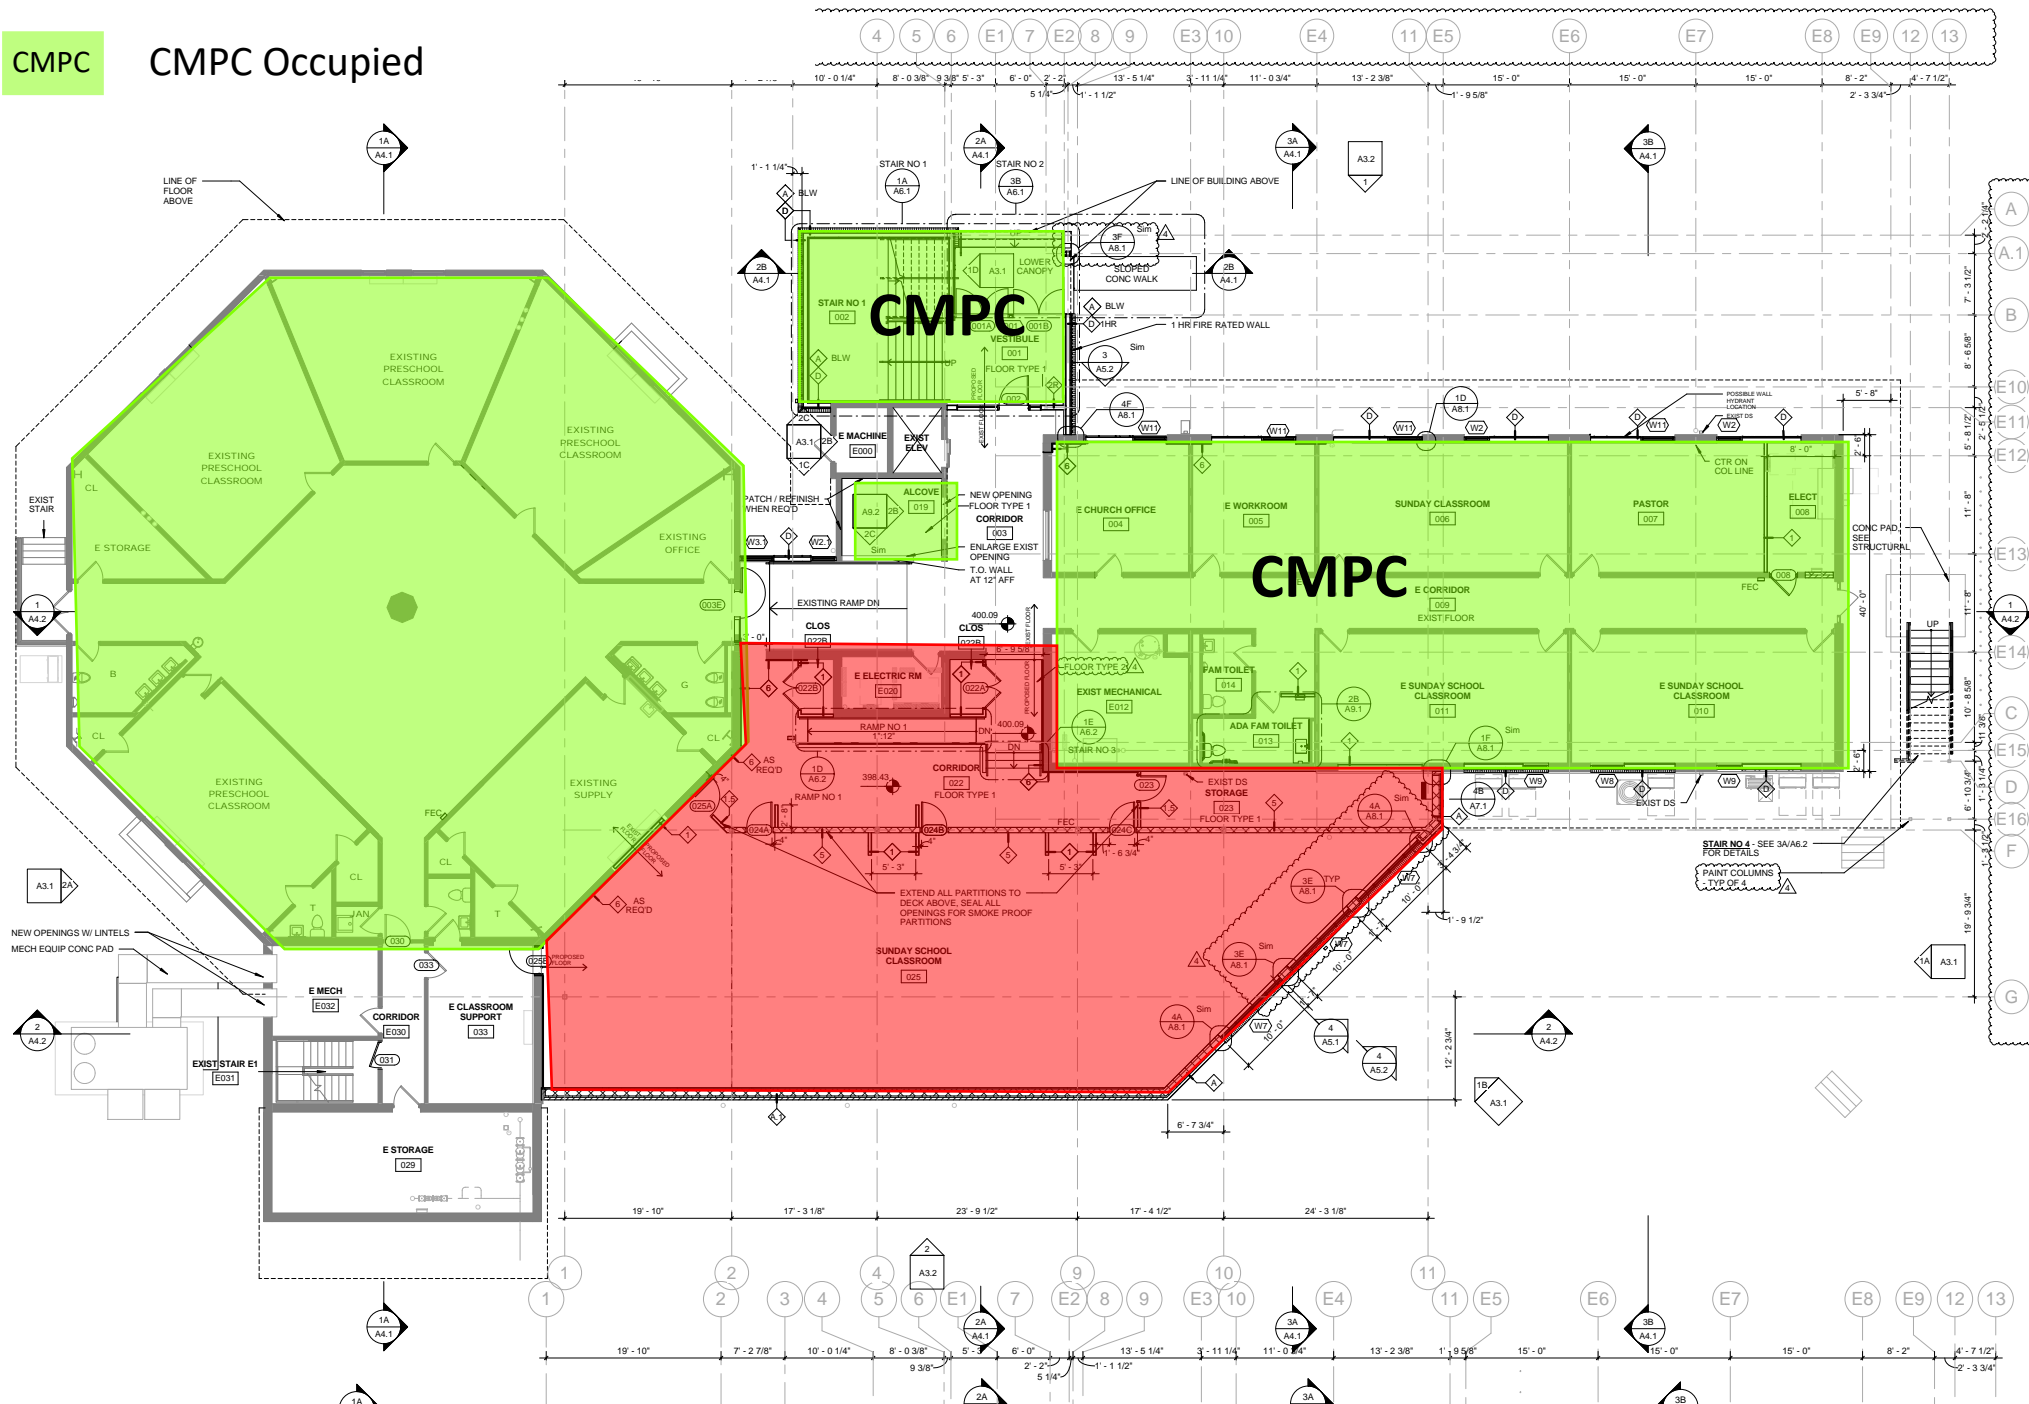

# Christ Memorial - Access Routes

## July 2019 - Project Completion



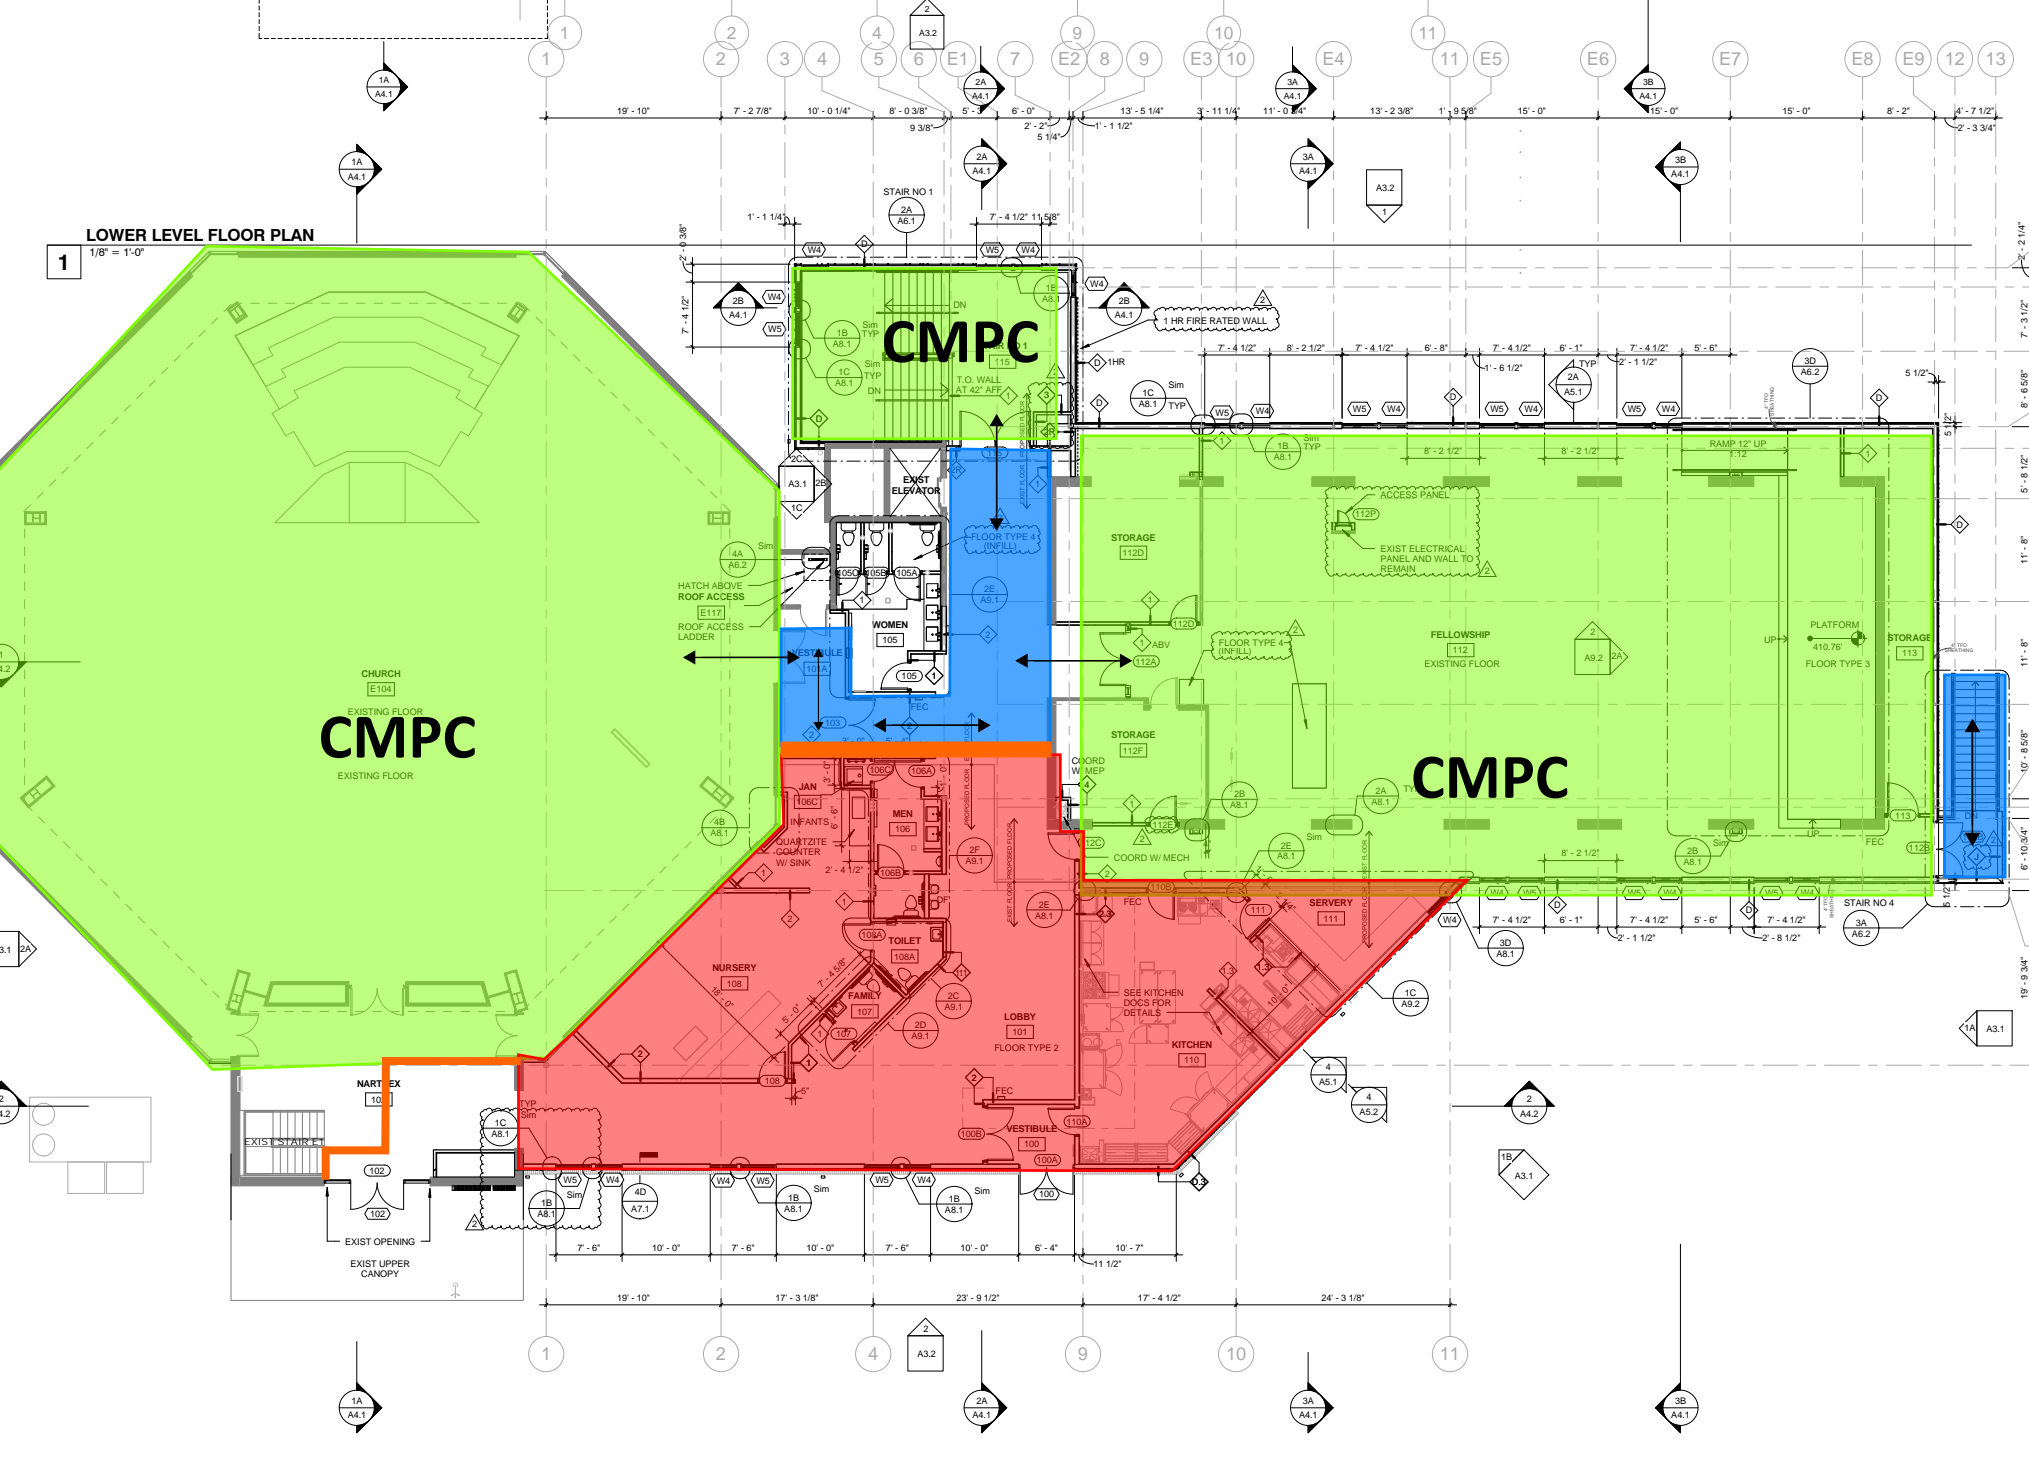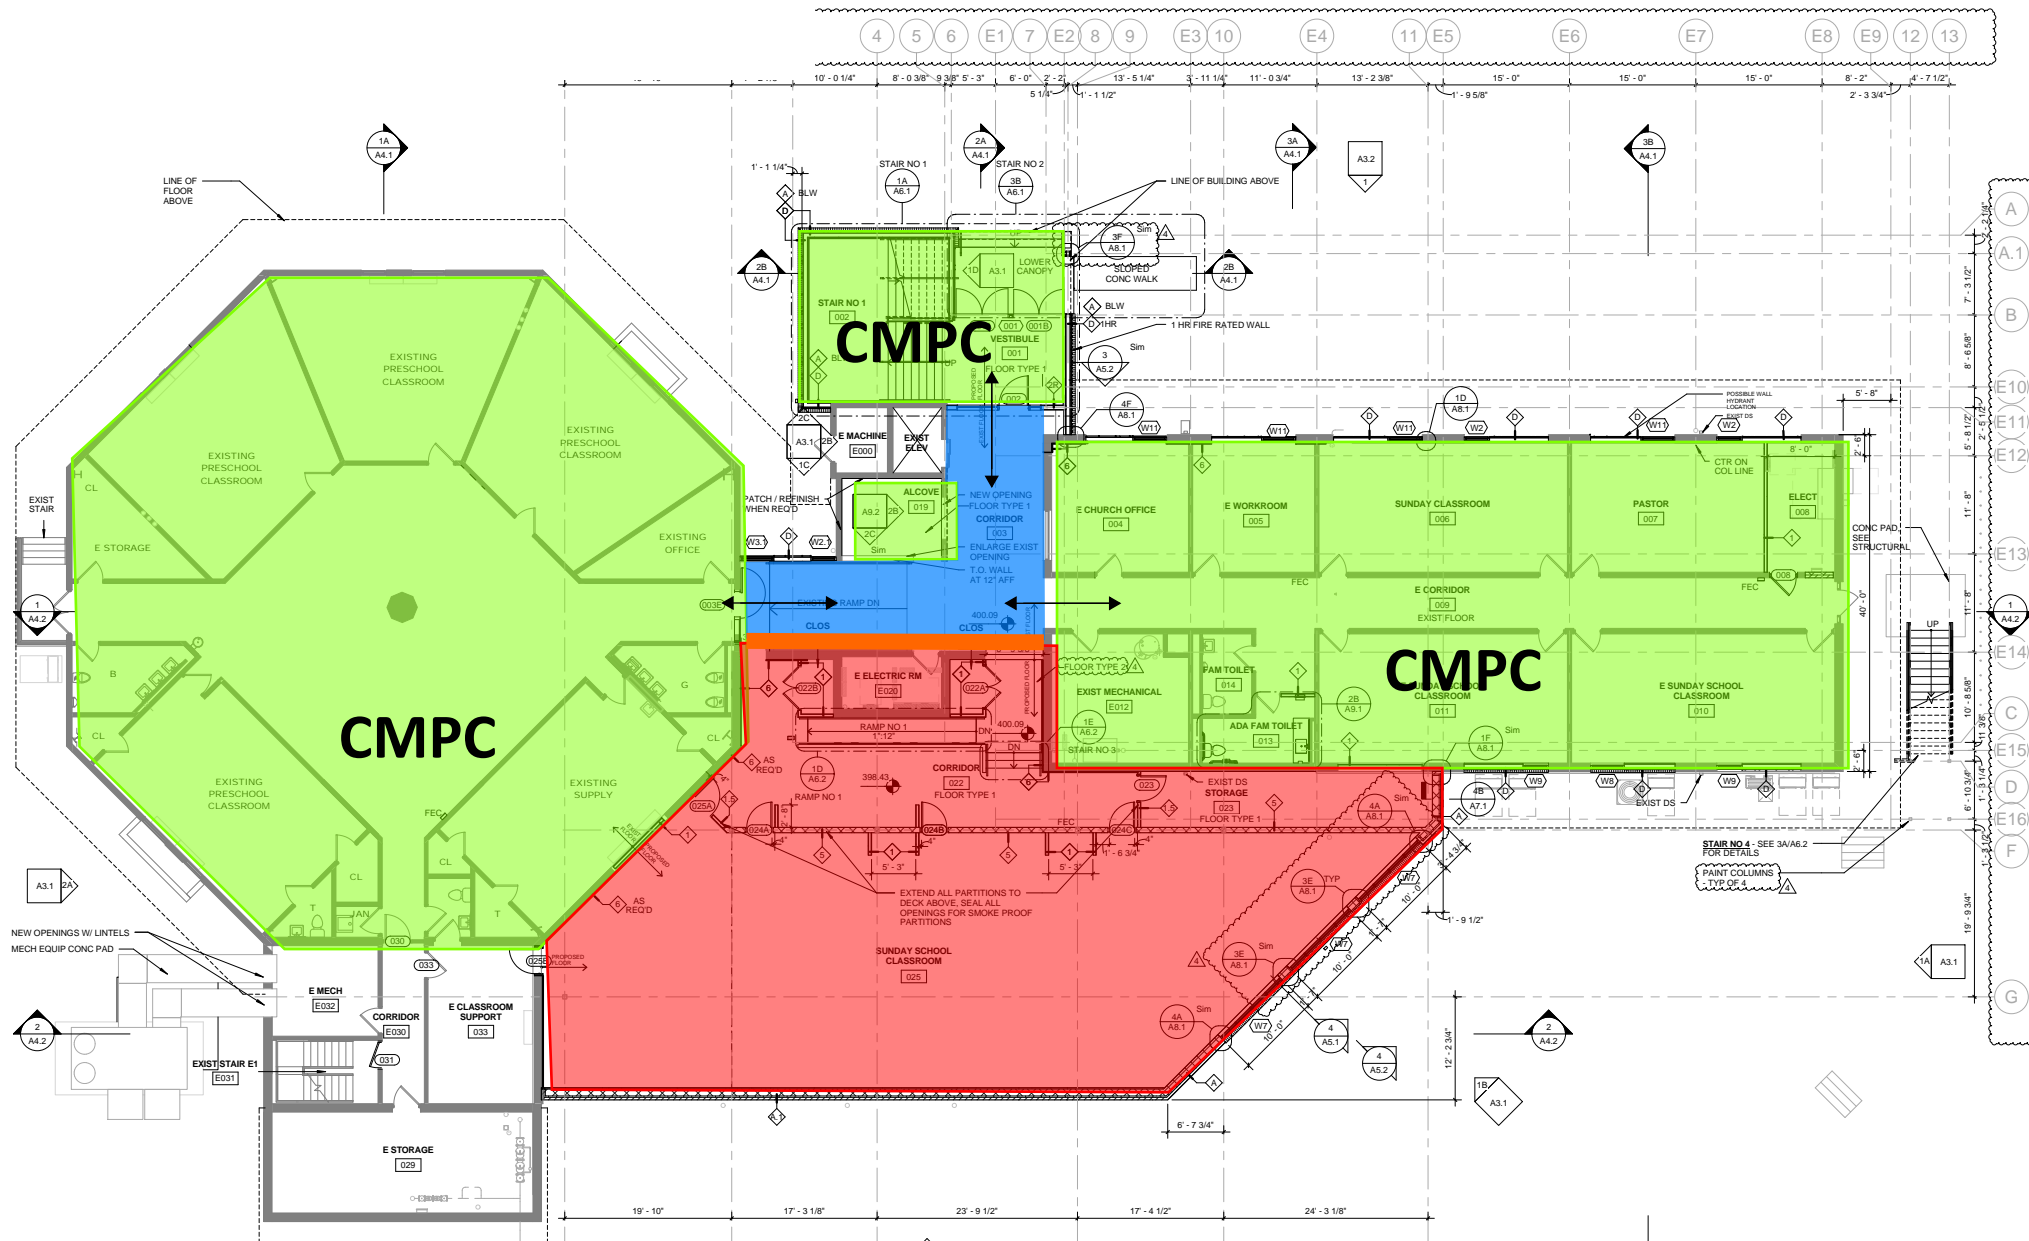




- Preschool
- Access Routes
- Lower Level Fellowship
- CMPC
- CMPC Occupied
- Sanctuary
- Upper Level Fellowship
- North Addition
- South Addition







# Christ Memorial - Phasing Plan

## August 2019



	Preschool - Complete		Lower Level Fellowship - Complete
	Sanctuary - Complete		Upper Level Fellowship - Complete
	South Addition - Finishes, Kitchen Fit Out		North Addition - Complete
	CMPC Occupied		

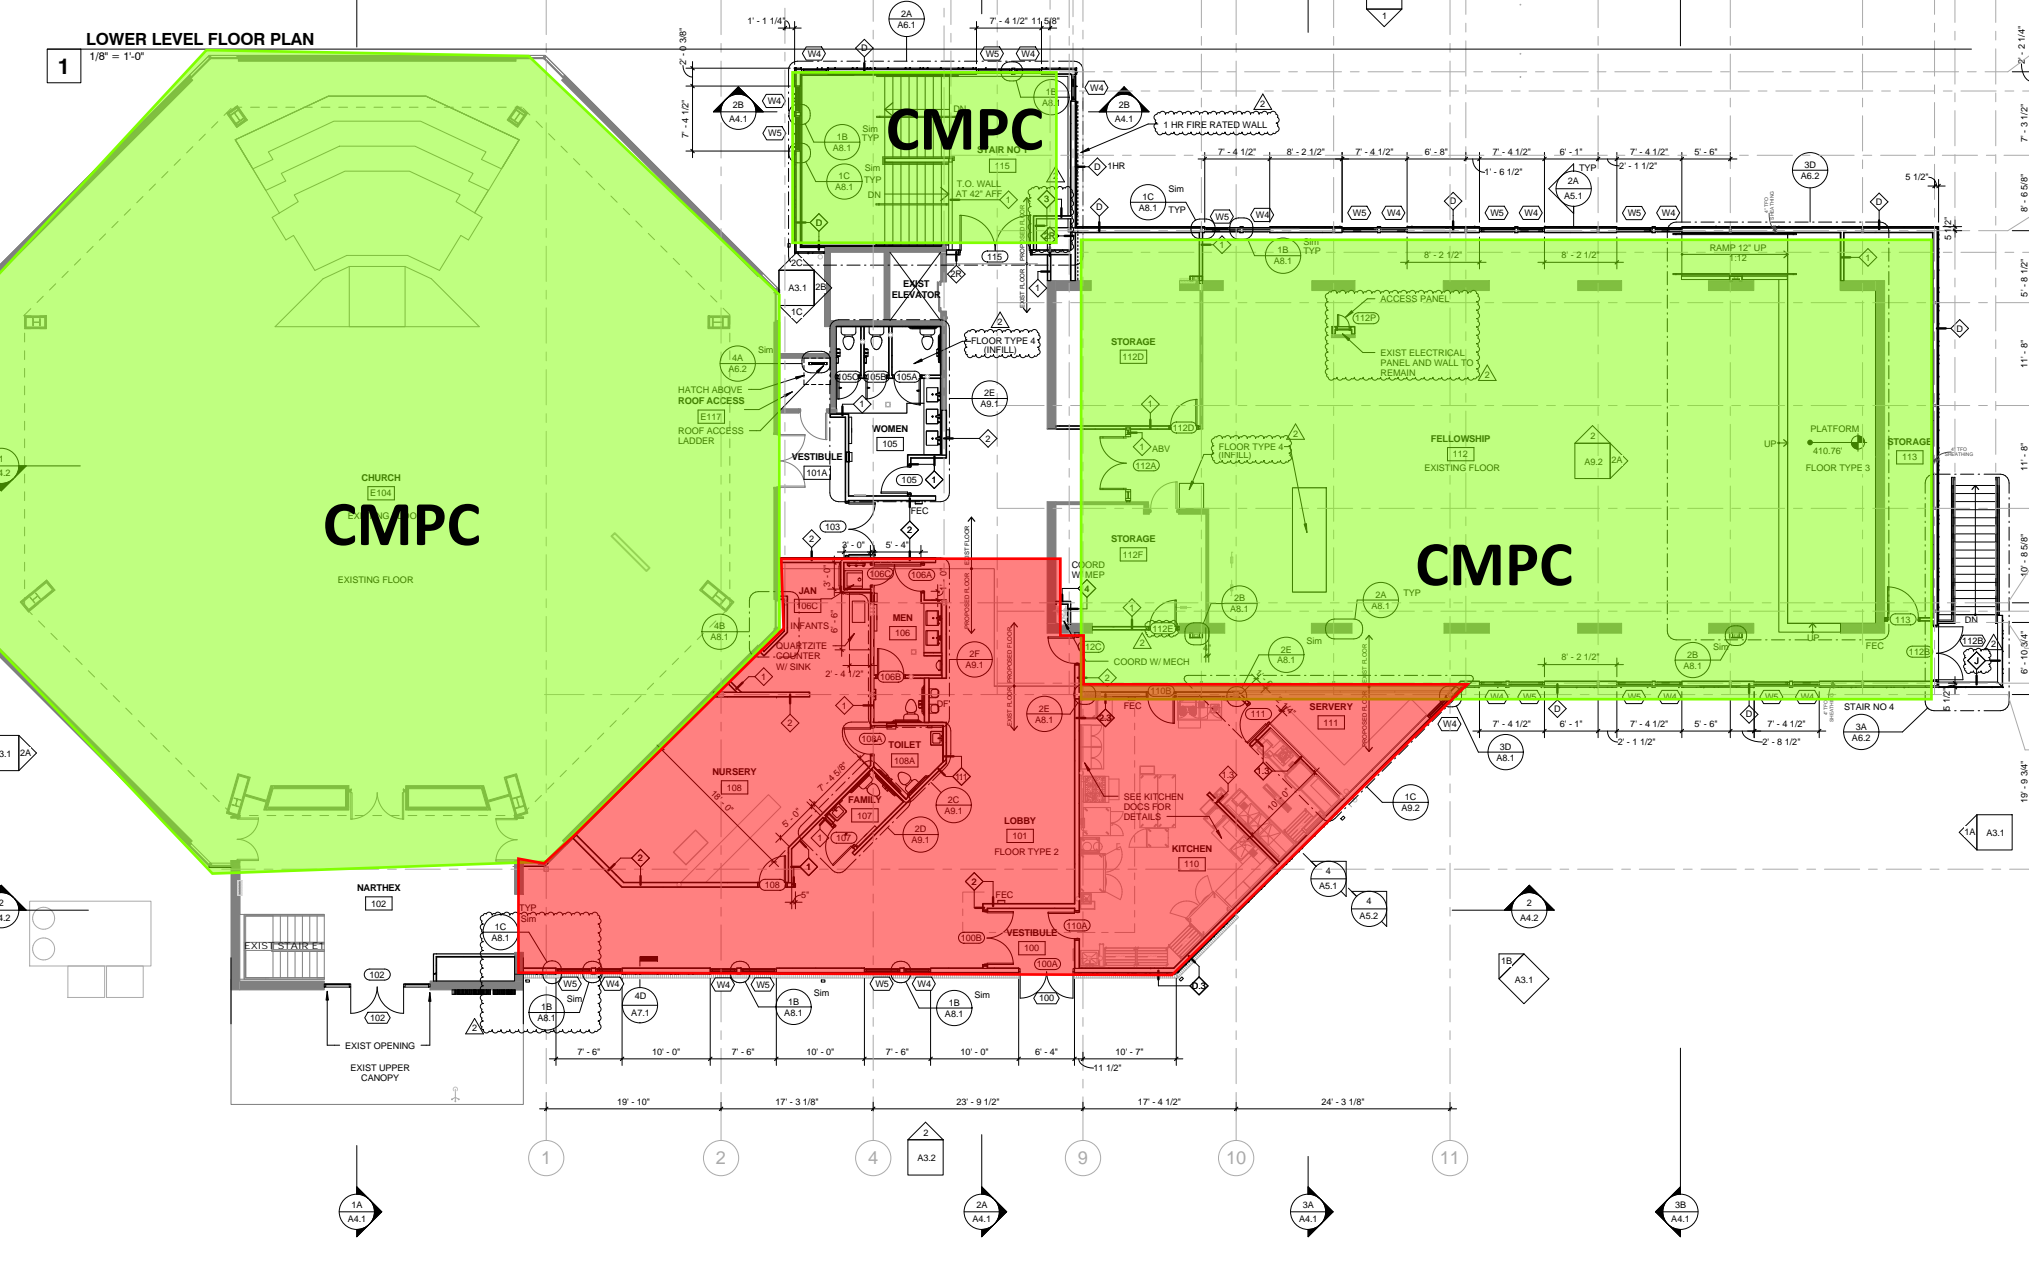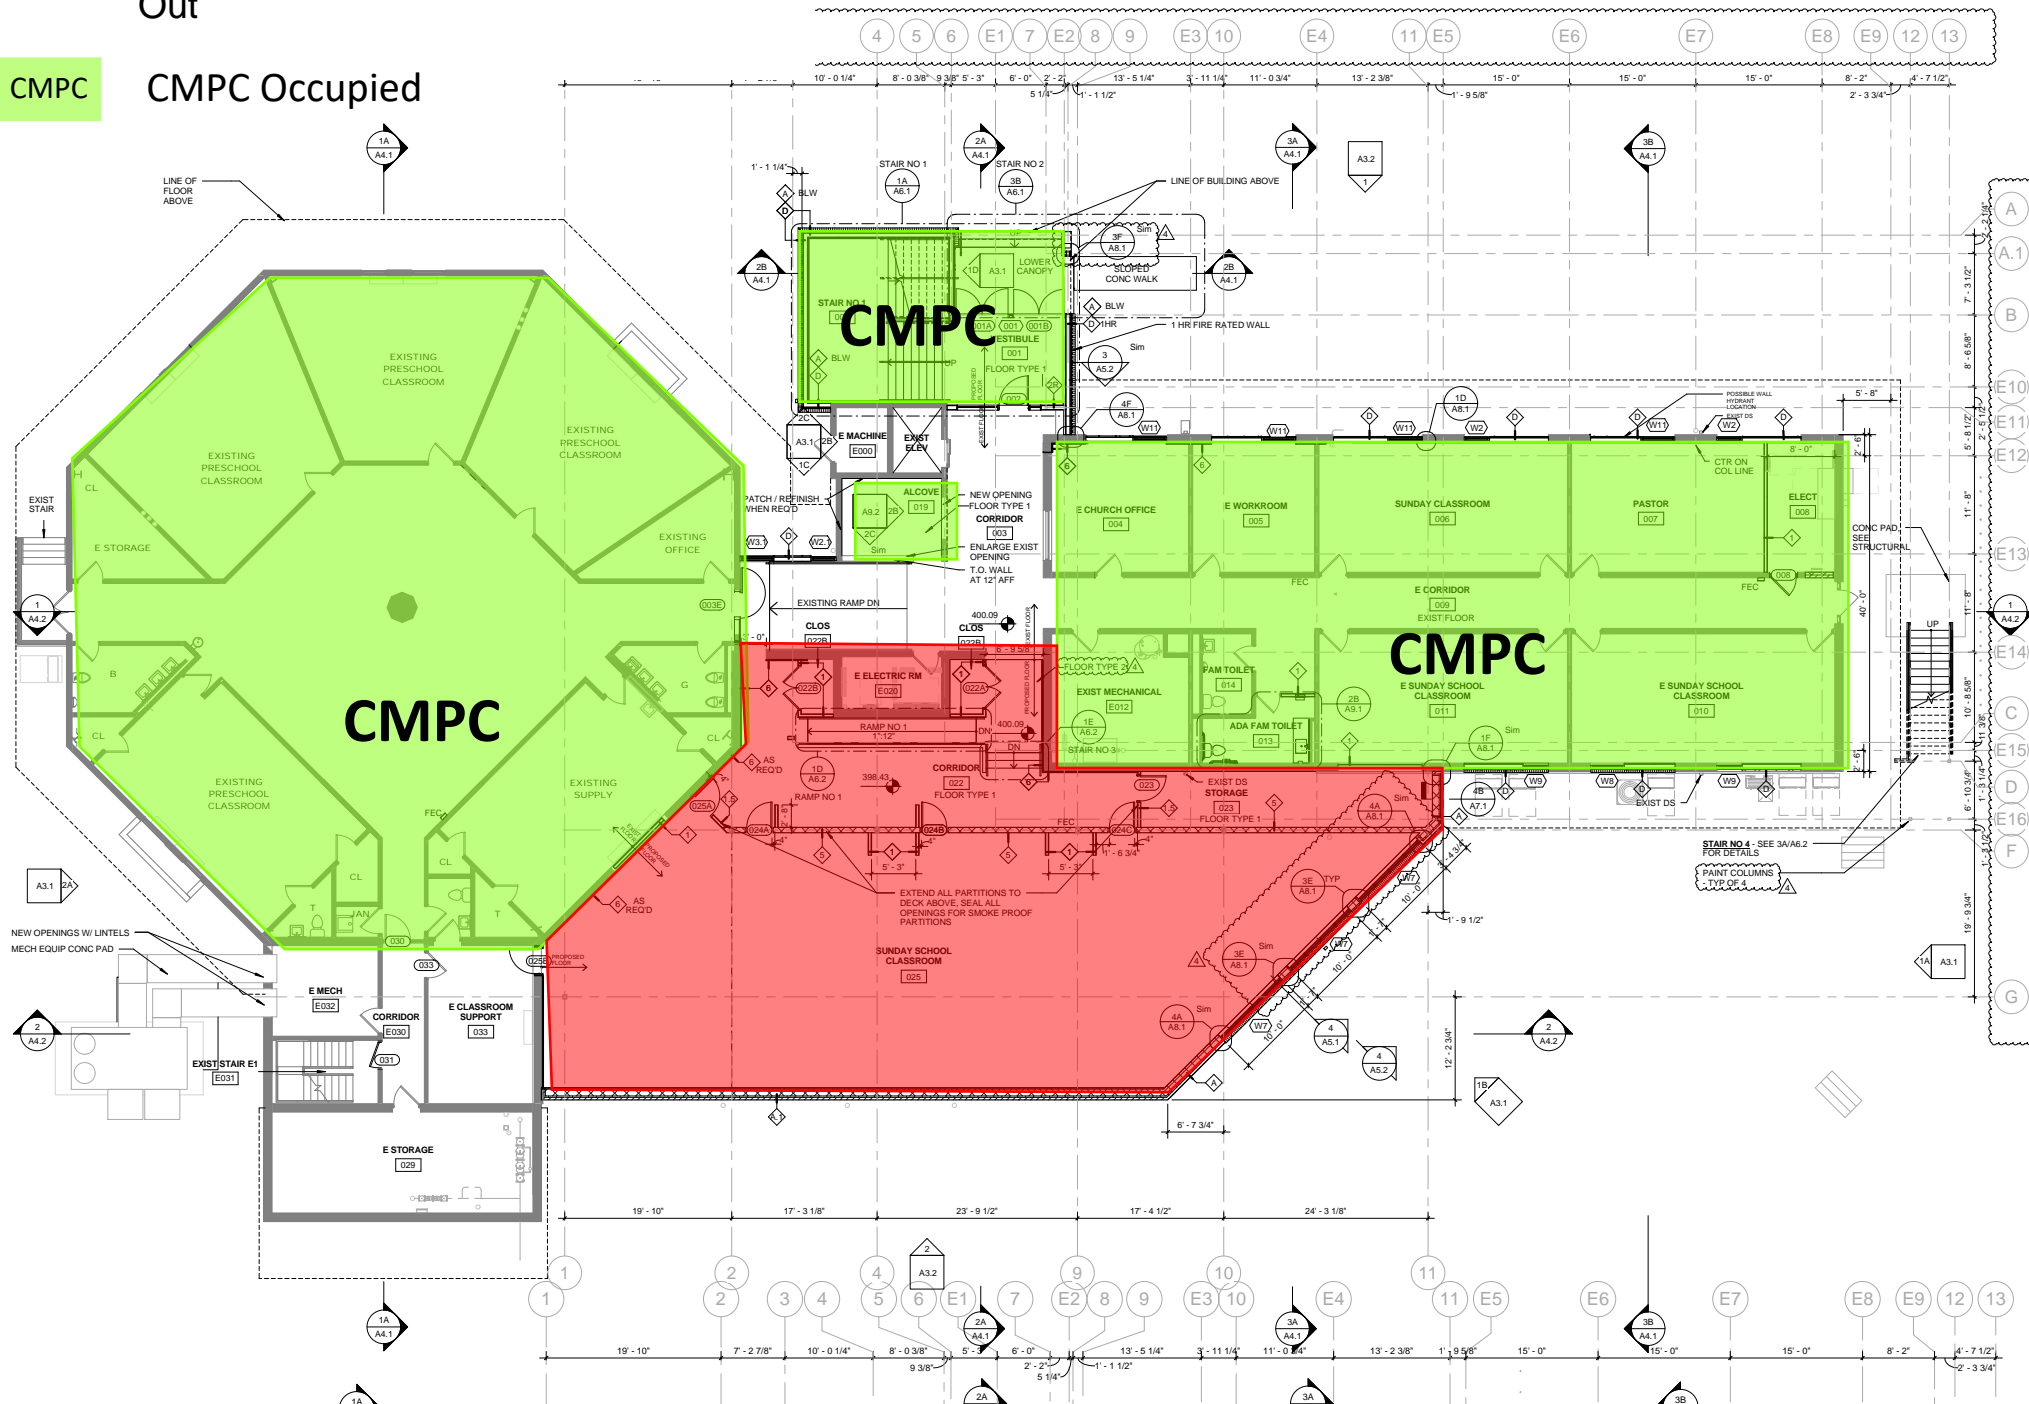

# Christ Memorial - Phasing Plan

## September 2019

- Preschool - Complete
- Lower Level Fellowship - Complete
- Sanctuary - Complete
- Upper Level Fellowship - Complete
- South Addition - Kitchen Fit Out, MEP Trim out
- North Addition - Complete
- CMPC Occupied

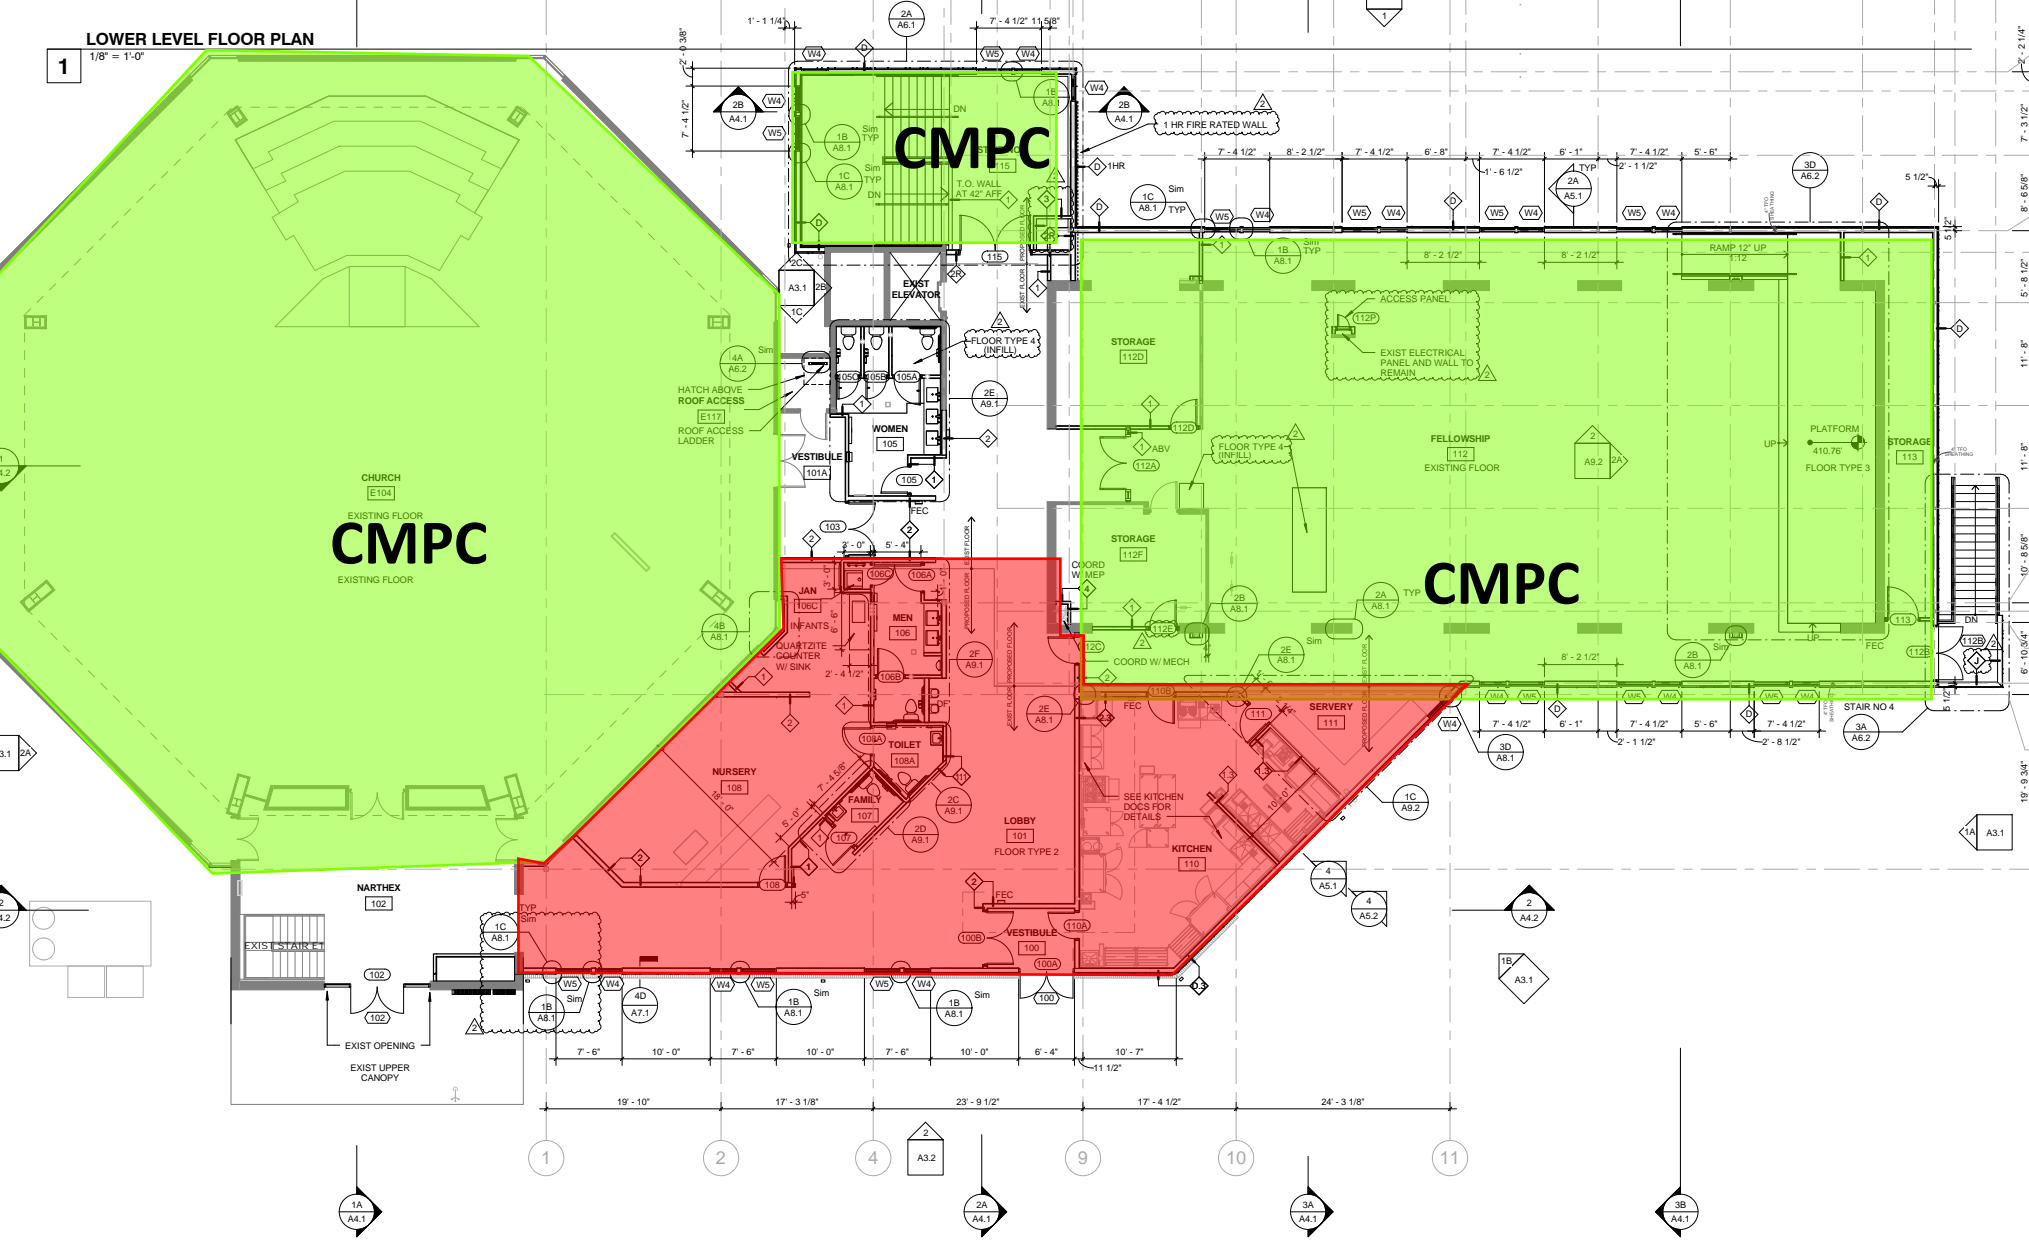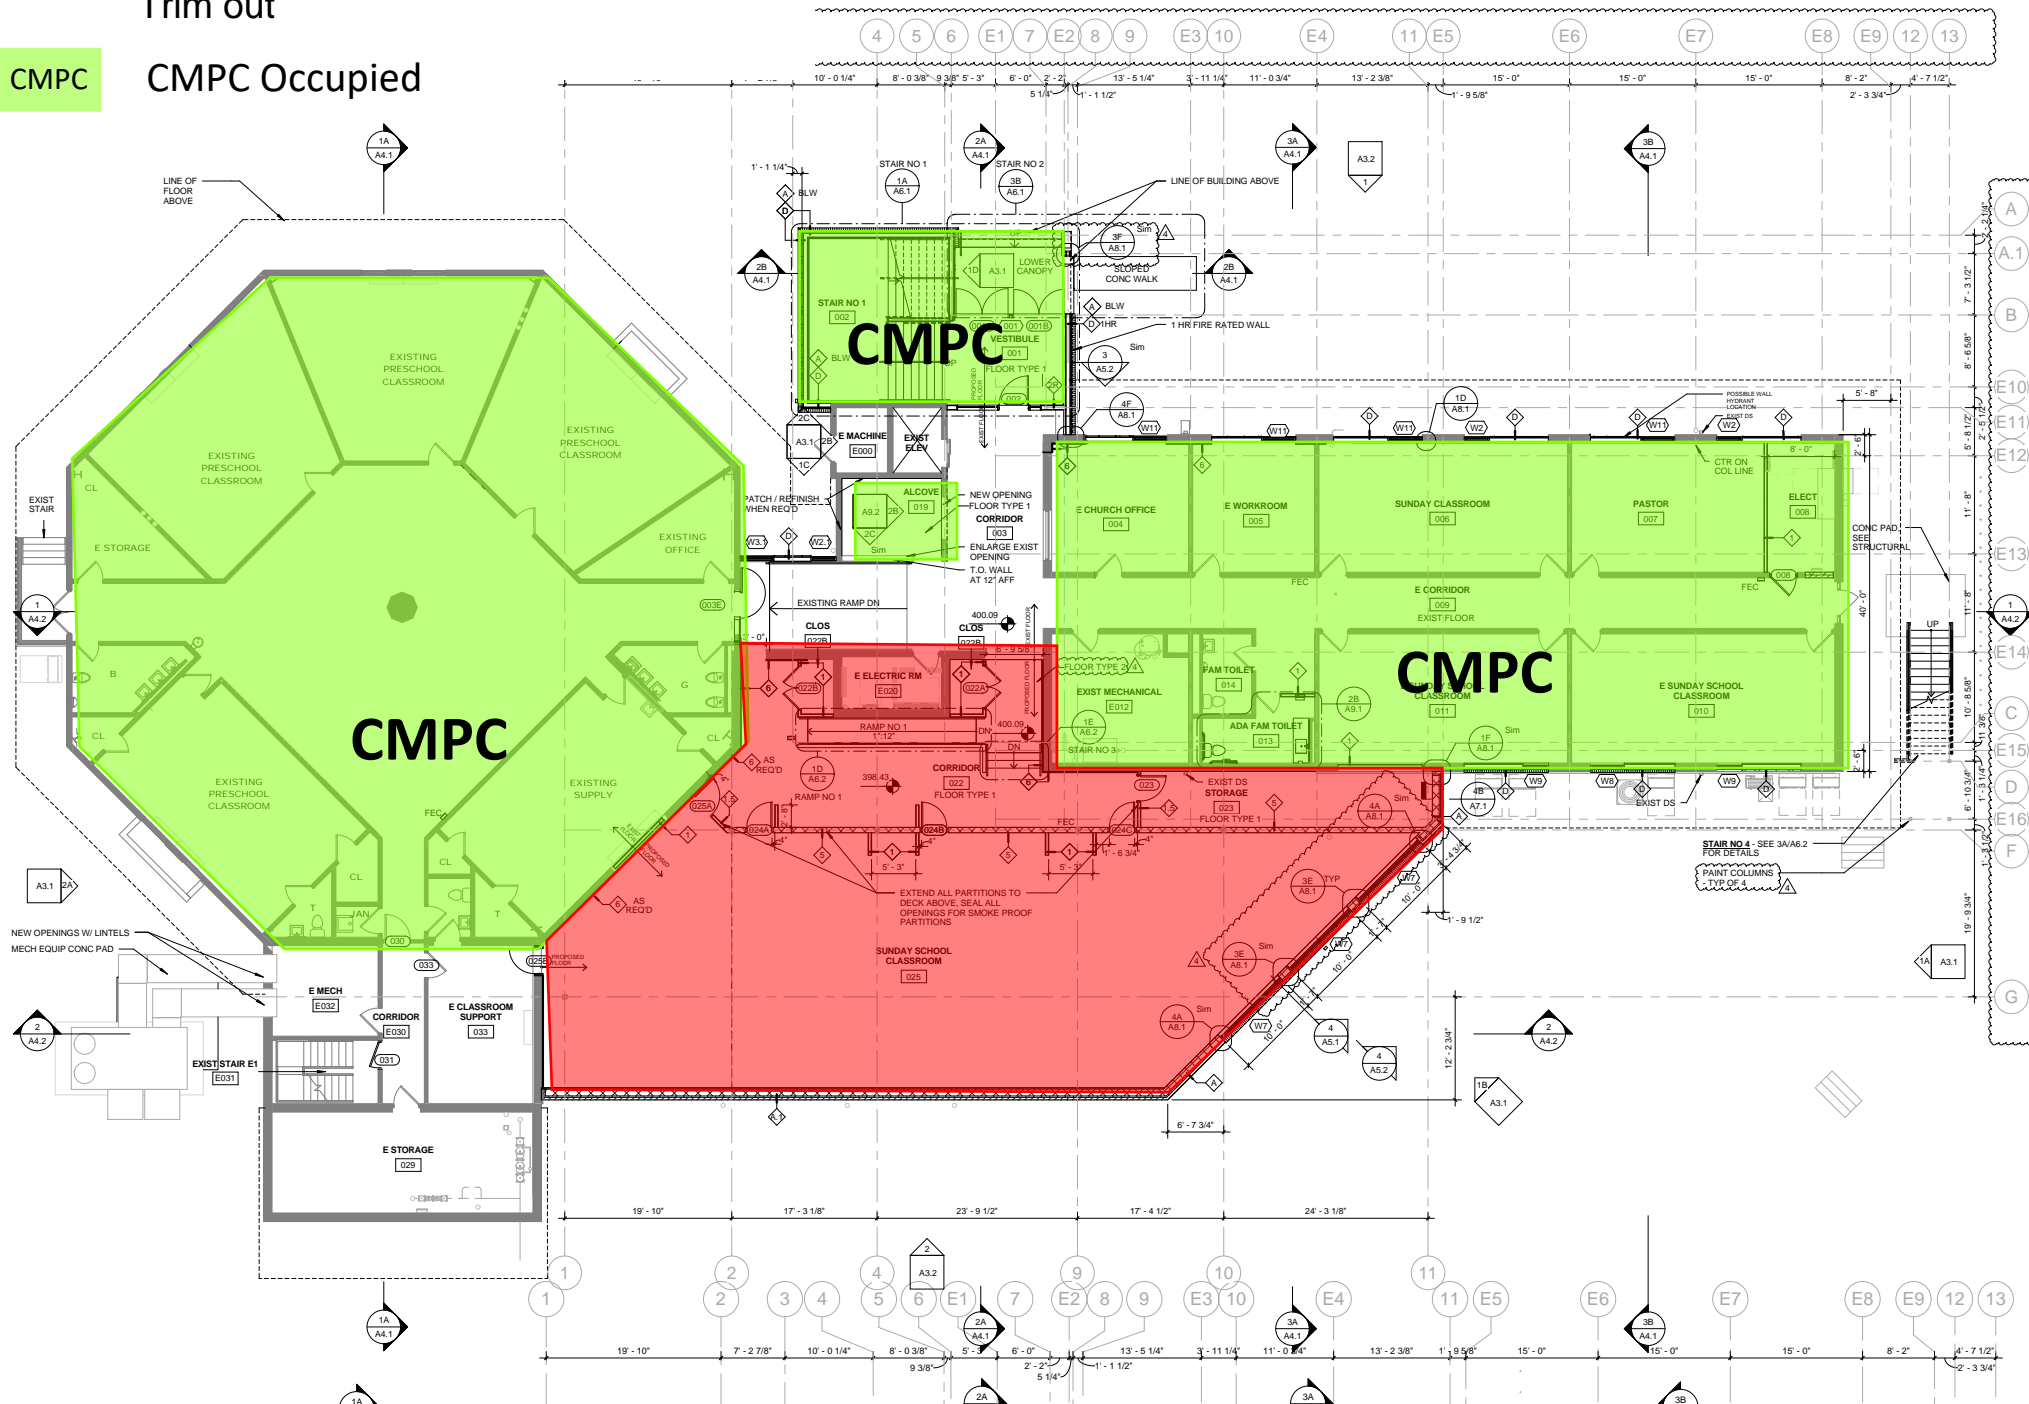



# Christ Memorial - Phasing Plan

## October 2019

- Preschool - Complete
- Lower Level Fellowship - Complete
- Sanctuary - Complete
- Upper Level Fellowship - Complete
- South Addition - MEP Trimout
- North Addition - Complete
- CMPC Occupied

